

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100




Slack: 0.19"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 72" - MH FLAT TOP w/24"x36" Hole - 10"
- P1) 72" - MH BASE Custom Ht - 49"
- 1) CASTING - HOE 525 LV SET (F/G/H)
- 1) 72" - Conseal CS-102 1.00"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) DOGHOUSE INVRTD - 50"x49"
- 1) Hole - 24
- 1) Hole - 44
- 1) Hole - 38
- 4) MH Step ML-10-TDS-NCR - 10"



0 lb
4149 lb
7732 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 12323 lb

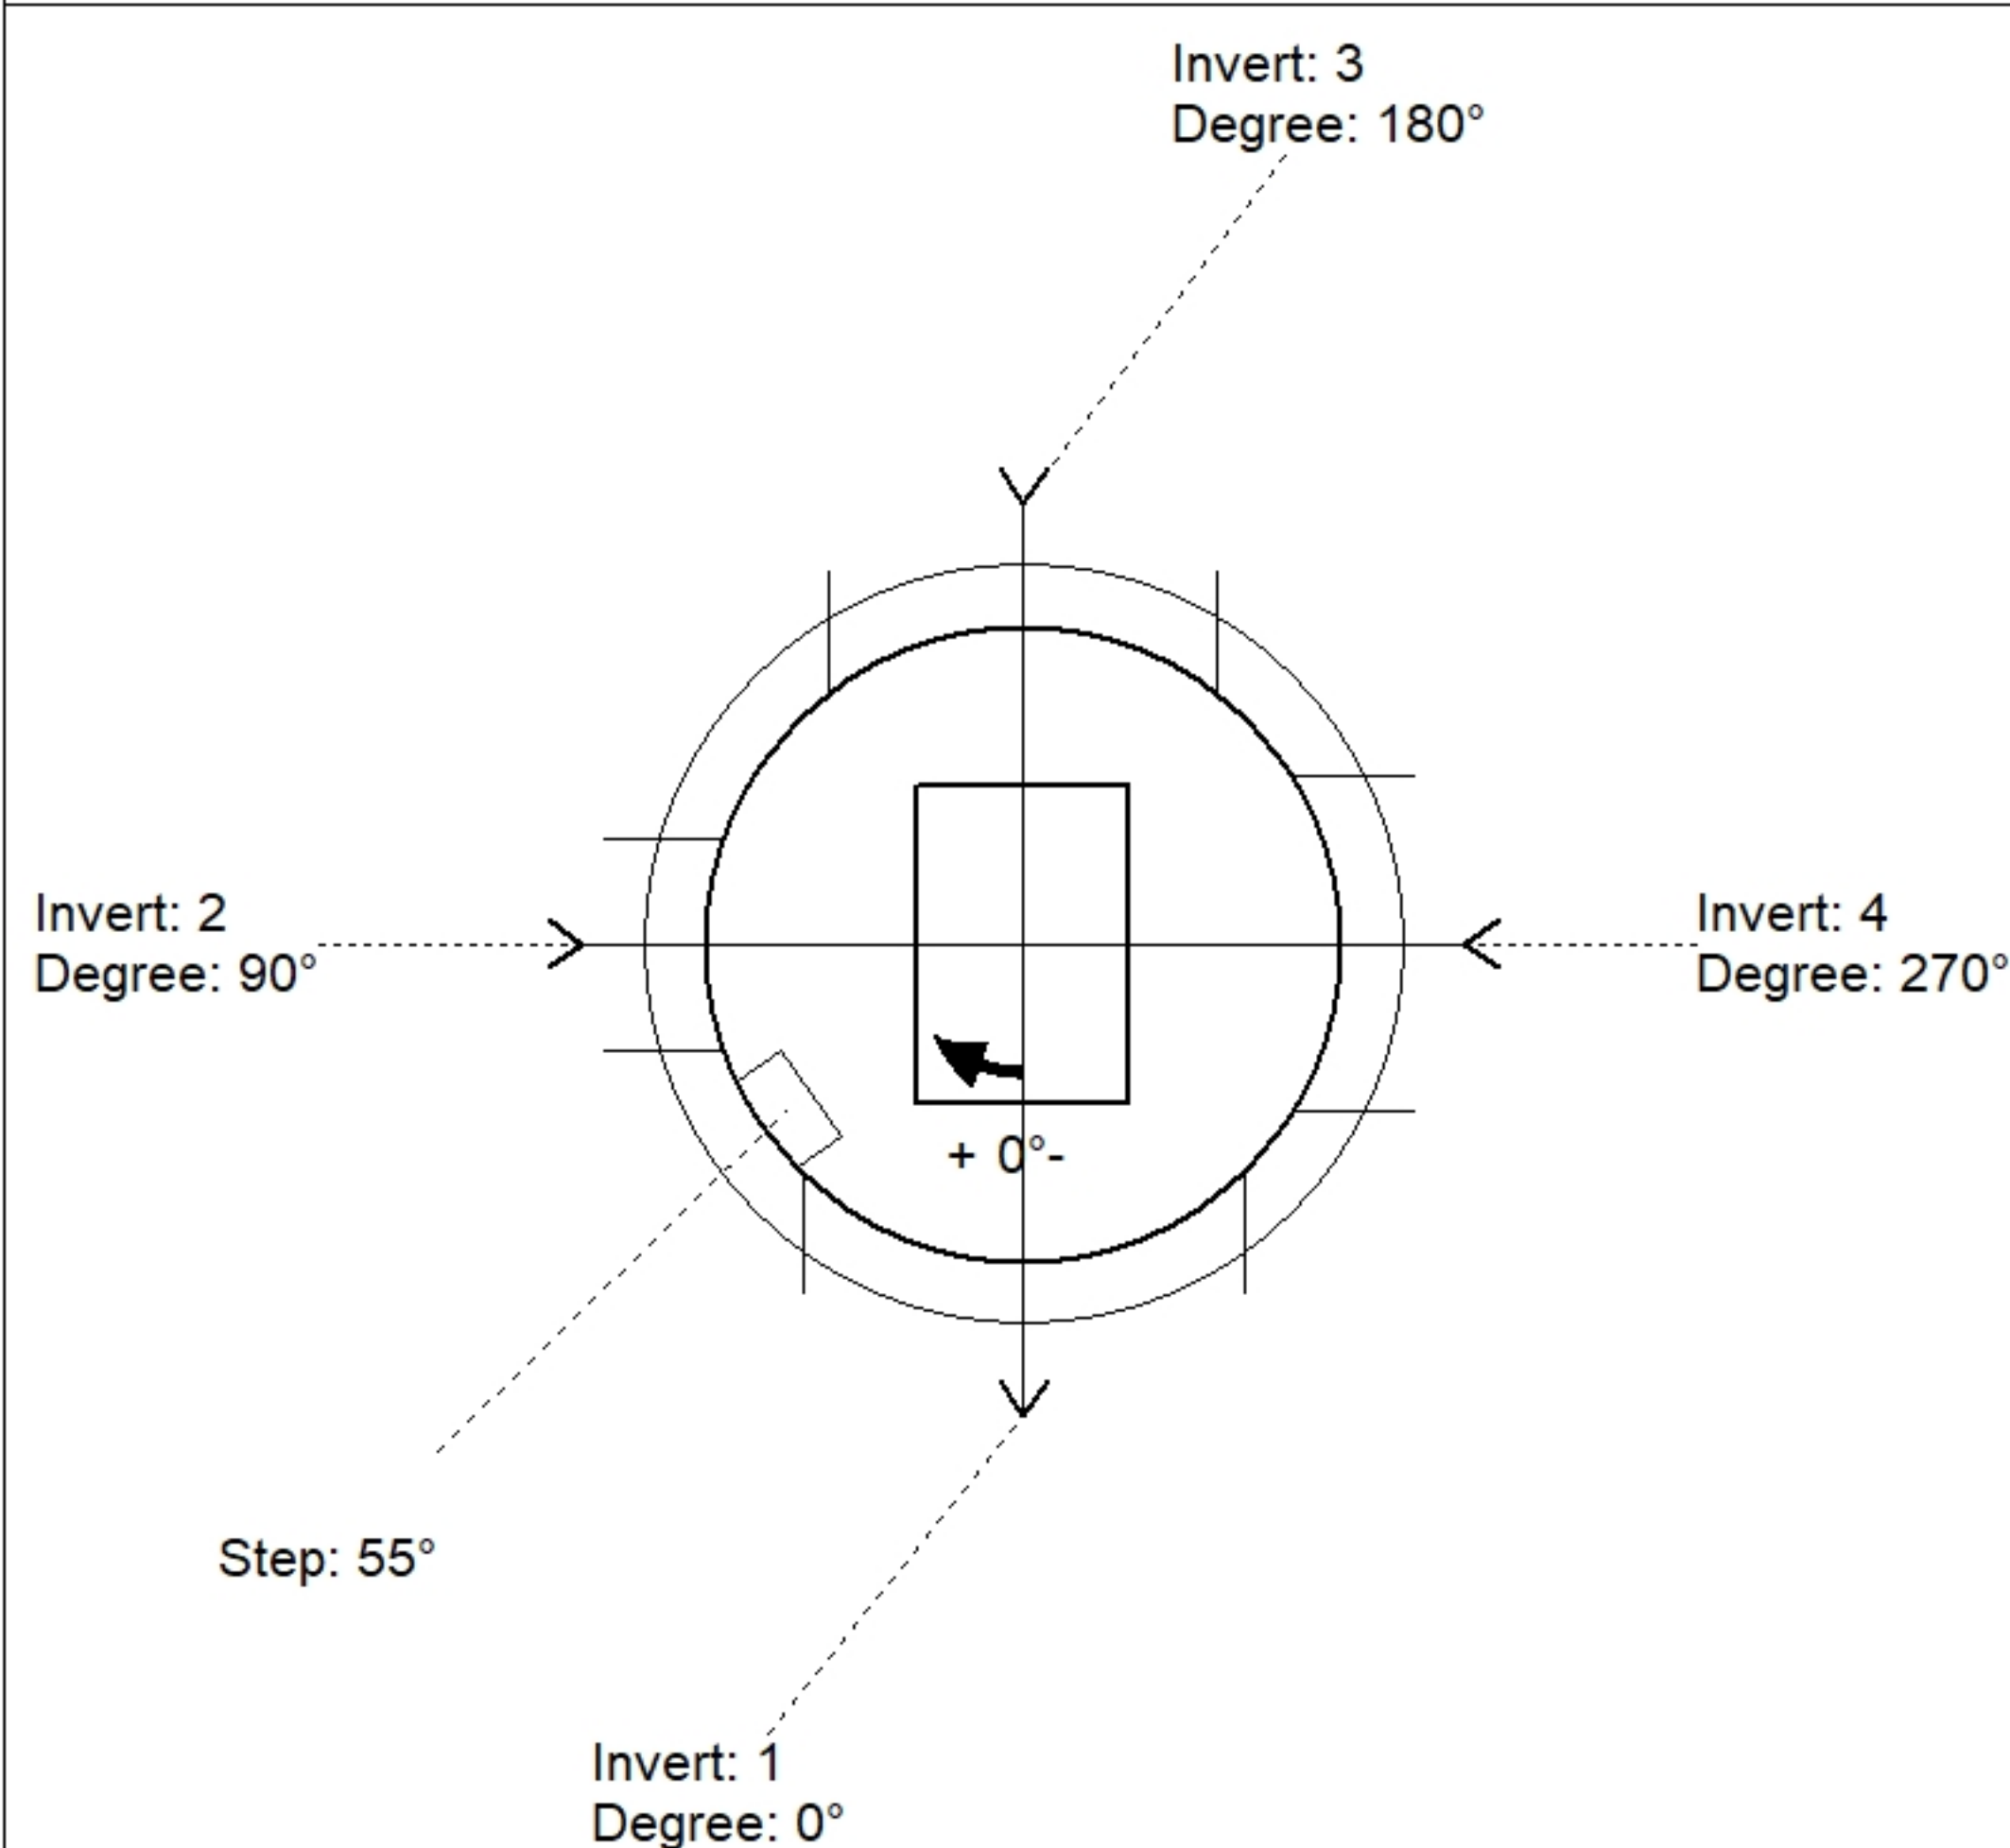

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	932.58'							
Reducer								
Invert 1	927.41'	0°	42" HDPE	47.7"	50" x 49"	DOGHOUSE INVRTD 50"x49"	0"	P1
Invert 2	928.5'	90°	18" HDPE	21.2"	24"	Hole 24	14.63"	P1
Invert 3	927.41'	180°	36" HDPE	41.7"	44"	Hole 44	0.3"	P1
Invert 4	927.41'	270°	30" HDPE	35.1"	38"	Hole 38	0.6"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

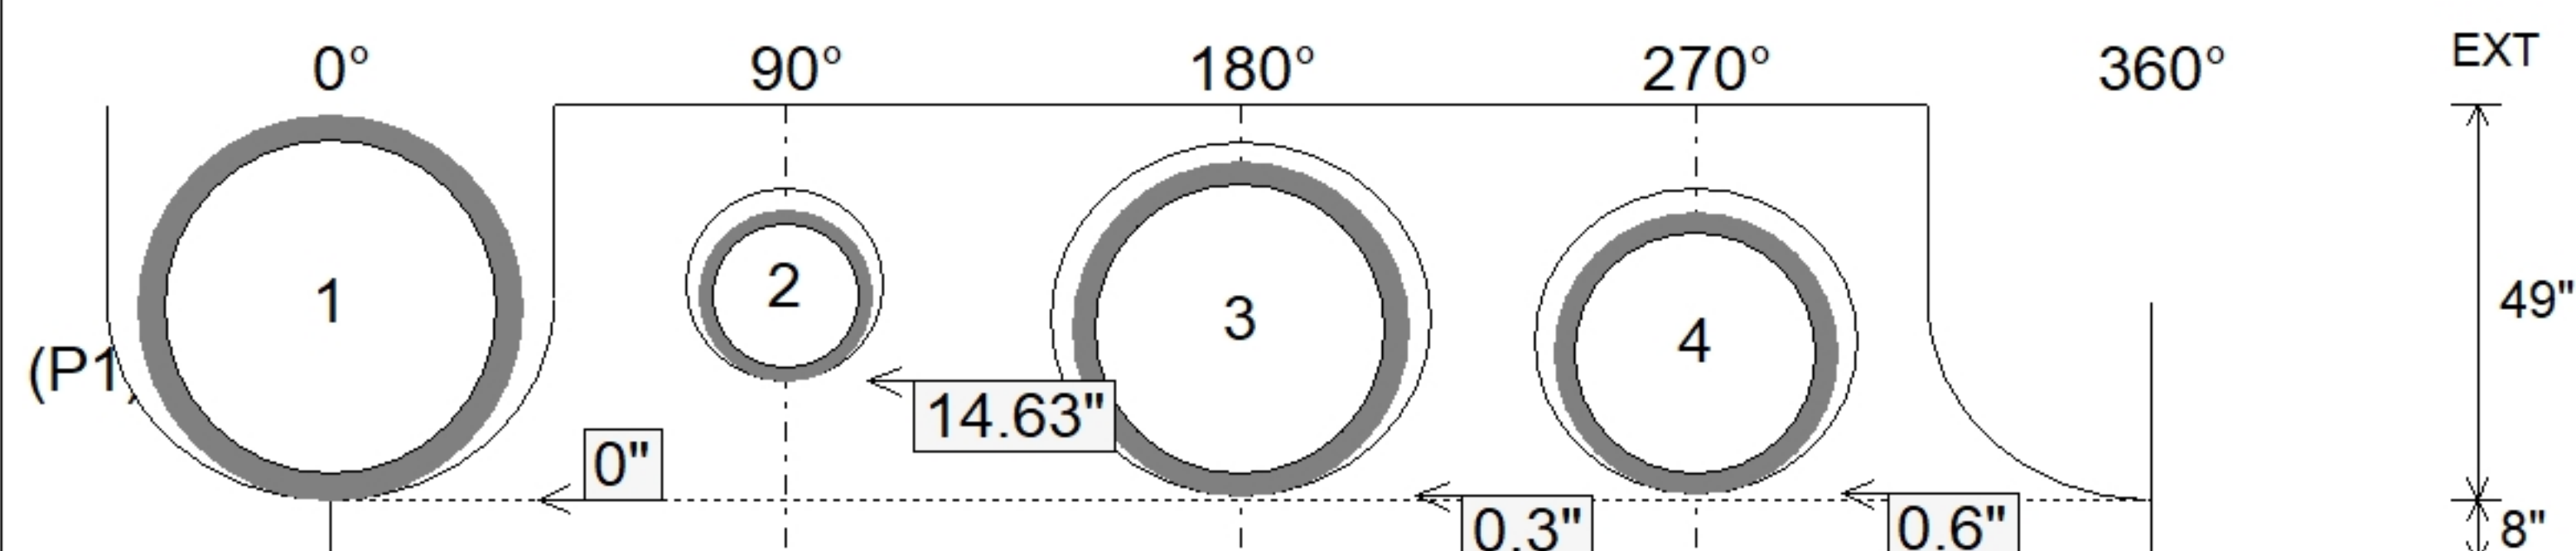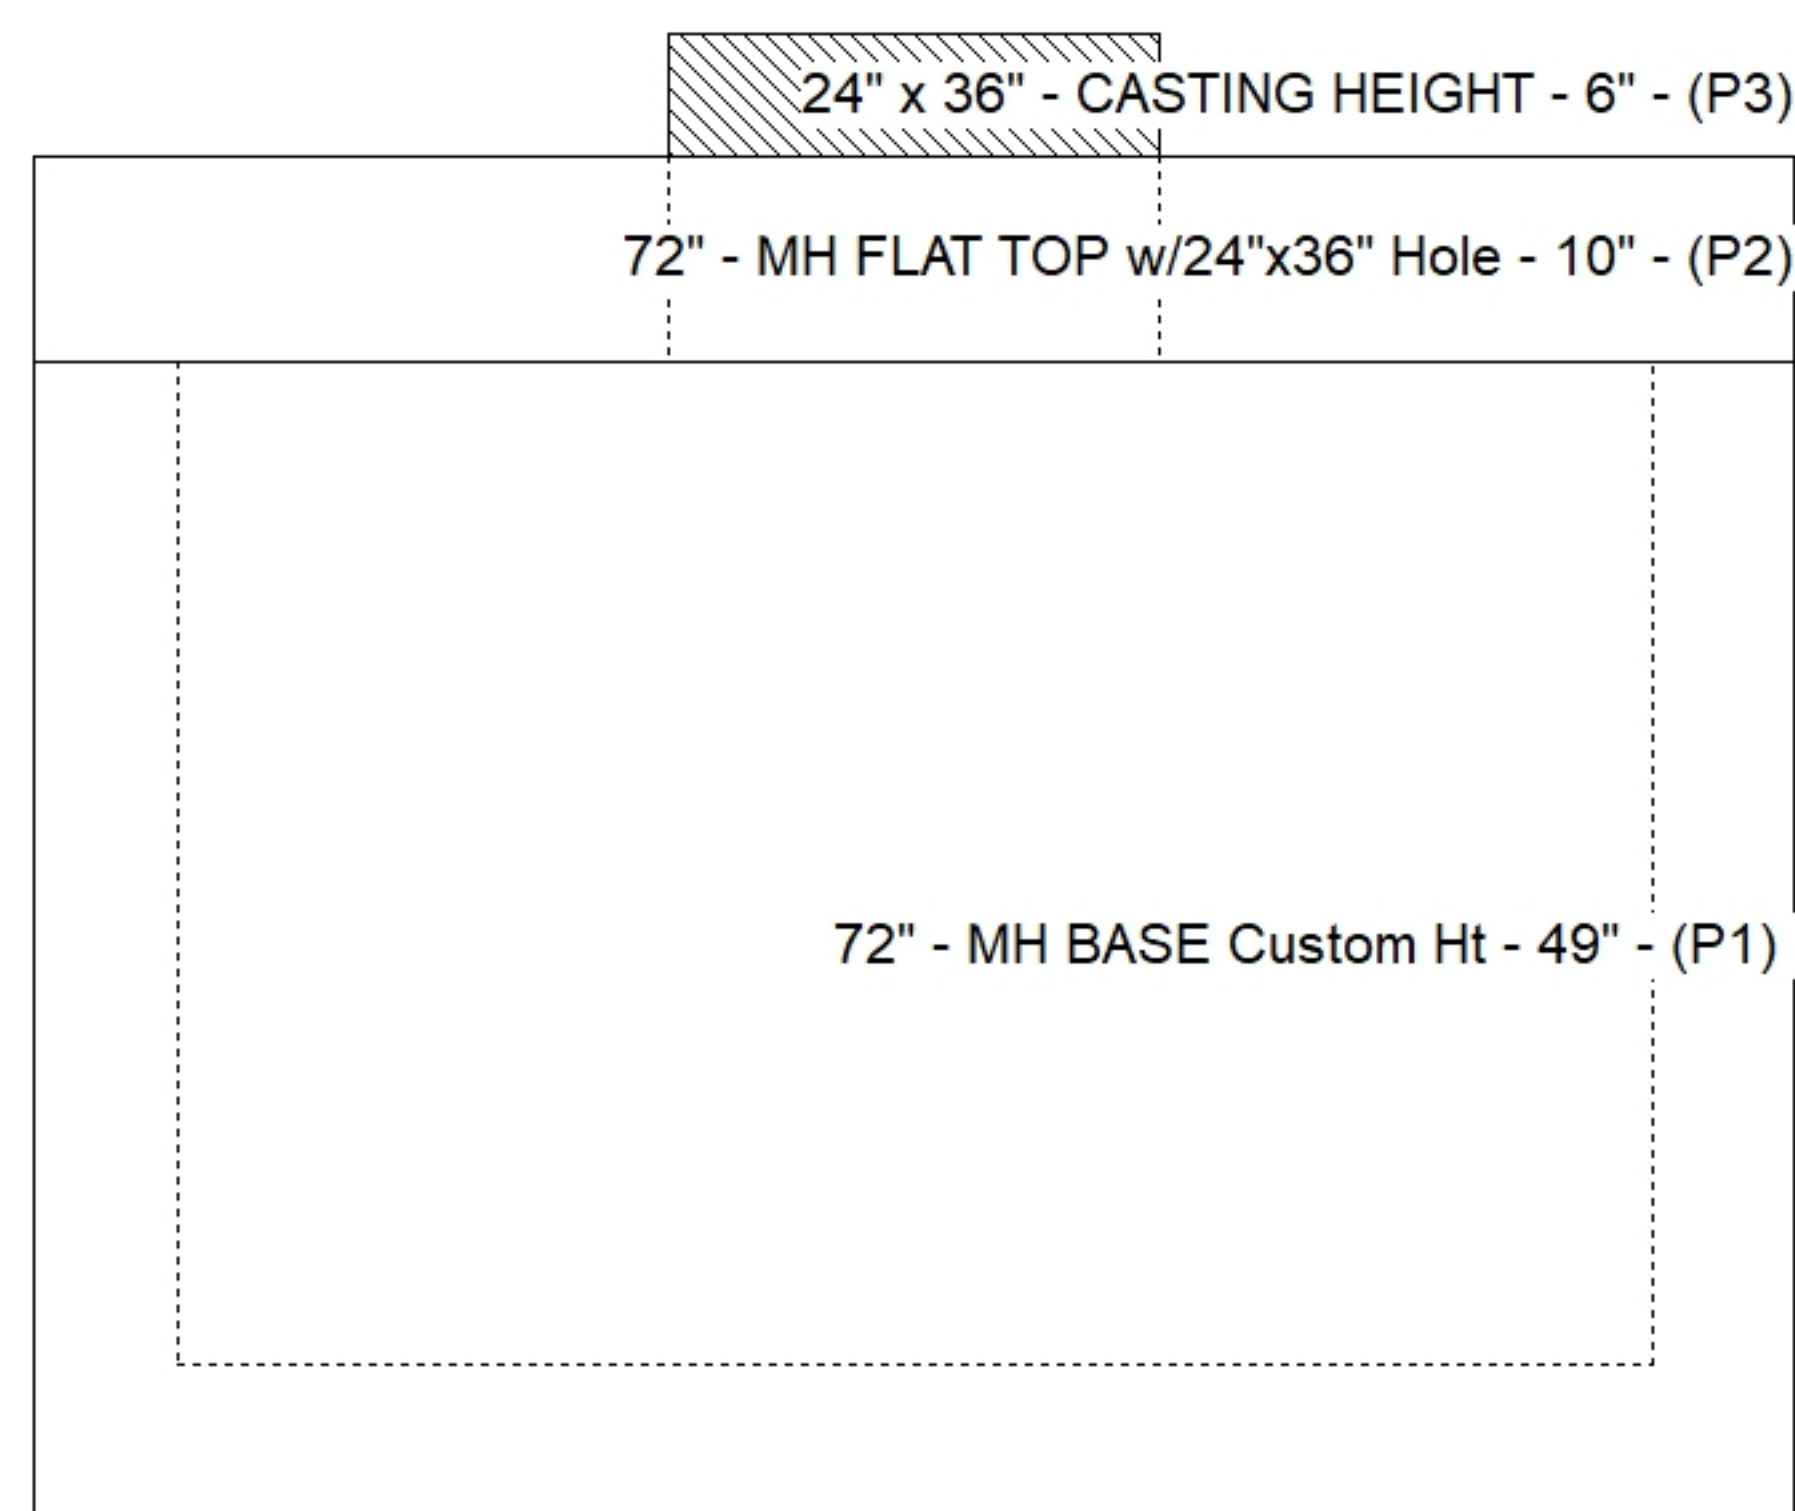

SUBMITTAL
APPROVED BY:
