


Contractor: KY Earthworks

Plant: 100



Slack: 2.82"

Structure Total:	5153 lb
------------------	---------

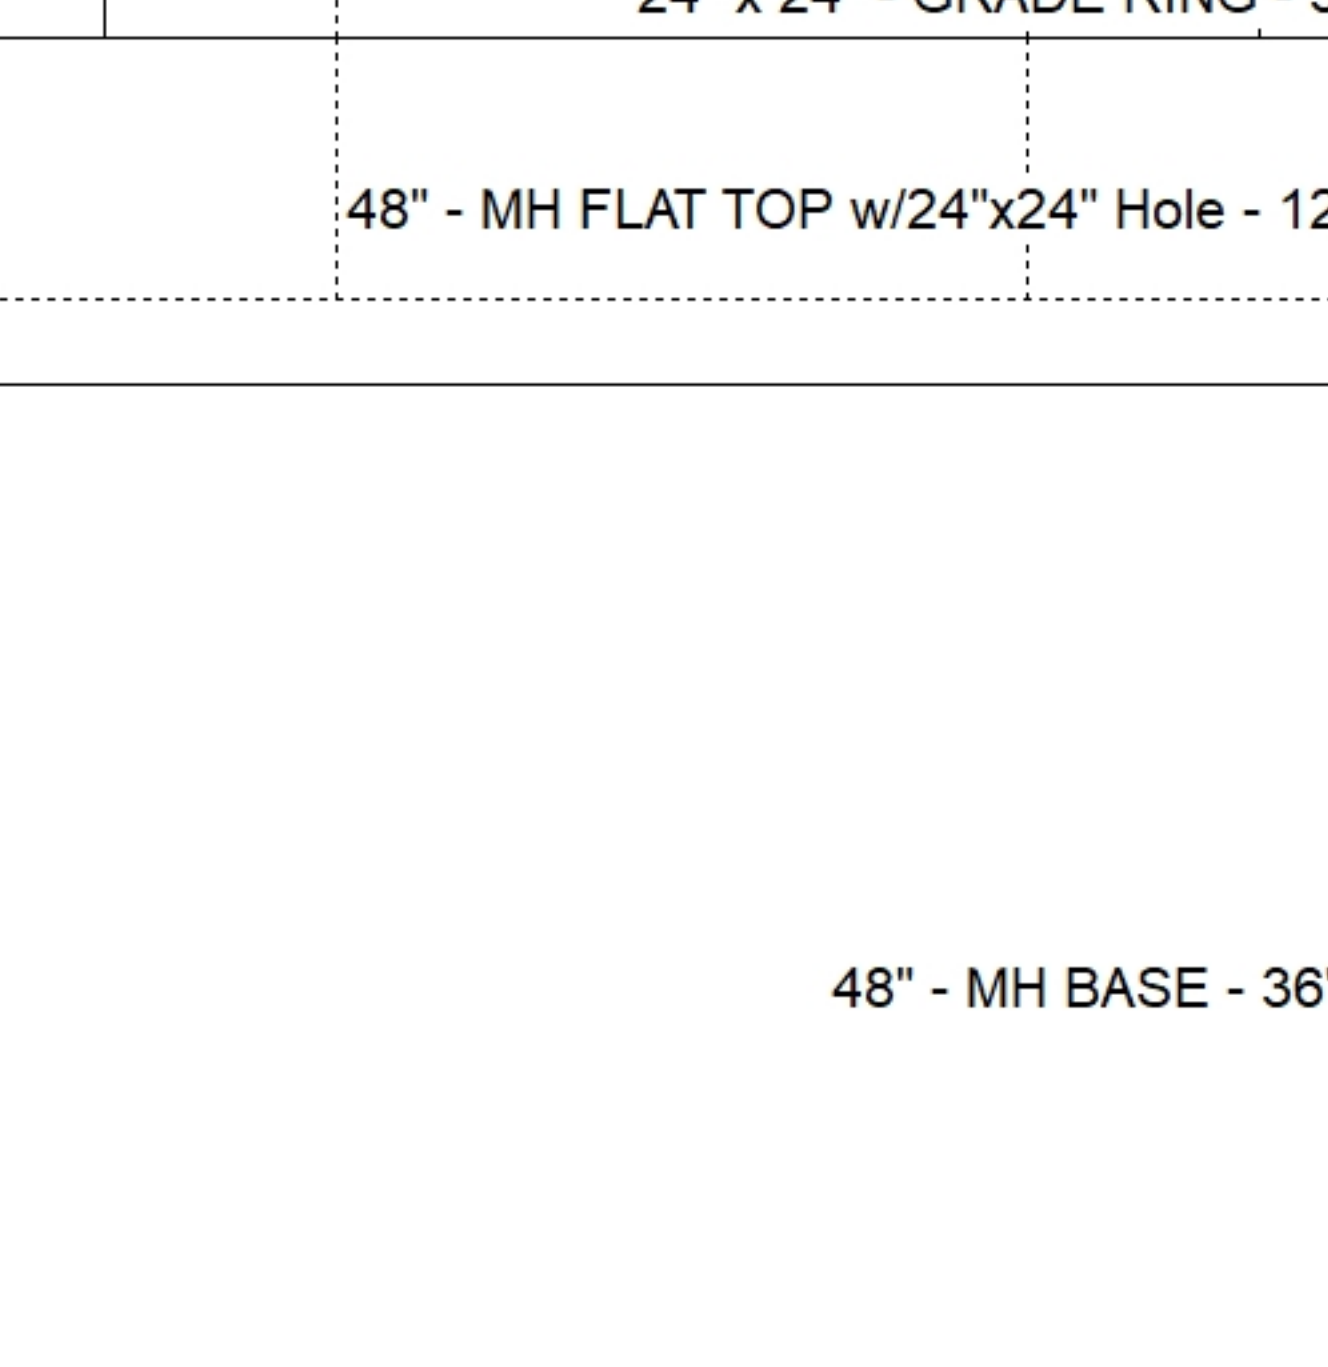

24" x 24" - CASTING HEIGHT - 4" - (P4)

24" x 24" - GRADE RING - 3" - (P3)

48" - MH FLAT TOP w/24"x24" Hole - 12" - (P2)

48" - MH BASE - 36" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌋)	Ref
Rim	933.1'							
Reducer								
Invert 1	928.44'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	928.44'	125°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
