


Contractor: KY Earthworks

Plant: 100




Slack: 1.1"

Structure Total:	5379 lb
------------------	---------

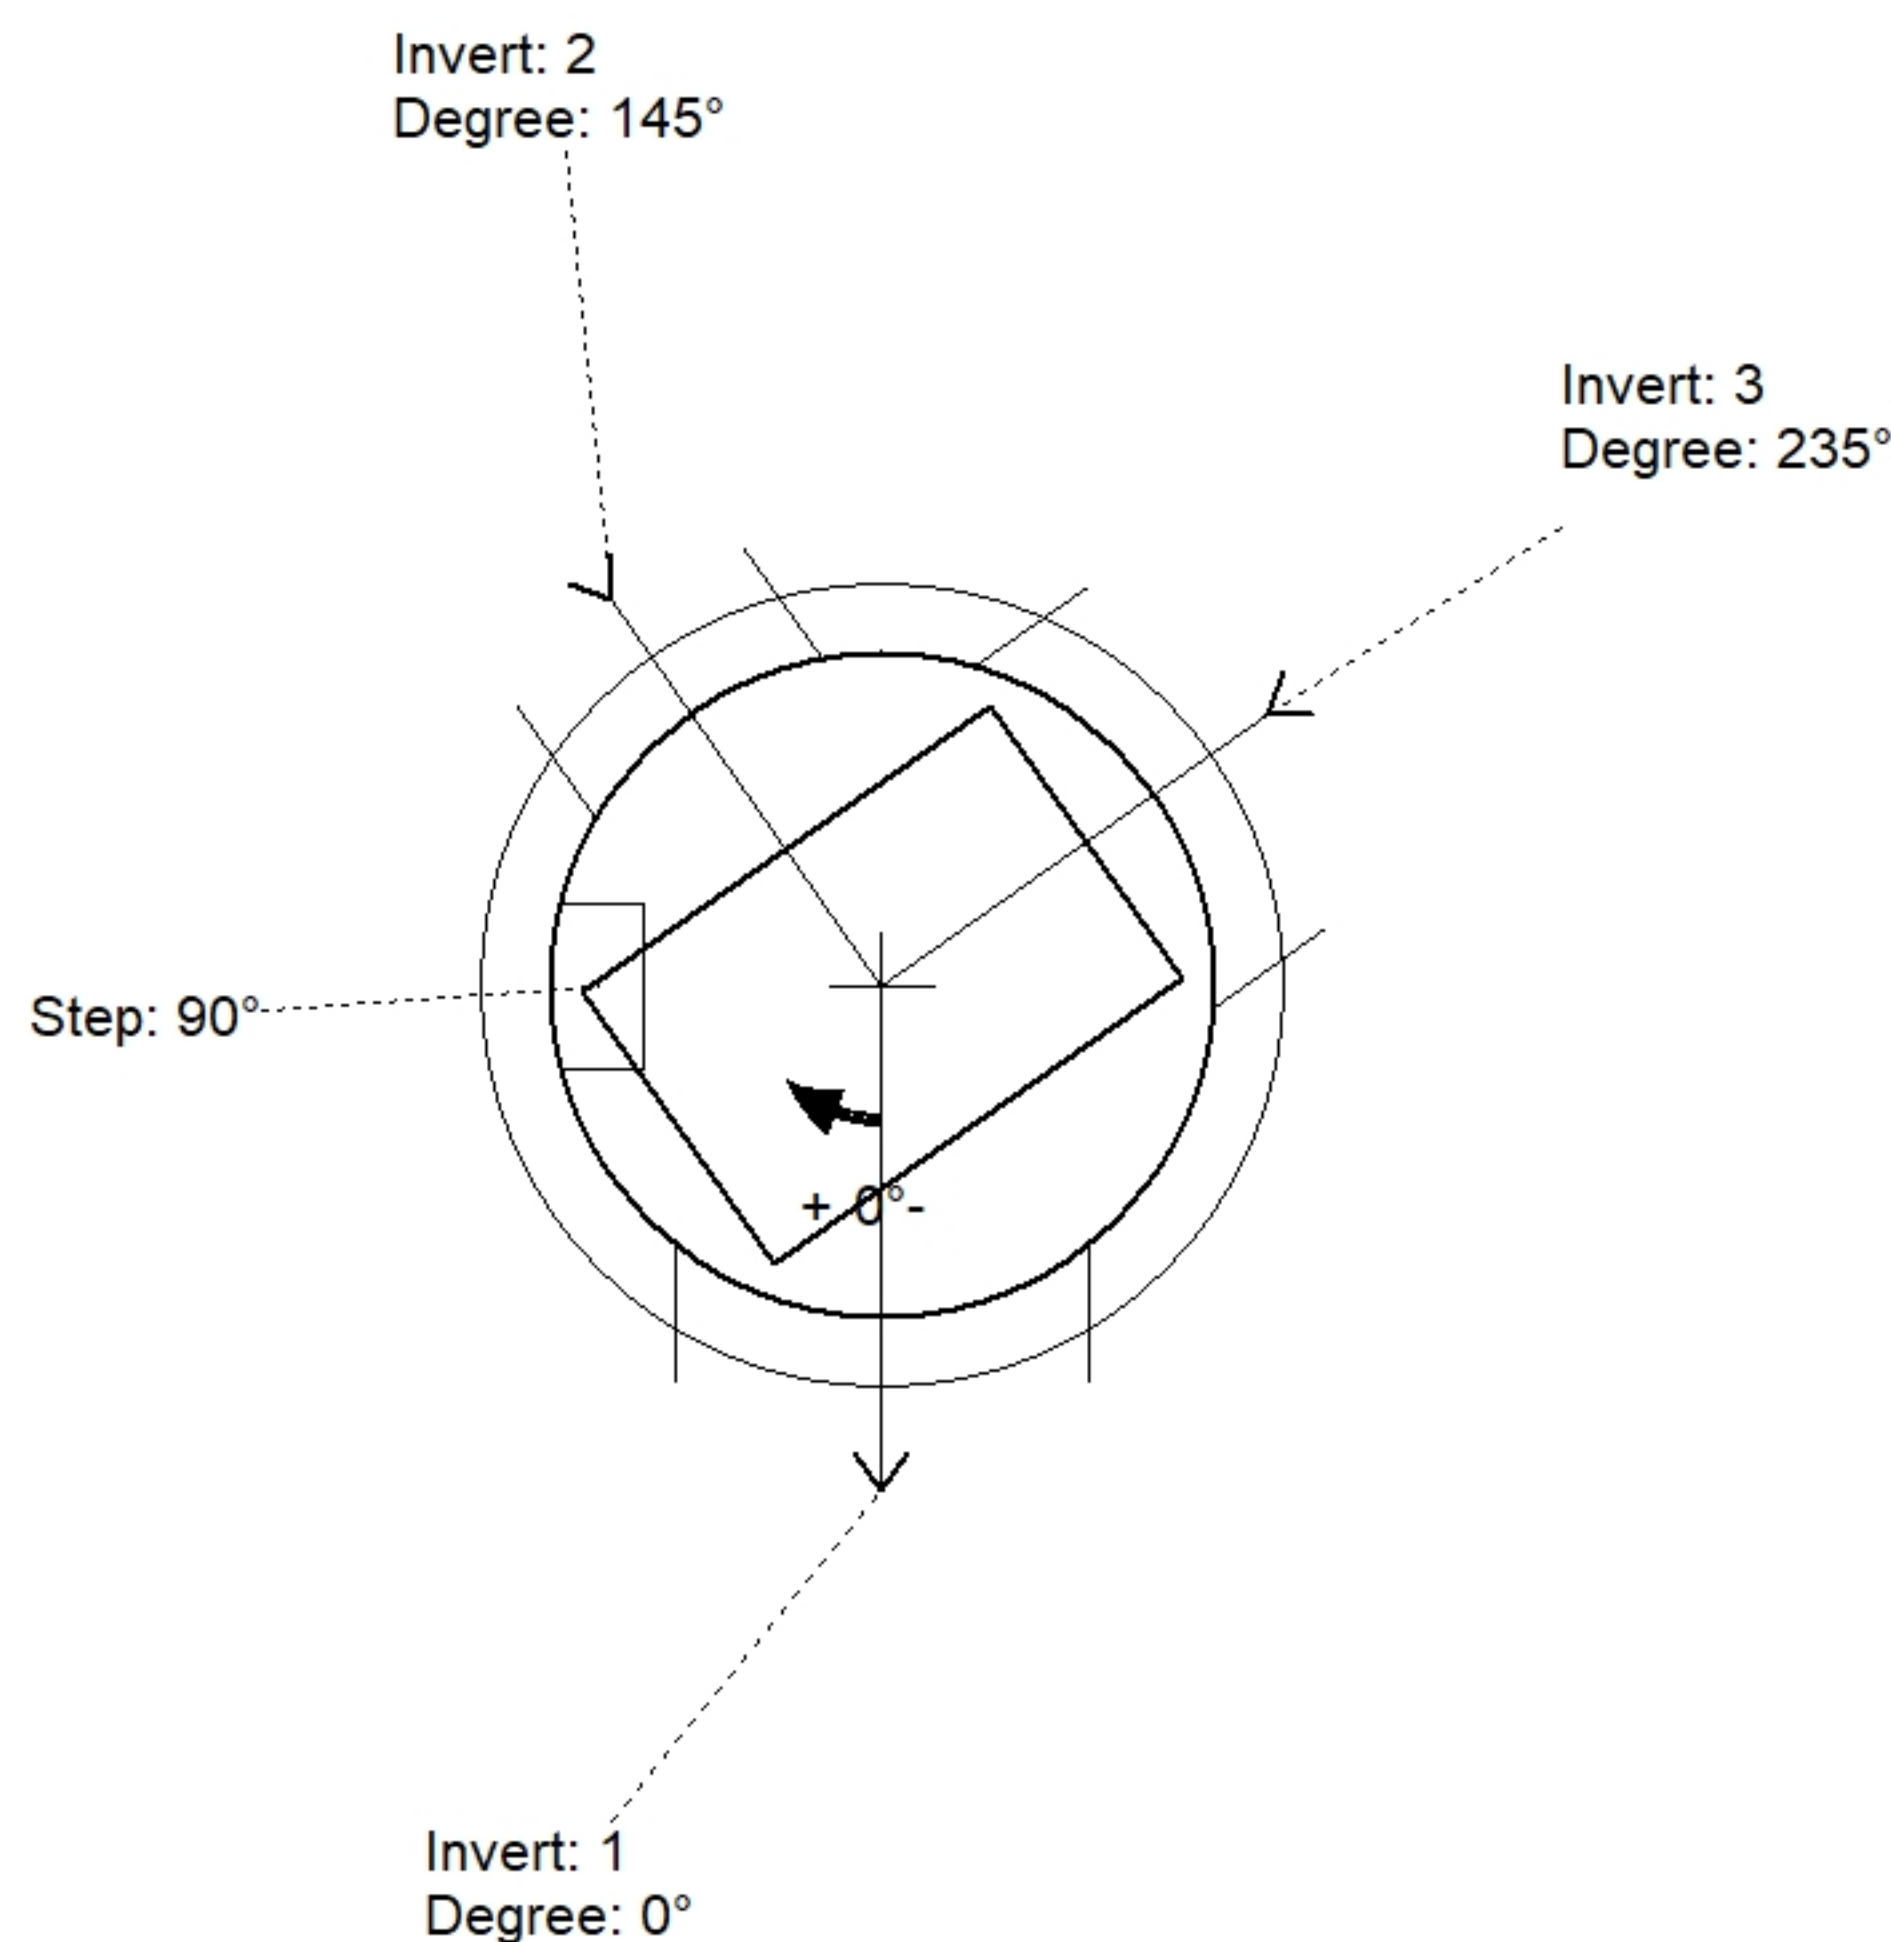

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	934.15'							
Reducer								
Invert 1	929.05'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	930.55'	145°	15" HDPE	17.6"	20"	Hole 20	18.6"	P1
Invert 3	929.05'	235°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

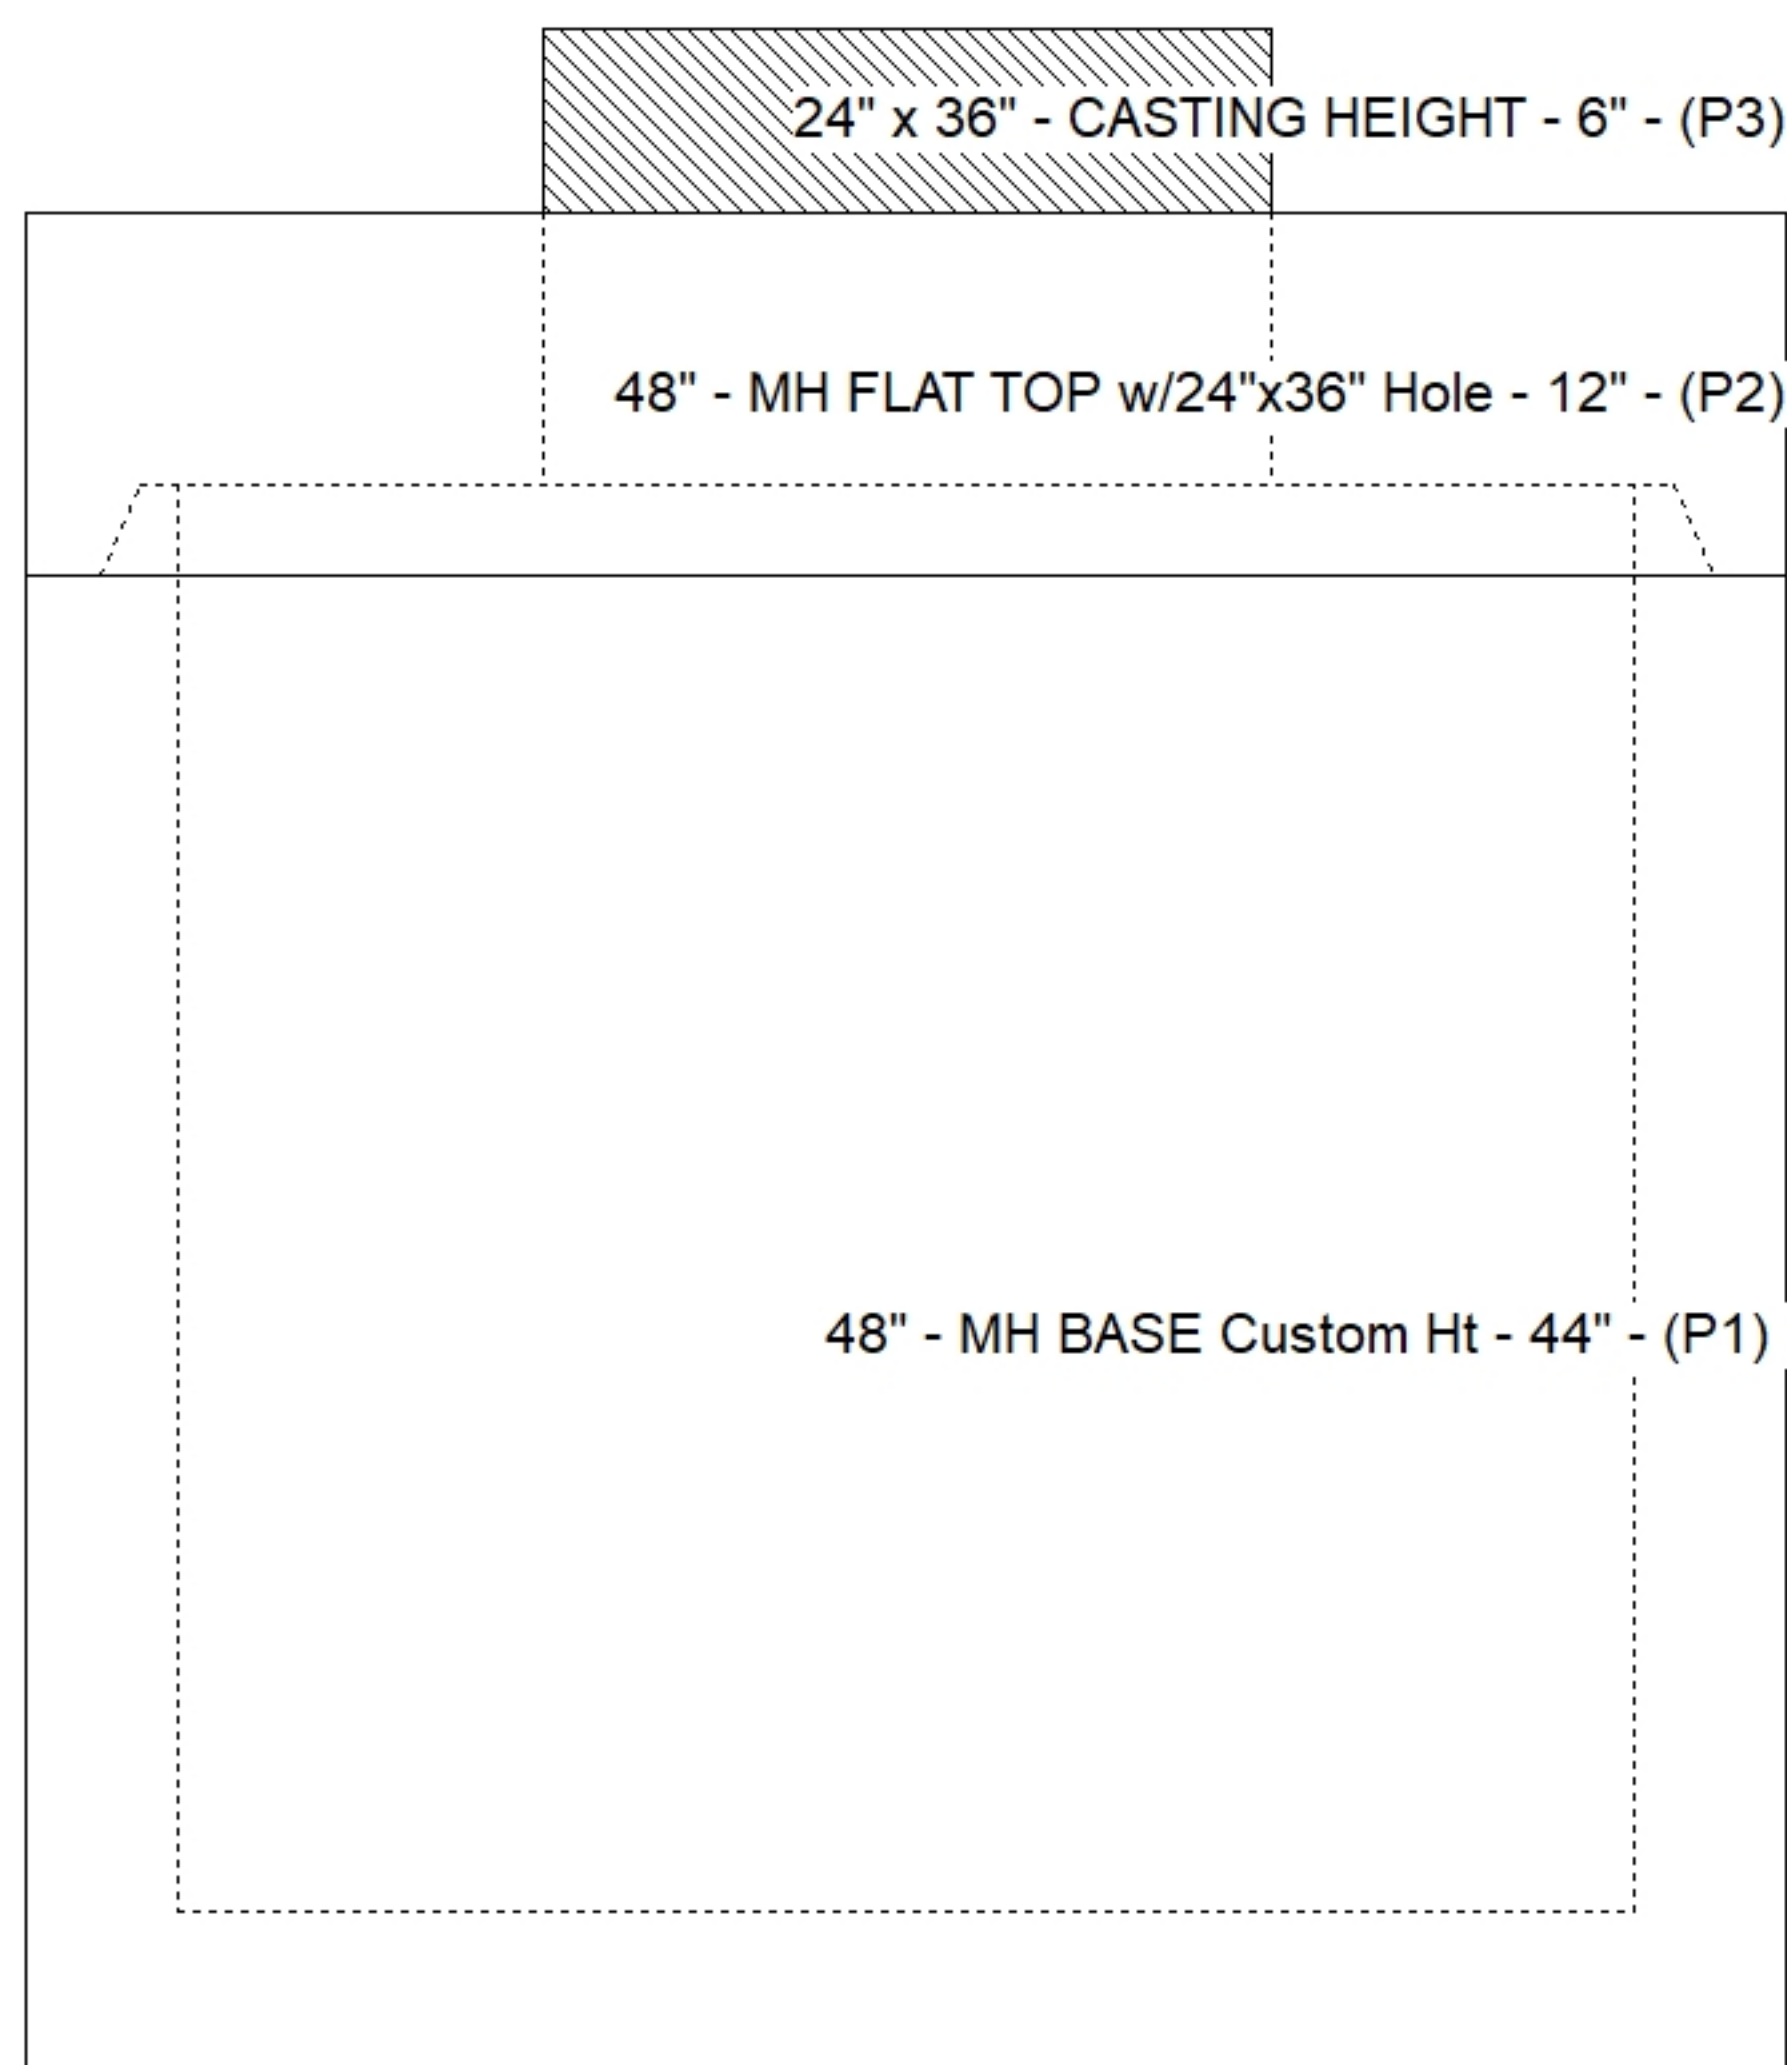

SUBMITTAL
APPROVED BY:
