

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 3.22'

Floor Height: 6"

Slack: 1.94"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P1) 48" - MH BASE Custom Ht - 25"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 20
2) MH Step ML-10-TDS-NCR - 10"



0 lb
1044 lb
2806 lb
442 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 4293 lb

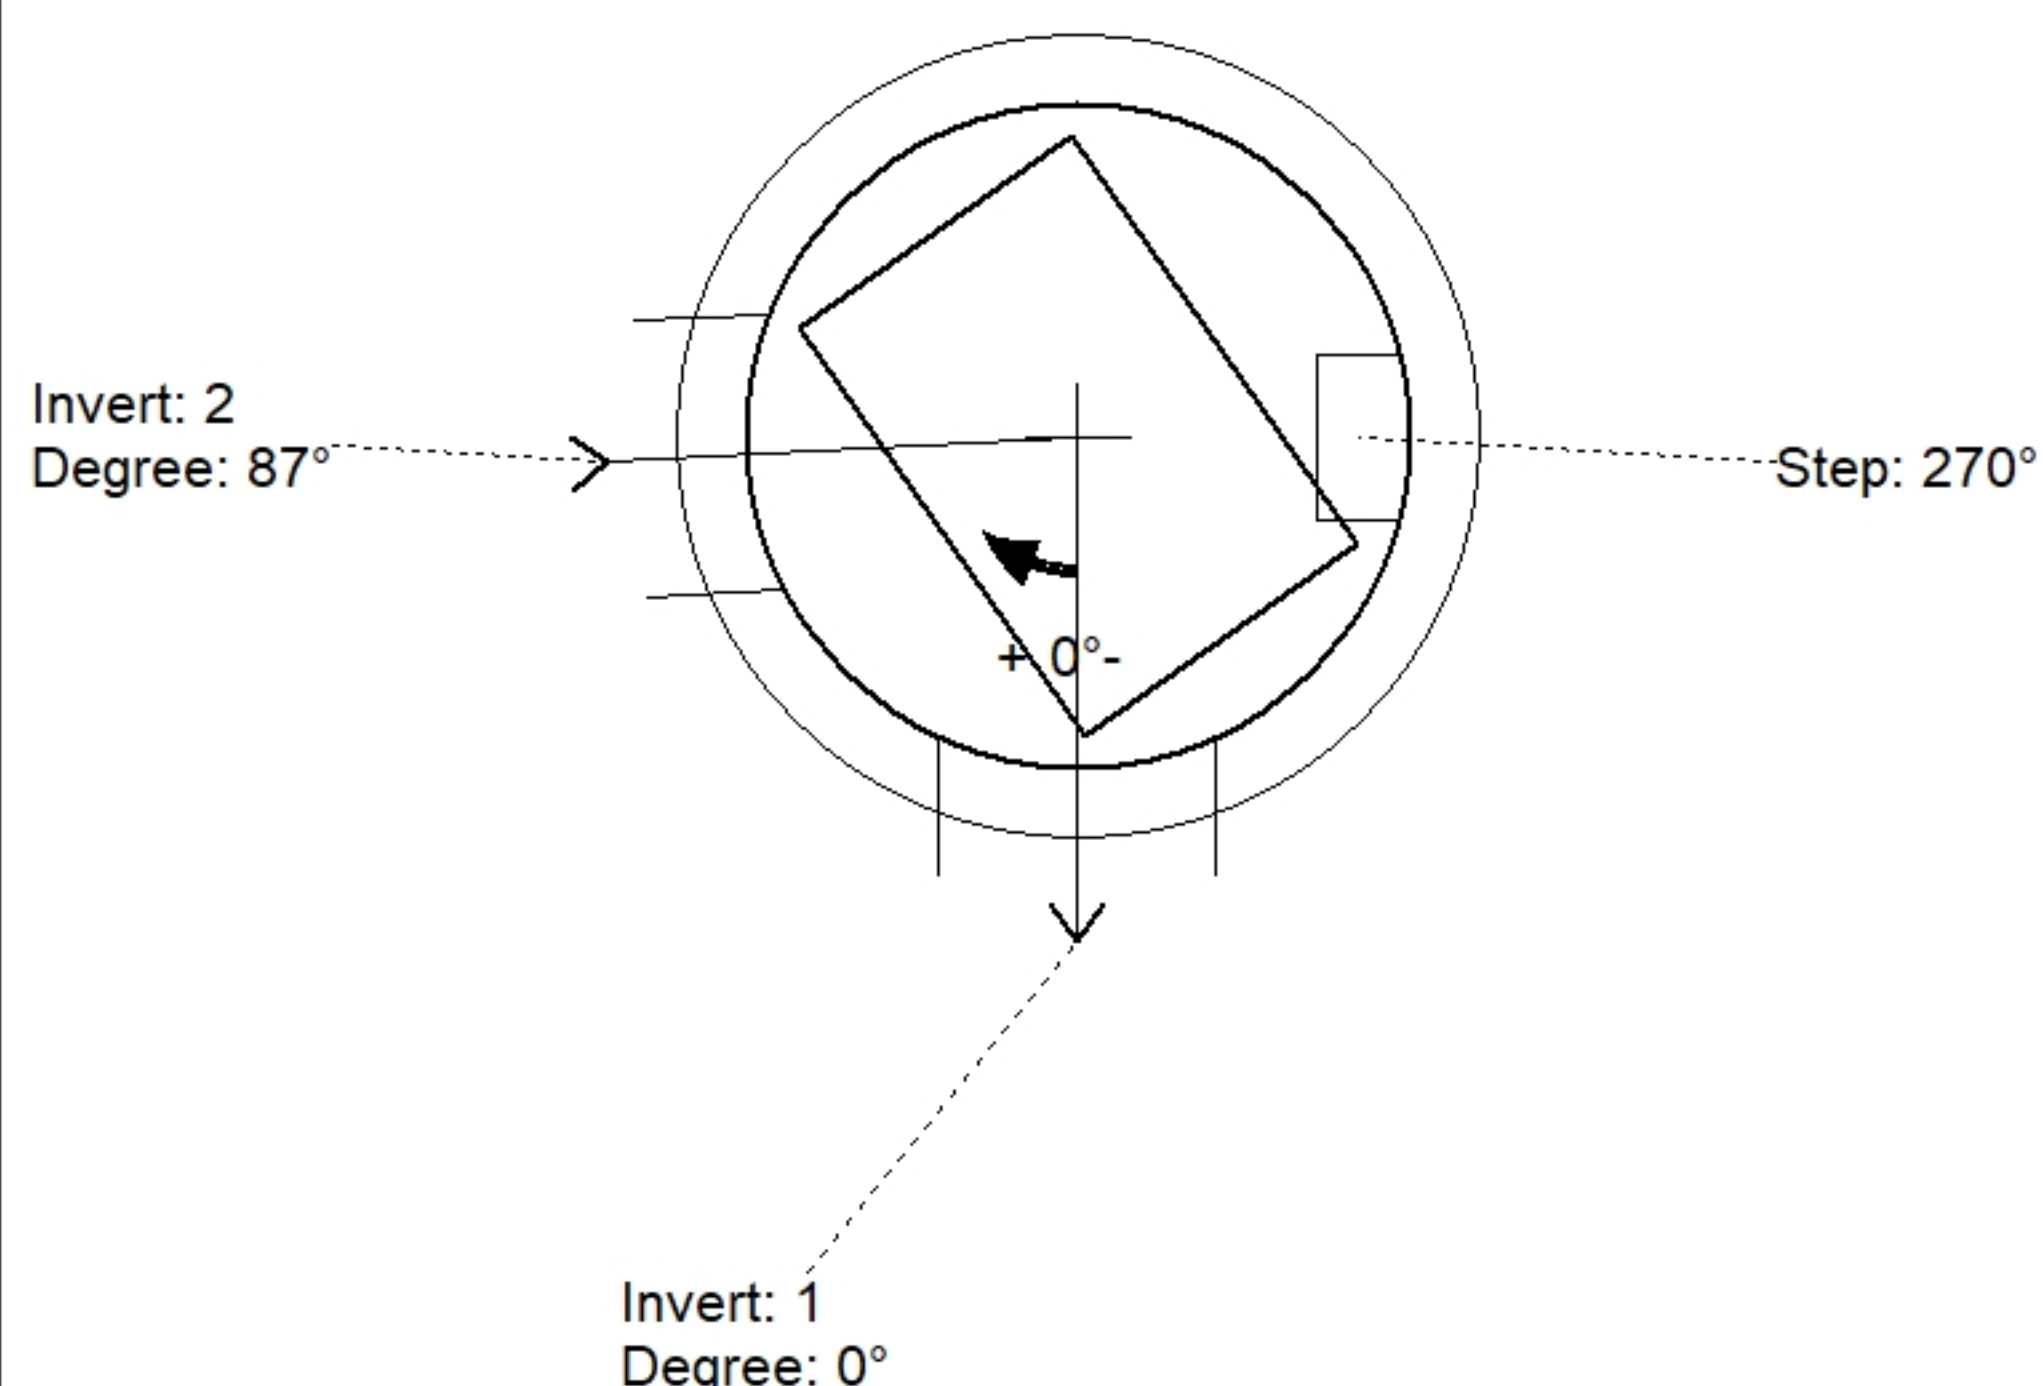

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	934.59'							
Reducer								
Invert 1	931.37'	0°	15" HDPE	17.6"	20"	Hole 20	0"	P1
Invert 2	931.37'	87°	15" HDPE	17.6"	20"	Hole 20	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

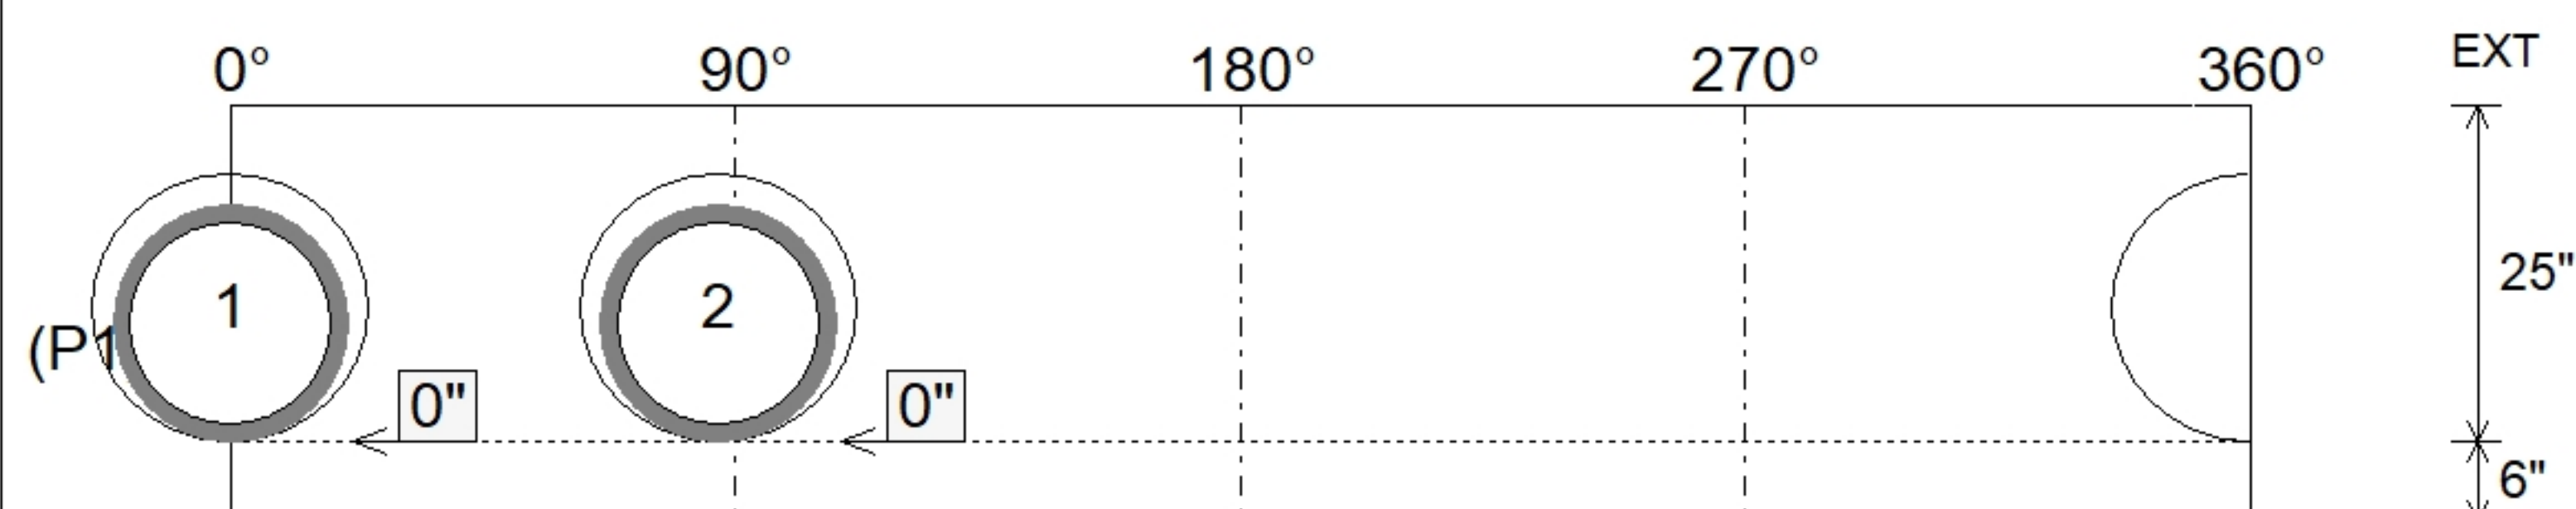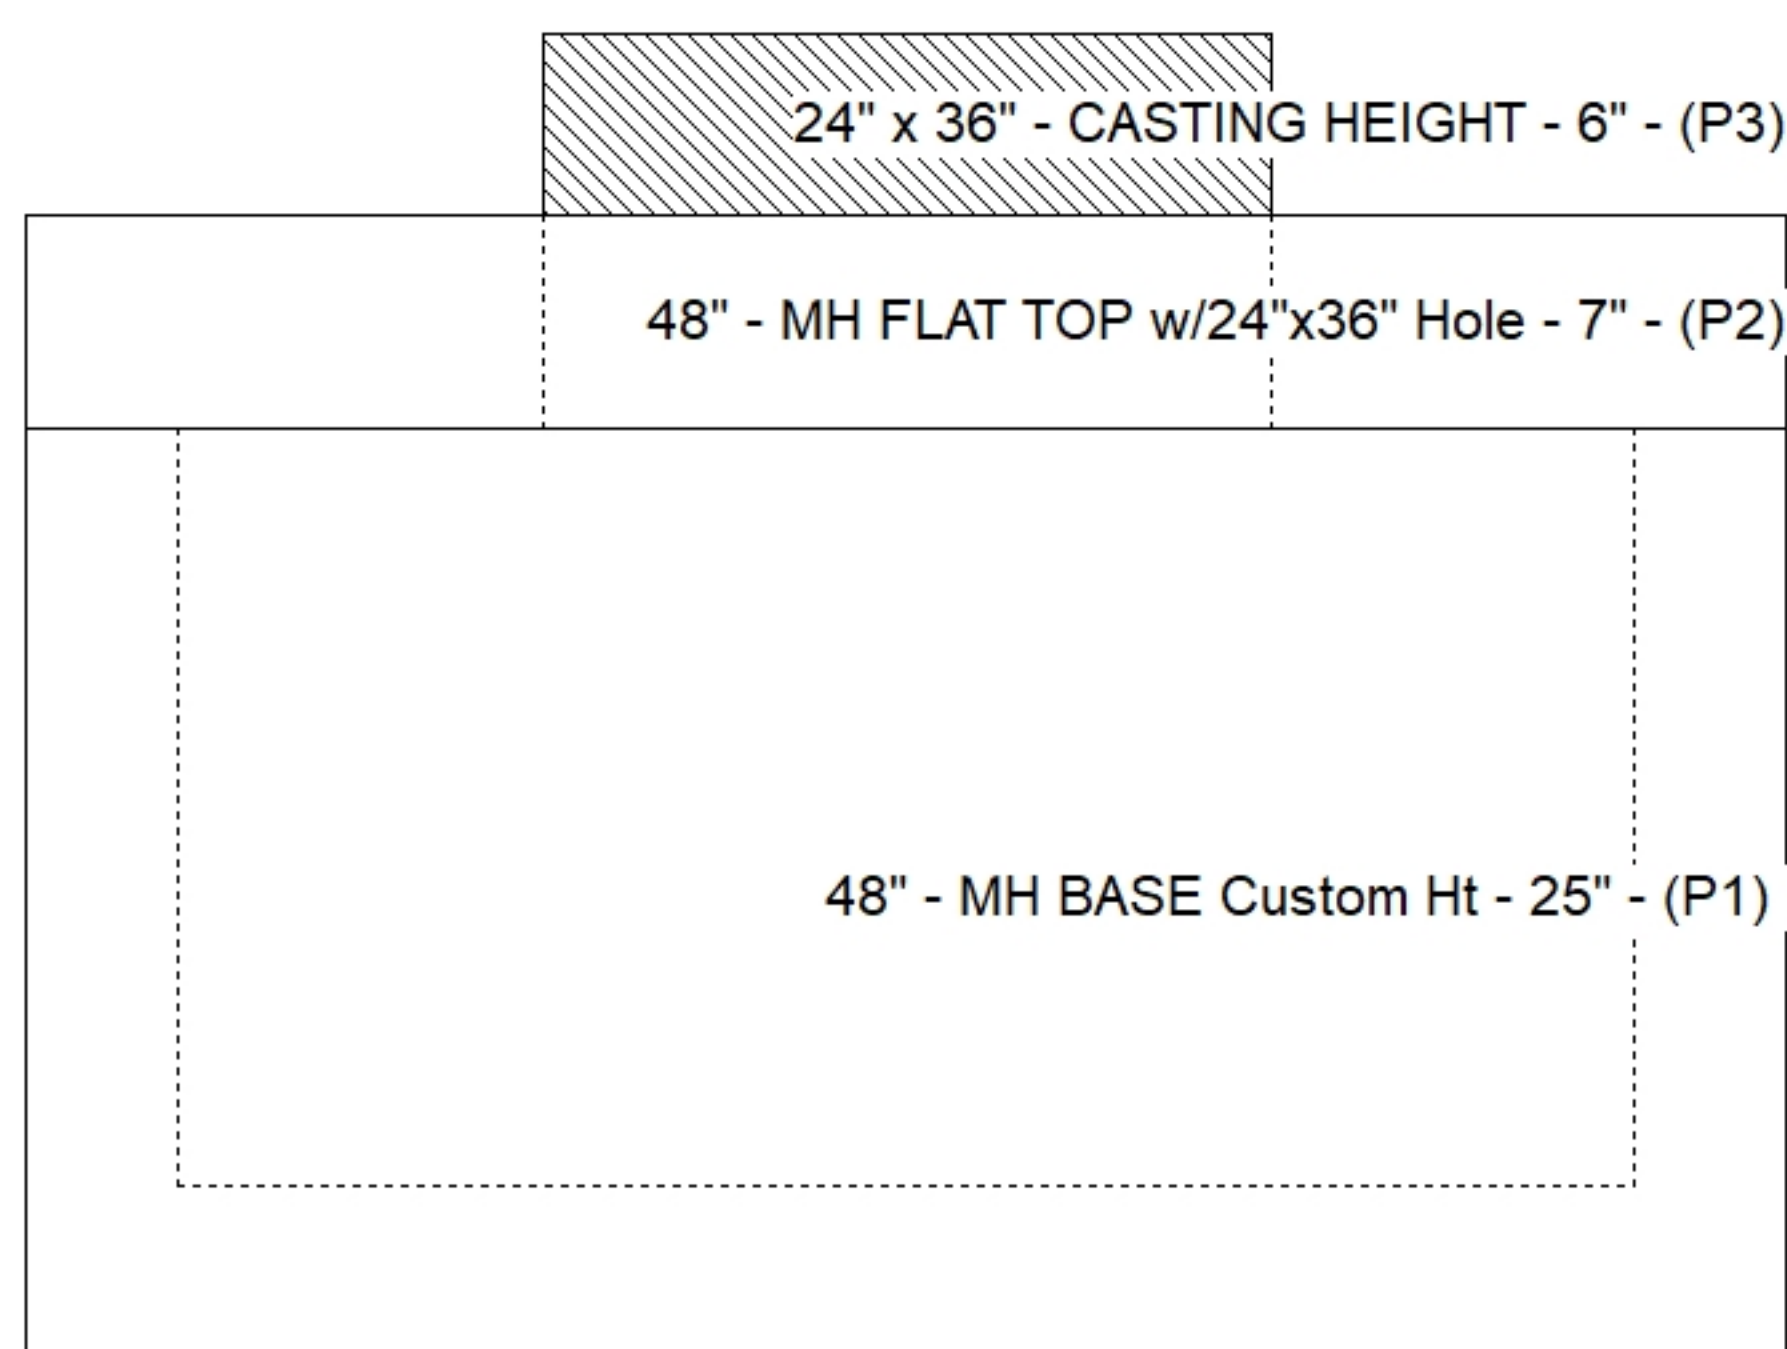

Submittal Drawing
9/29/2026 8:25:52 AM

SUBMITTAL
APPROVED BY:
