

Contractor: KY Earthworks

Plant: 100



Size: 24" x 24"

Rim to Invert: 4.86'

Floor Height: 8"


Slack: 1.92"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 24" - CASTING HEIGHT - 4"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 54"
1) CASTING - HOE 280T F/G
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 24

0 lb
5486 lb
182 lb
0 lb
0 lb

Structure Total: 5668 lb

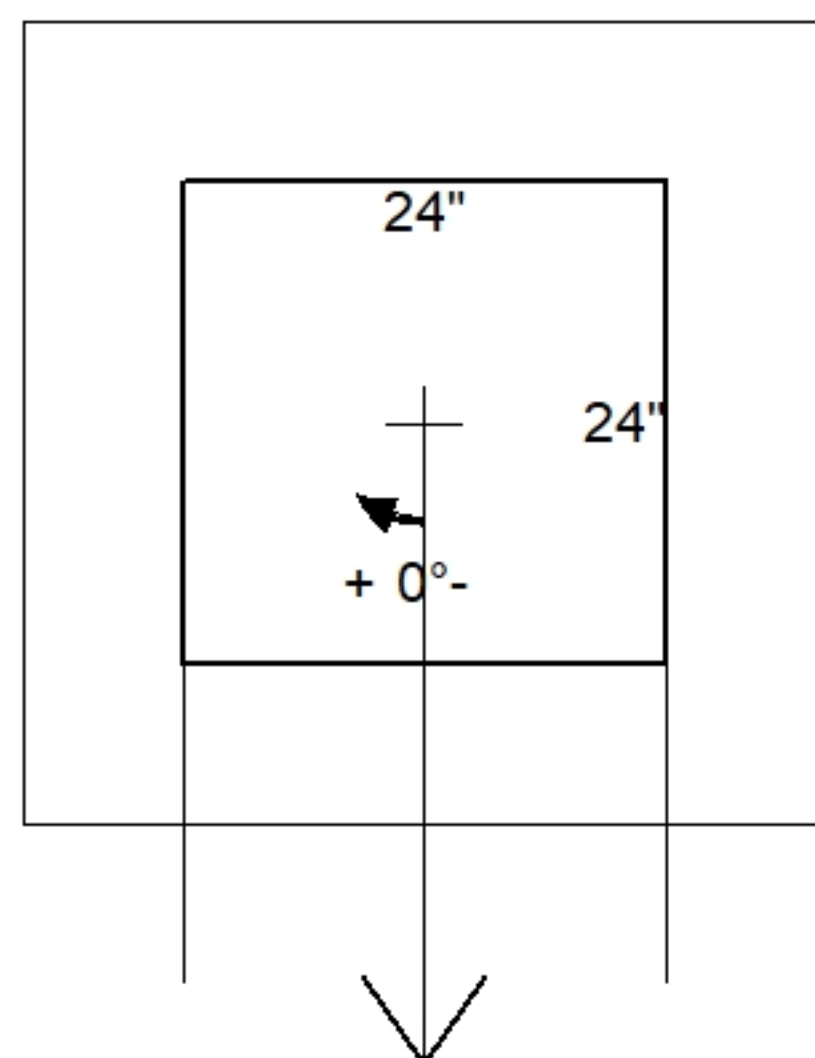


Invert: 1
Degree: 0°

24" x 24" - CASTING HEIGHT - 4" - (P2)

24" x 24" - BOX BASE 8inW, 8inF - 54" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	934.5'							
Reducer								
Invert 1	929.64'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

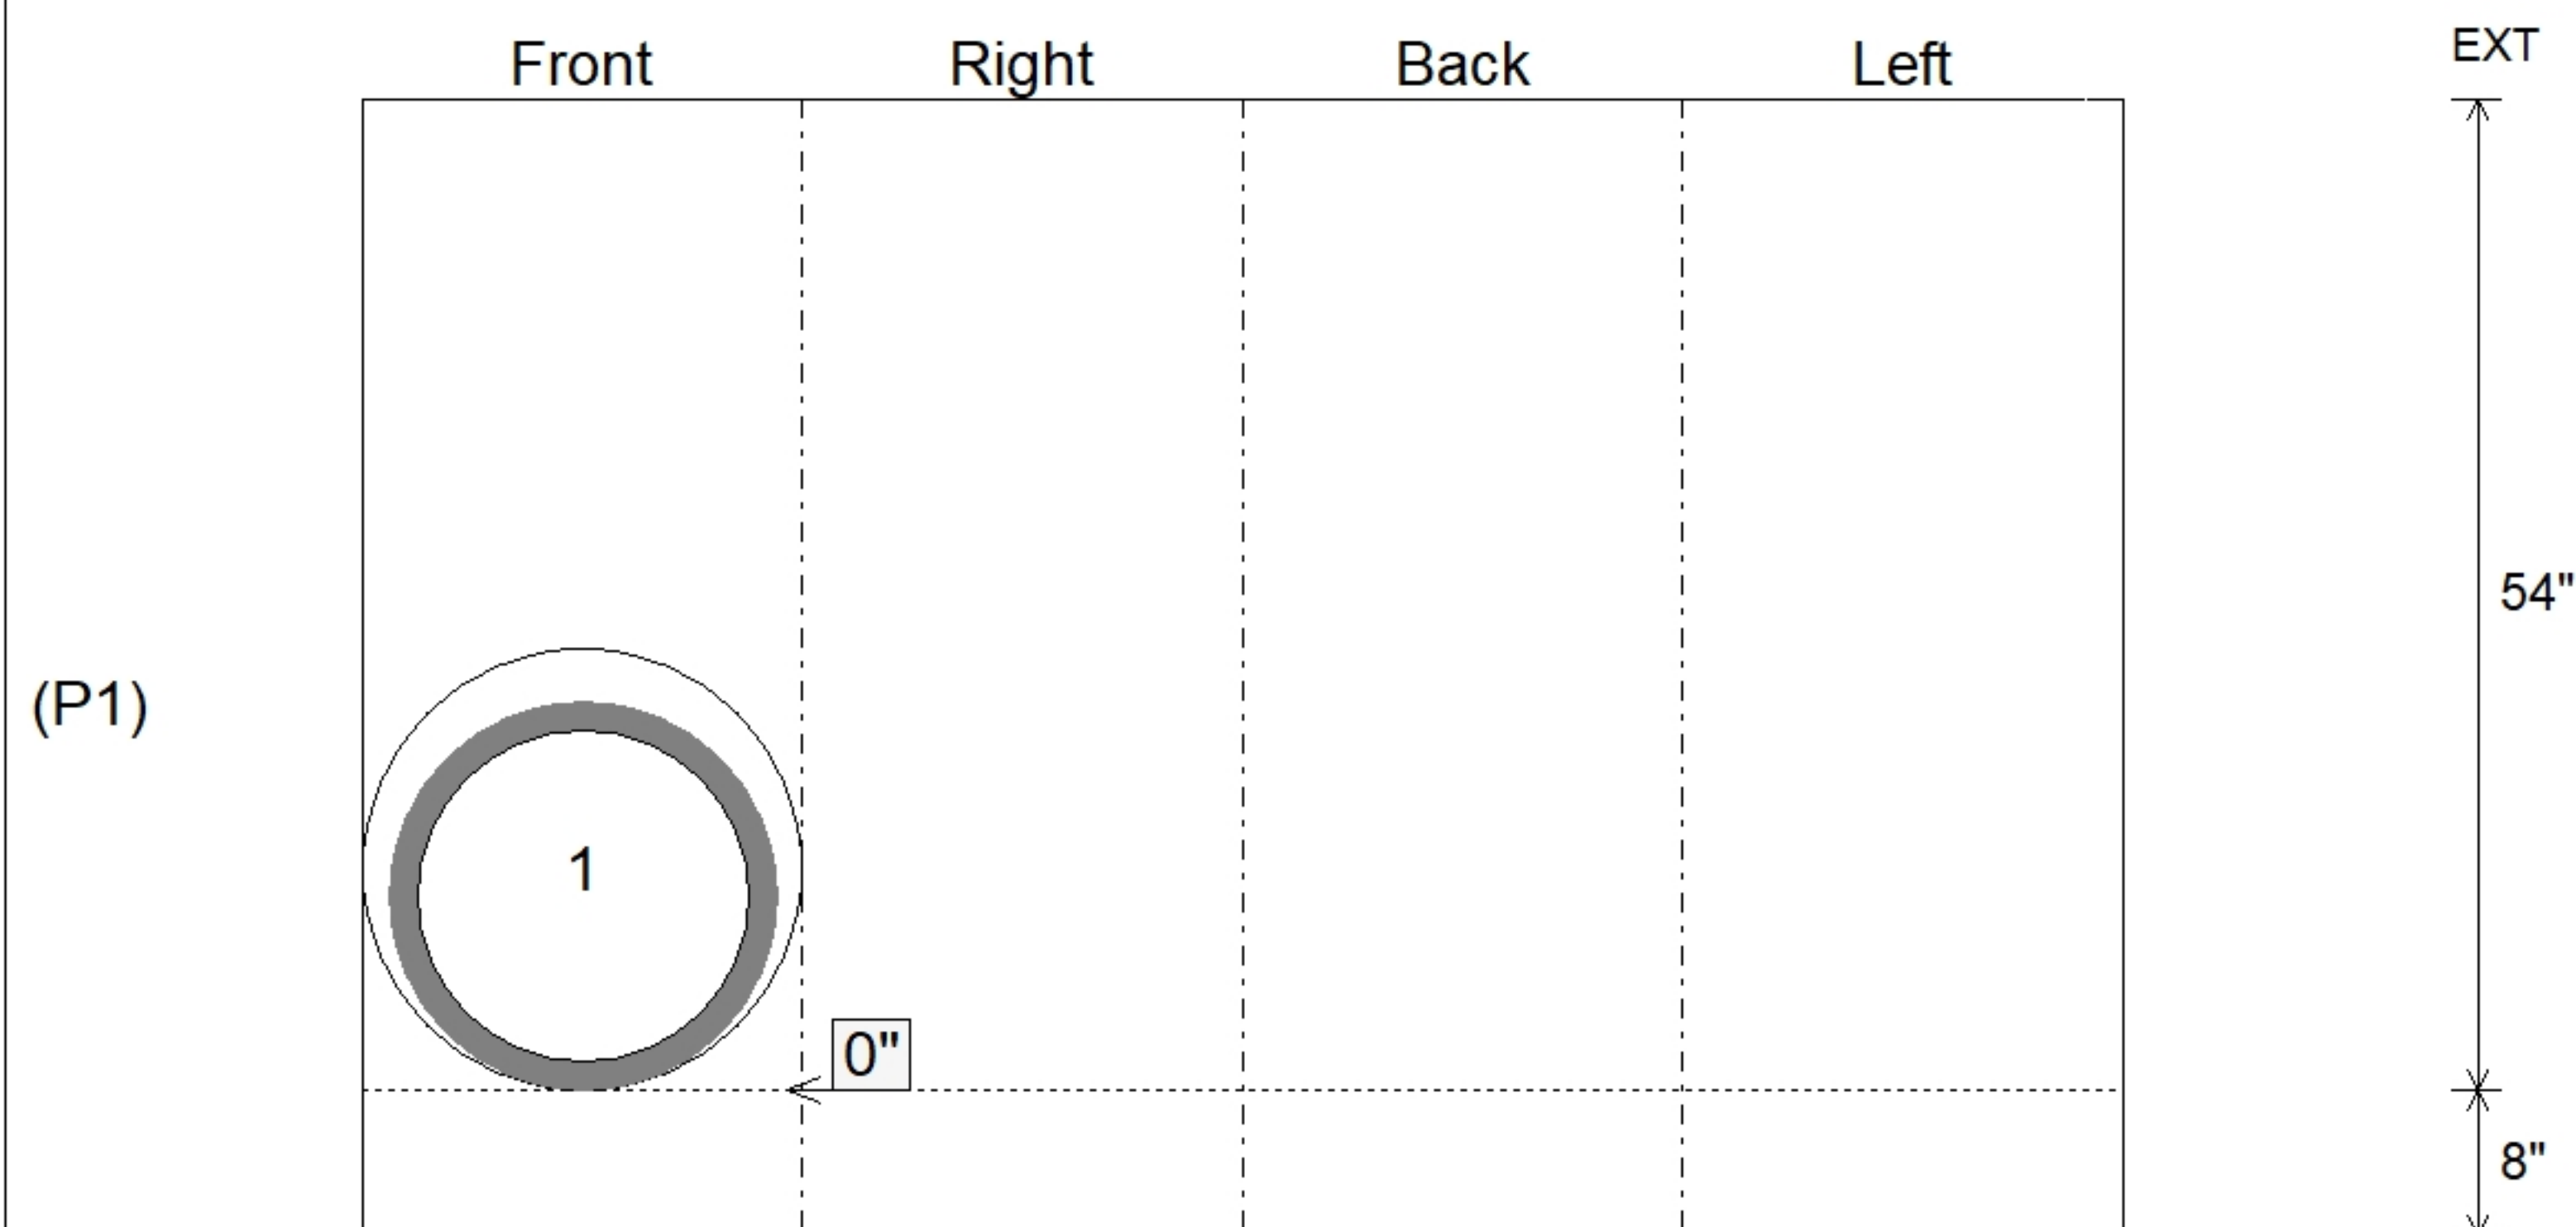

SUBMITTAL
APPROVED BY:
