


**Contractor: KY Earthworks**

Plant: 100



Slack: 1.505"

|                  |         |
|------------------|---------|
| Structure Total: | 4510 lb |
|------------------|---------|

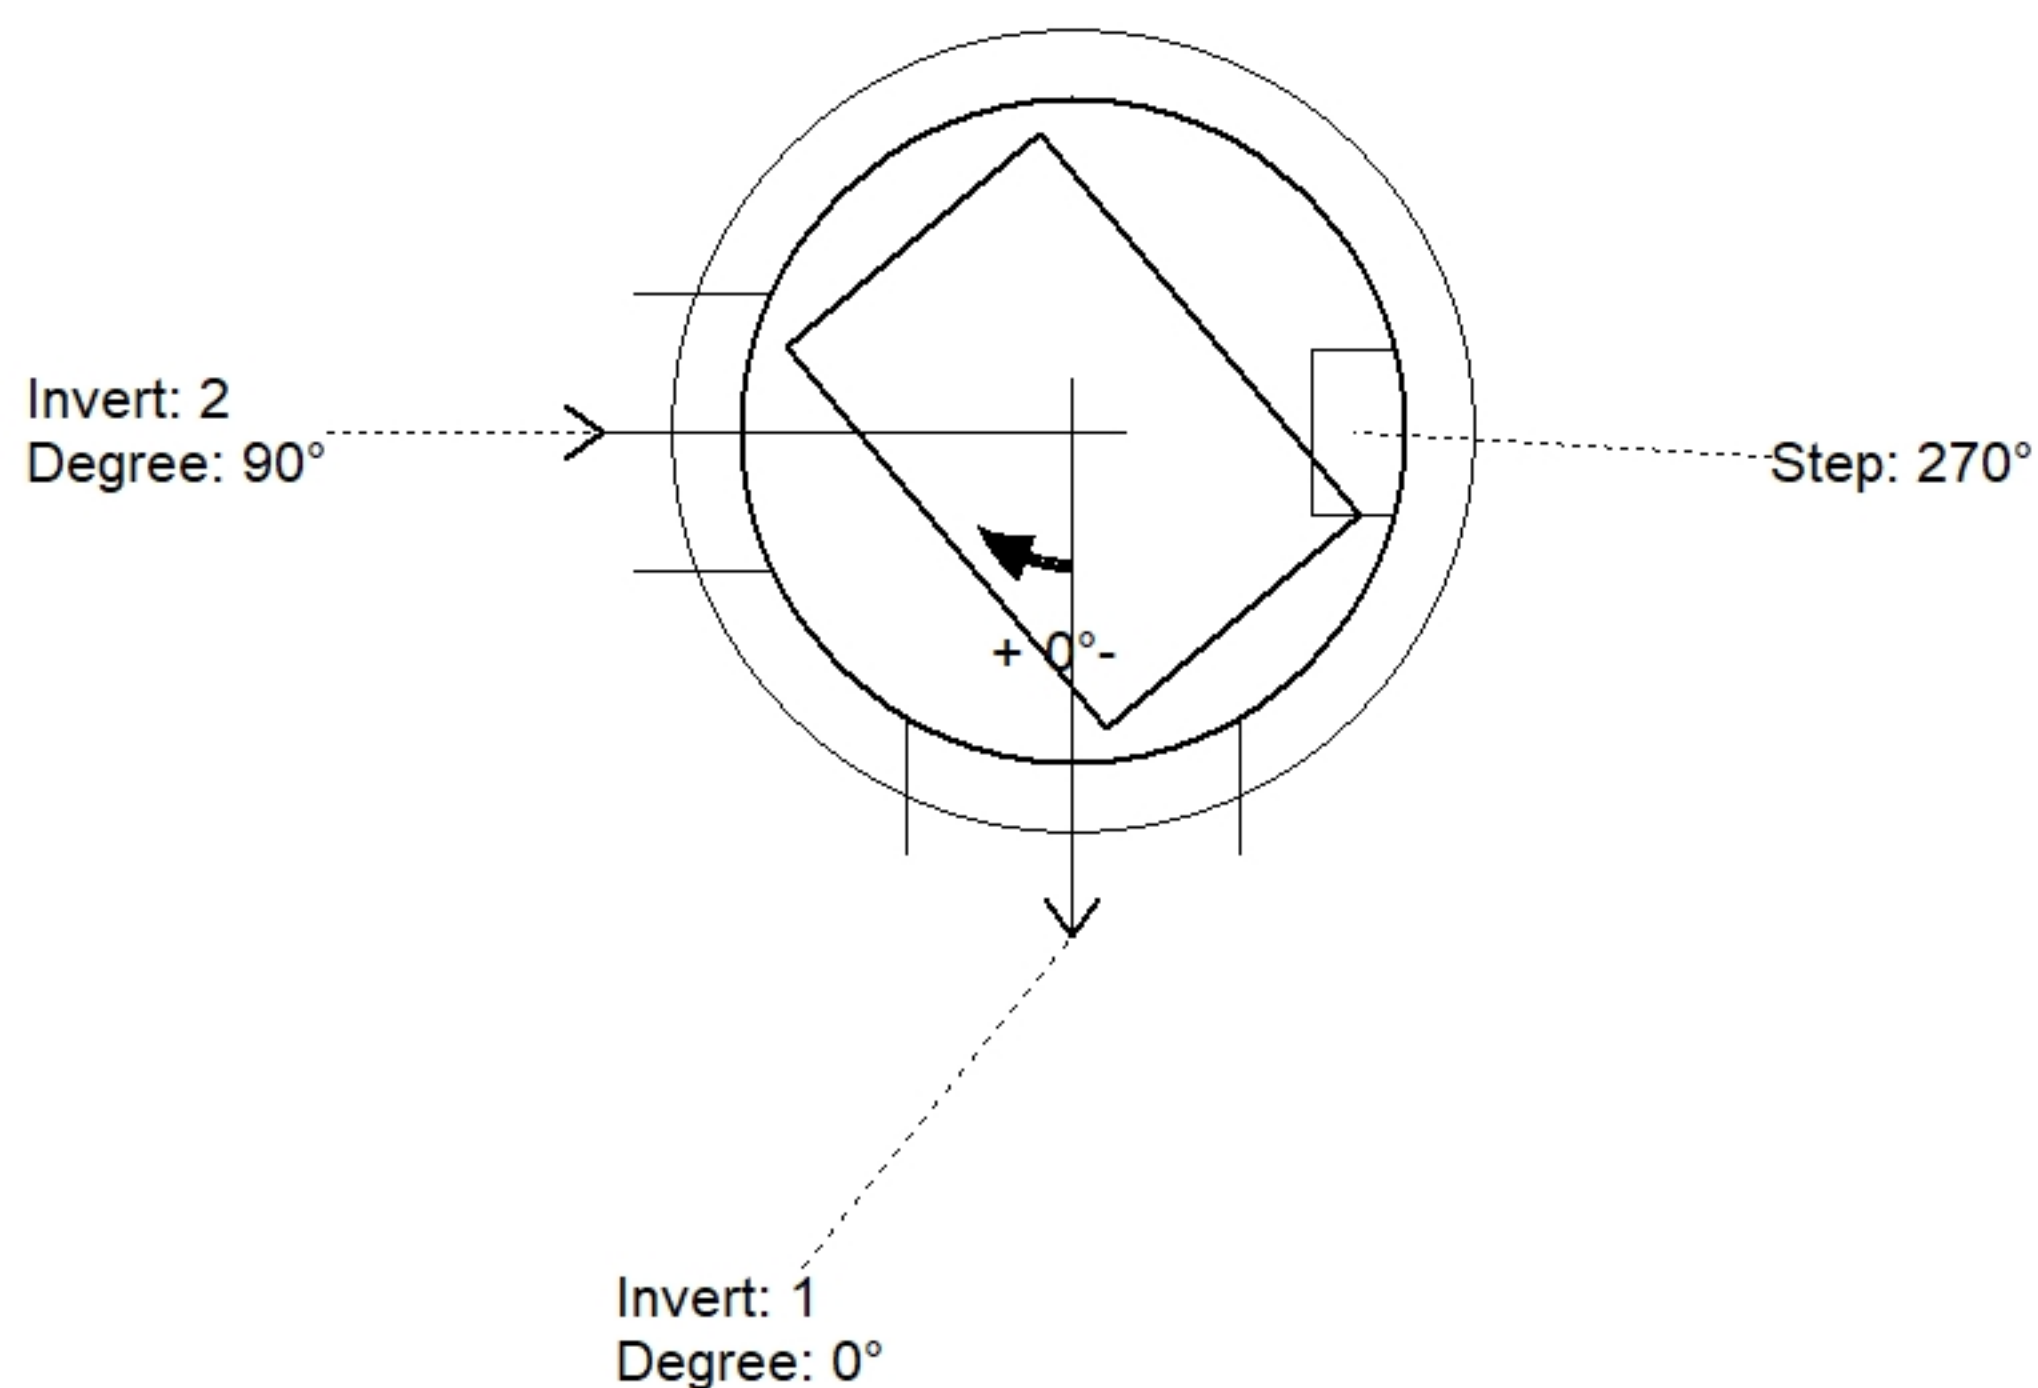


| Position | Elev    | Angle | Pipe     | Pipe OD | Hole | Connector | Up (⌵) | Ref |
|----------|---------|-------|----------|---------|------|-----------|--------|-----|
| Rim      | 934.66' |       |          |         |      |           |        |     |
| Reducer  |         |       |          |         |      |           |        |     |
| Invert 1 | 931.17' | 0°    | 18" HDPE | 21.2"   | 24"  | Hole 24   | 0.025" | P1  |
| Invert 2 | 931.17' | 90°   | 15" HDPE | 17.6"   | 20"  | Hole 20   | 0.325" | P1  |
| Invert 3 |         |       |          |         |      |           |        |     |
| Invert 4 |         |       |          |         |      |           |        |     |
| Invert 5 |         |       |          |         |      |           |        |     |
| Invert 6 |         |       |          |         |      |           |        |     |
| Invert 7 |         |       |          |         |      |           |        |     |
| Invert 8 |         |       |          |         |      |           |        |     |

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 7" - (P2)

48" - MH BASE Custom Ht - 29" - (P1)

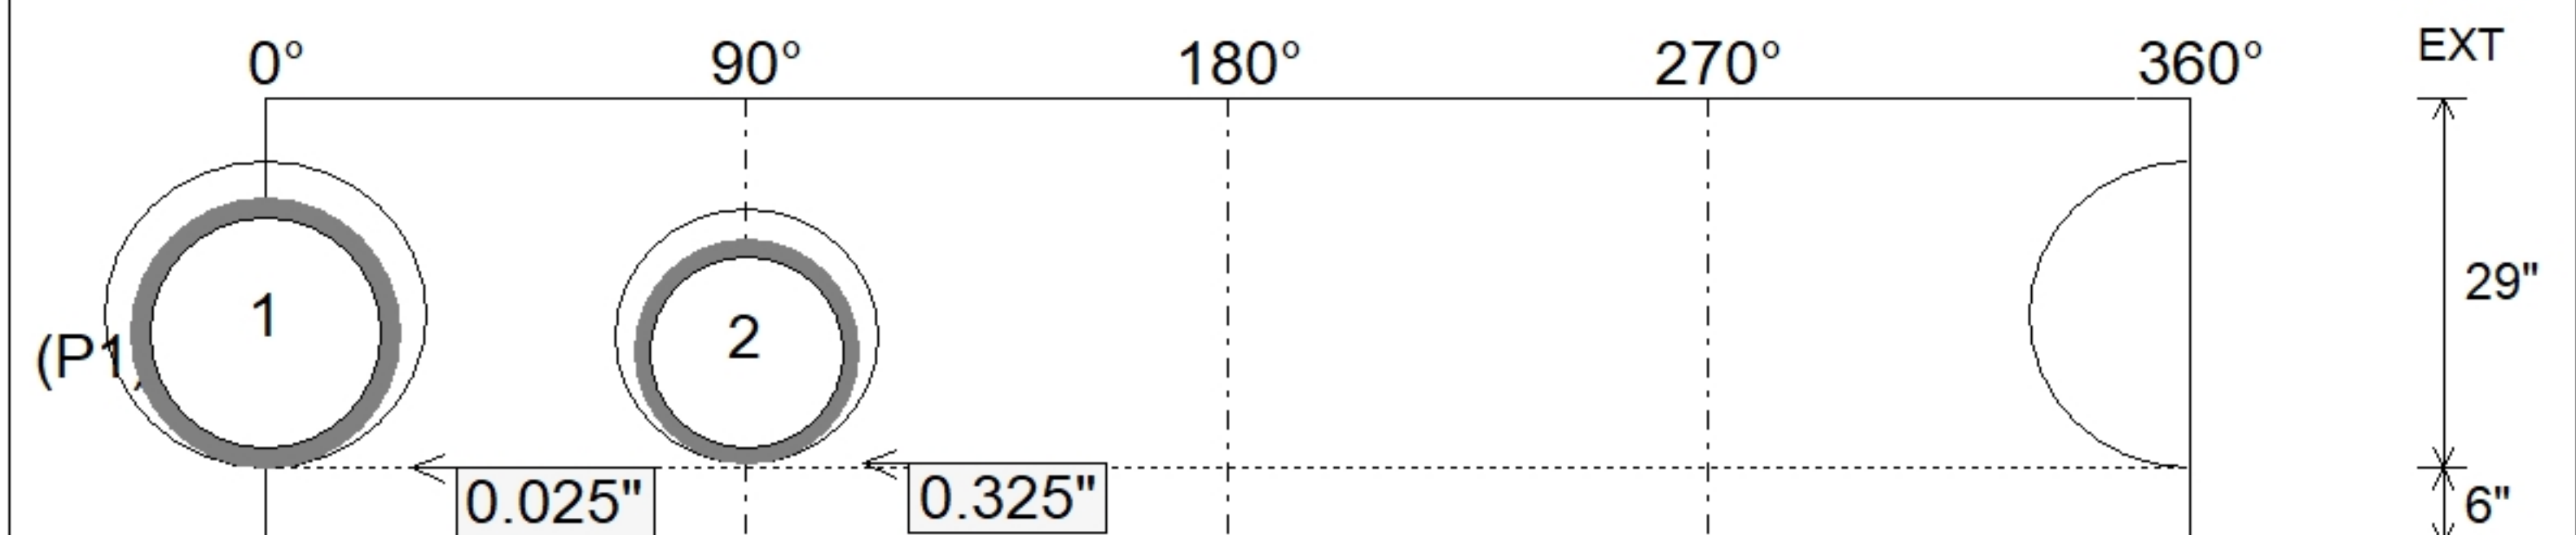

SUBMITTAL  
APPROVED BY:
