

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5.08'

Floor Height: 6"

Slack: 1.86"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


- P4) 24" x 24" - CASTING HEIGHT - 4"
- P3) 24" x 24" - GRADE RING - 3"
- P2) 48" - MH FLAT TOP w/24"x24" Hole - 12"
- P1) 48" - MH BASE - 42"
- 1) CASTING - HOE 280T F/G
- 1) 48" - Conseal CS-102 1.00"
- 2) 24" x 24" - Conseal CS-102 1.00"
- 2) Hole - 30
- 3) MH Step ML-10-TDS-NCR - 10"

0 lb
258 lb
1500 lb
3632 lb
182 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 5572 lb

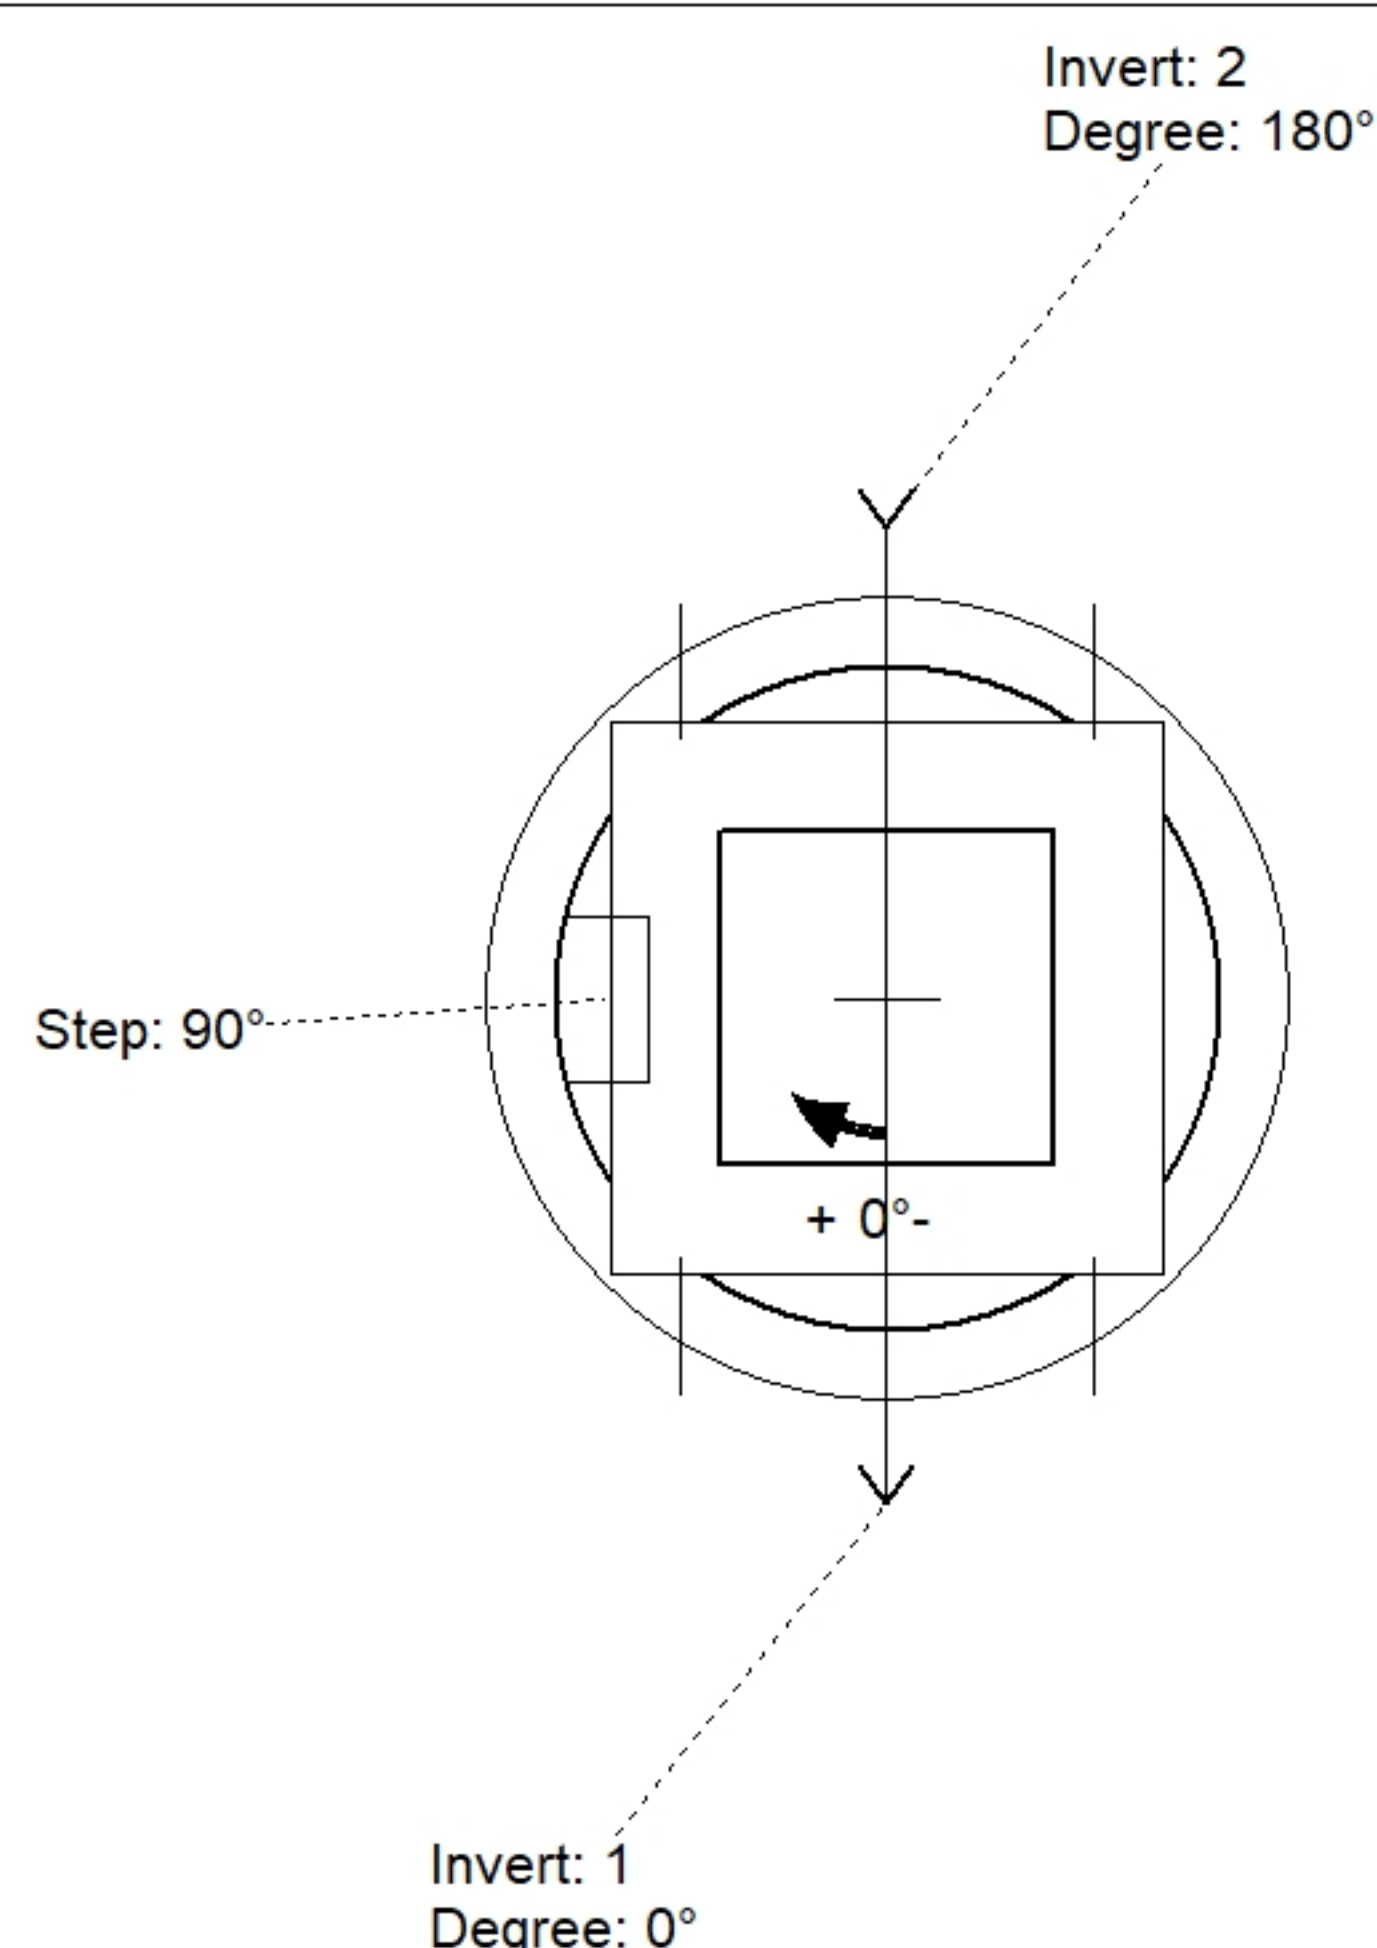

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	931.15'							
Reducer								
Invert 1	926.07'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	926.07'	180°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

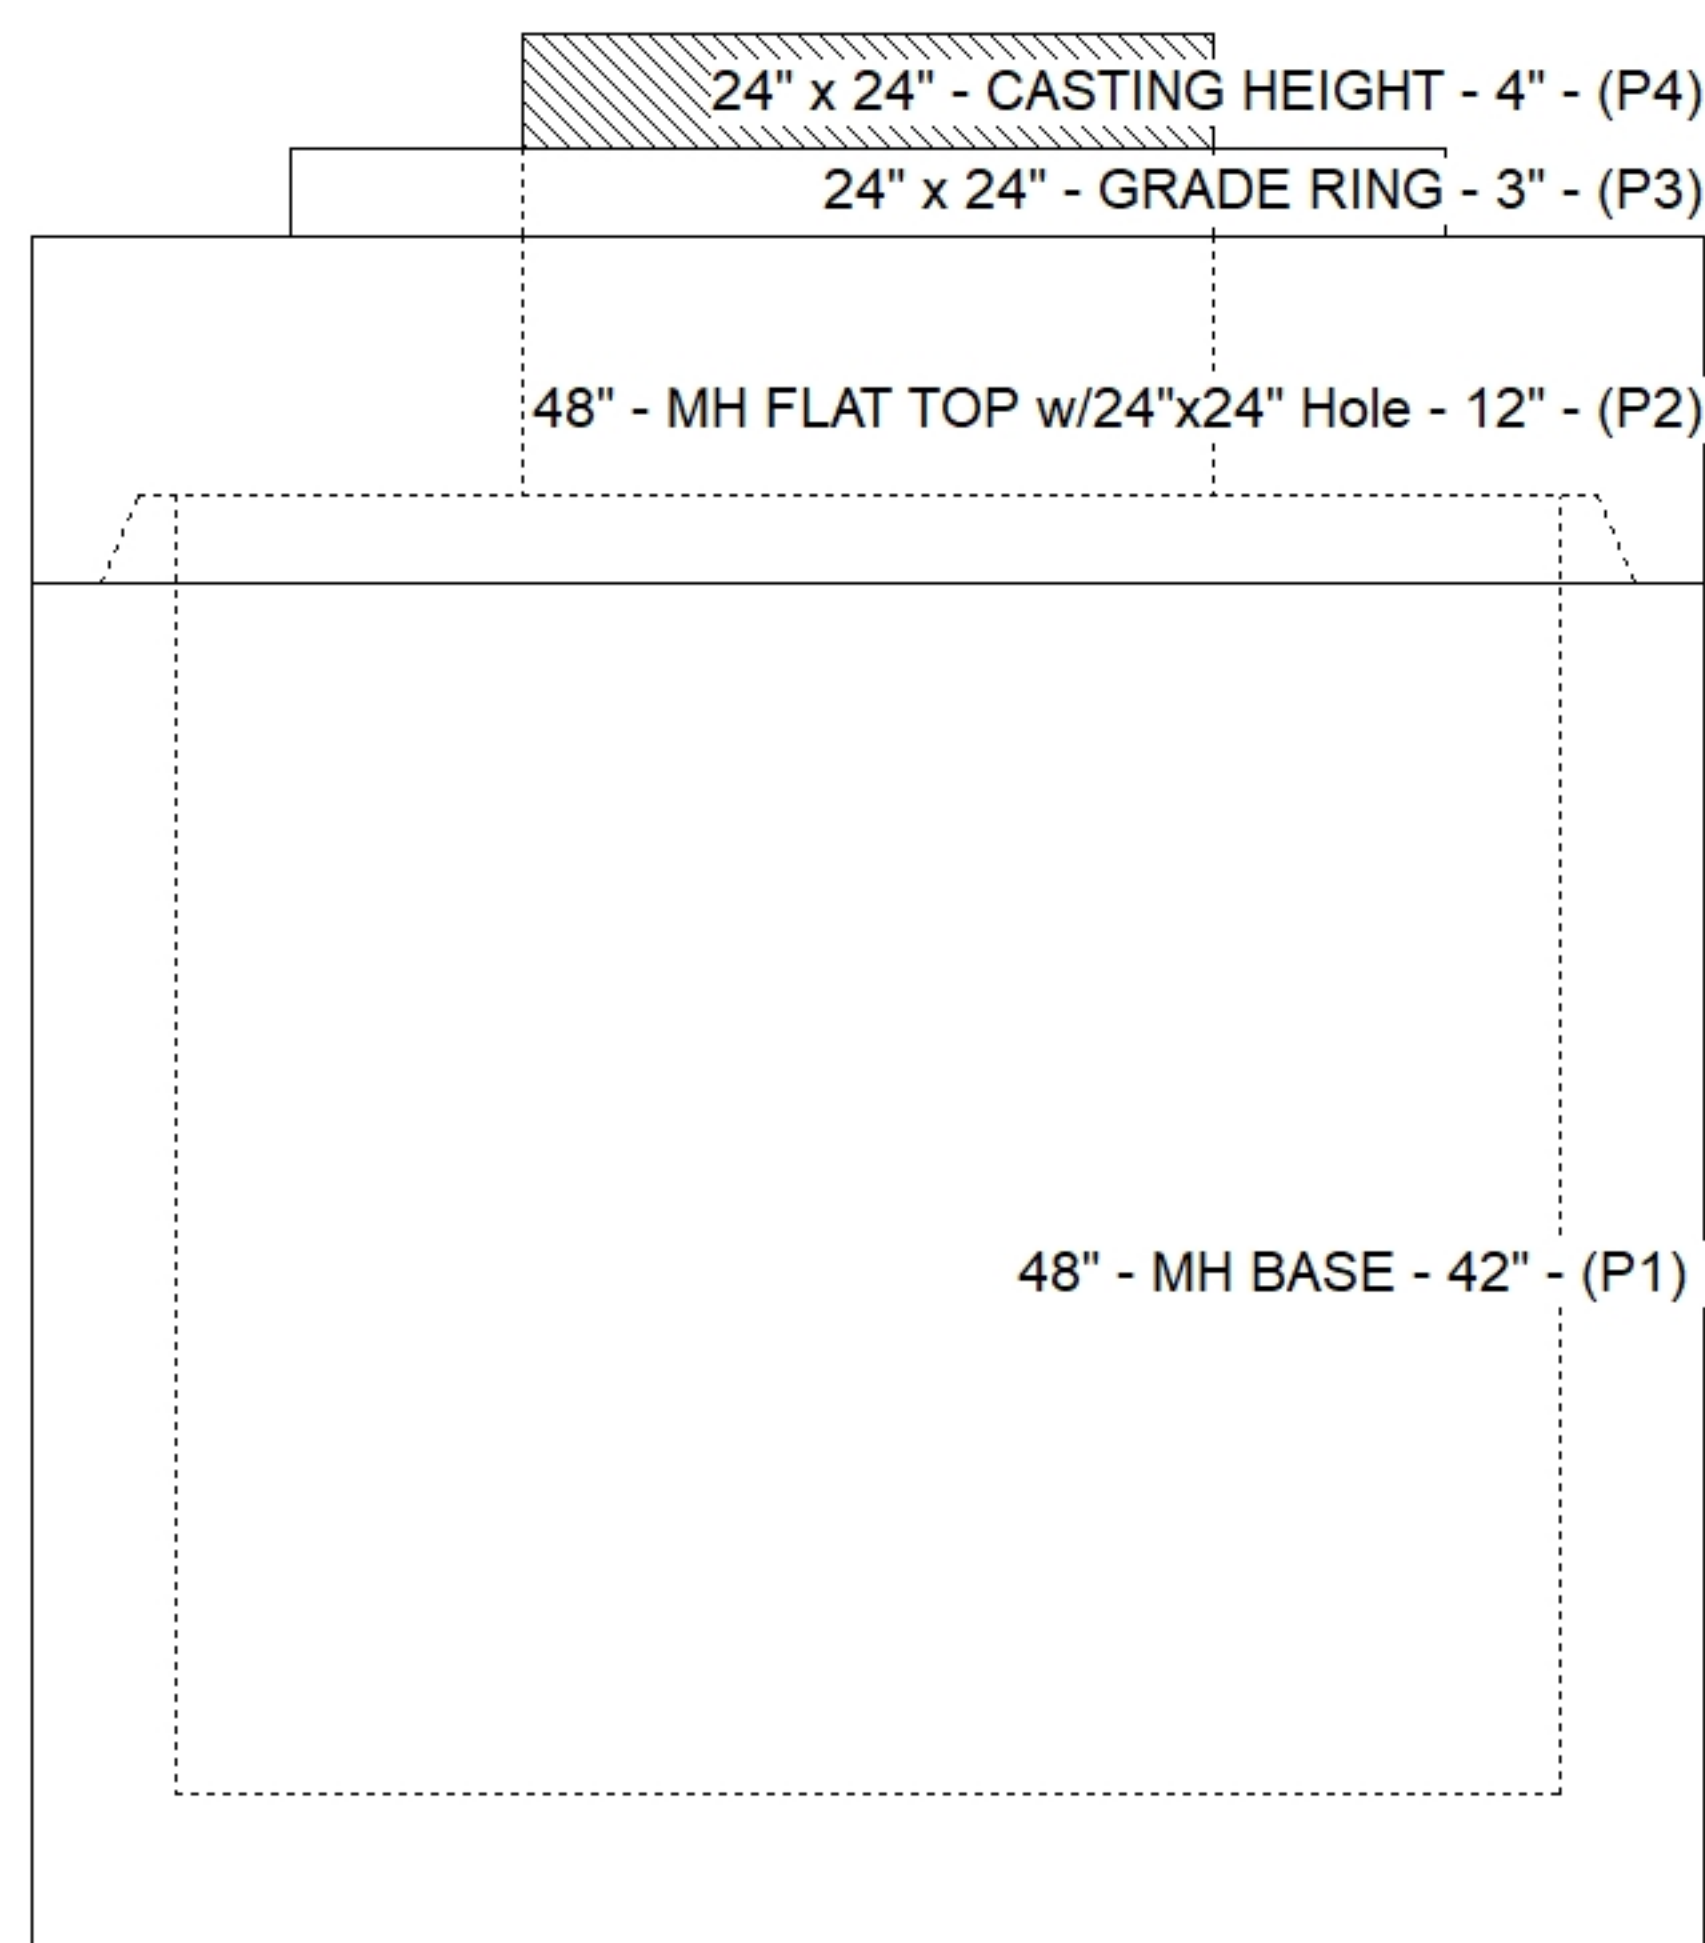

Default - Interior Dimensions

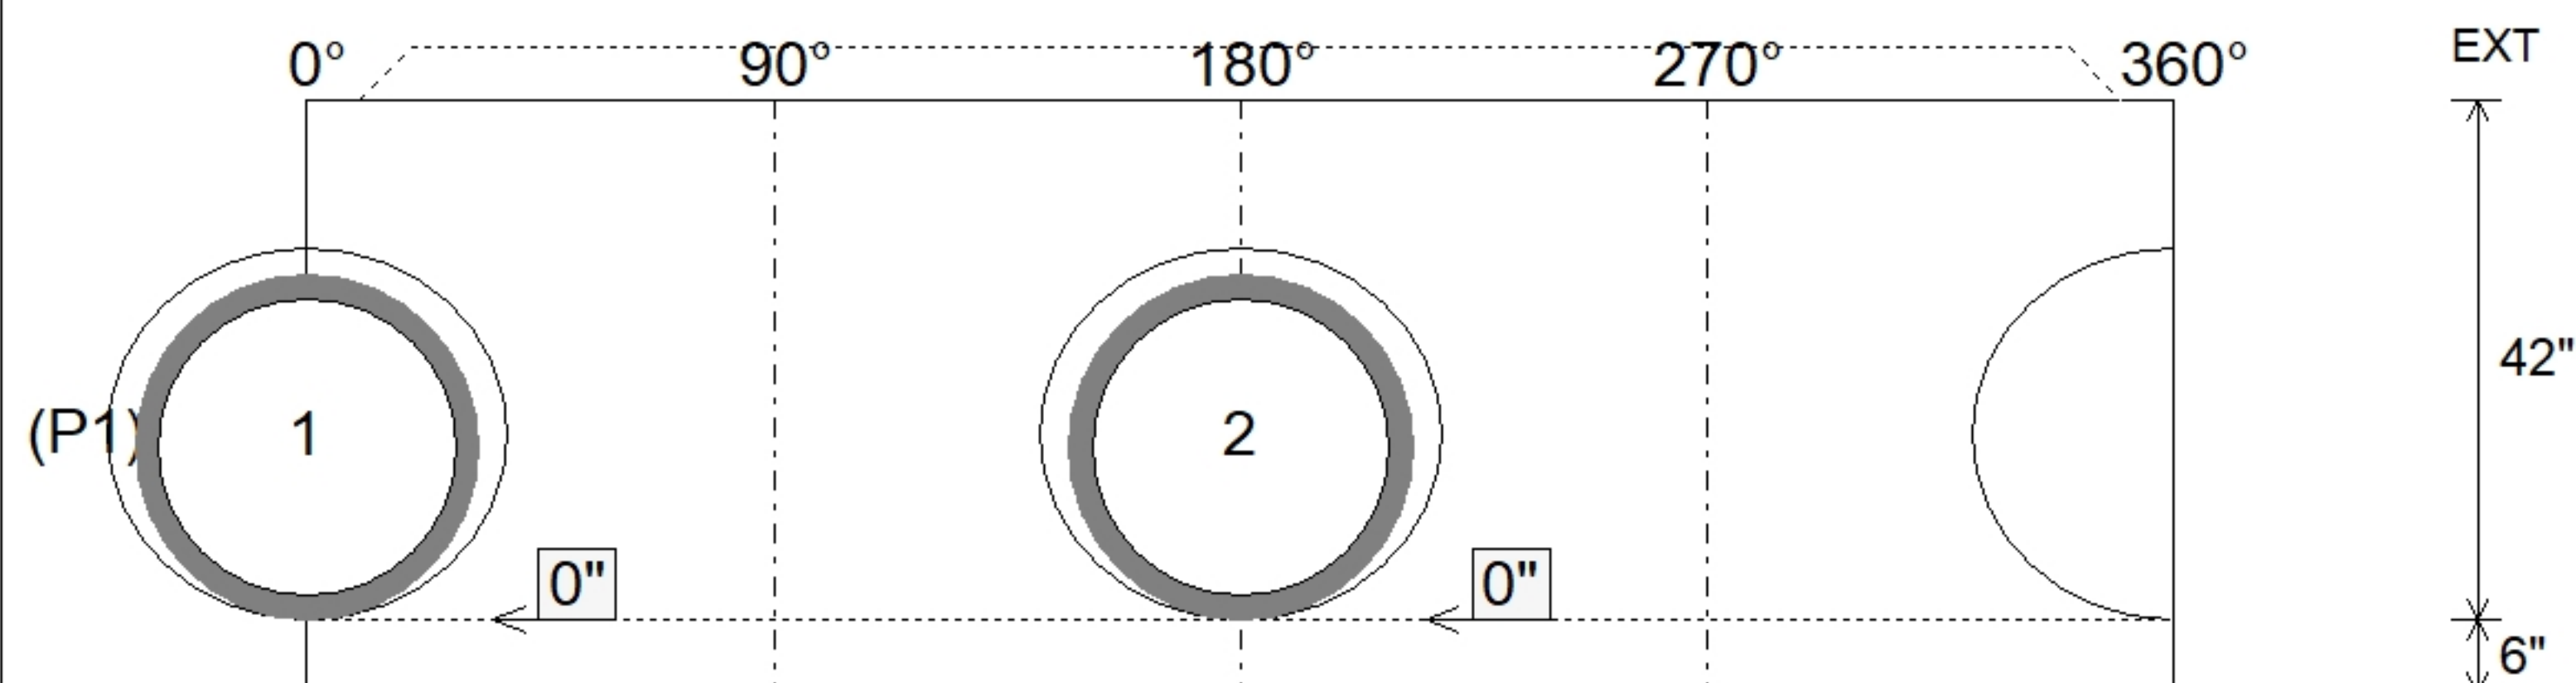

Submittal Drawing
9/29/2026 8:26:02 AM

SUBMITTAL
APPROVED BY:
