




Job Name: 26-1822 - Project Versailles Job Location: Versailles, KY Contractor: KY Earthworks					Plant: 100 9/24/2026 11:26:59 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: C8 ST-YD										
P1 MH048BA42		MH BASE Custom Ht T/n								
P4) 24" x 24" - CASTING HEIGHT - 4" P3) 24" x 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 42" 1) CASTING - HOE 280T F/G 1) 48" - Conseal CS-102 1.00" 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 24 3) MH Step ML-10-TDS-NCR - 10"					0 lb 258 lb 1500 lb 3870 lb 182 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5810 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 934.24' Rim to Invert: 5.08' Slack: 1.56" Sump: 1.6" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	929.16'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 2	929.16'	180°	91.125"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

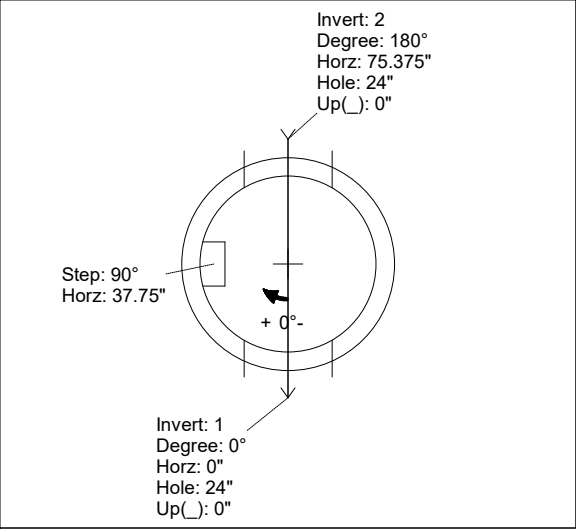


UPSIDE-DOWN VIEW (int. dimensions)

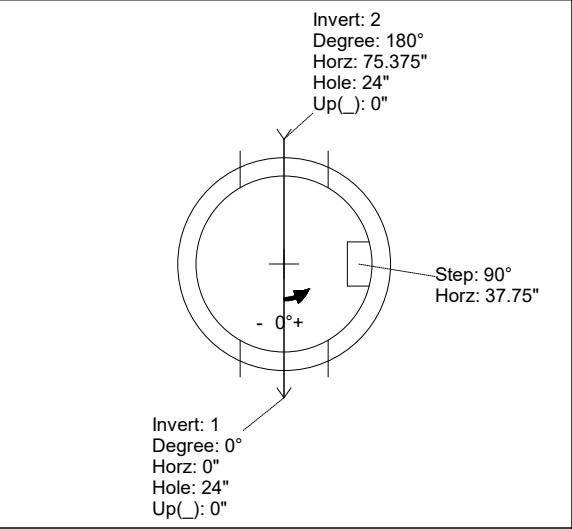

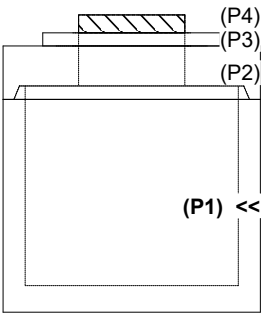

INSIDE WALL DIMENSIONS

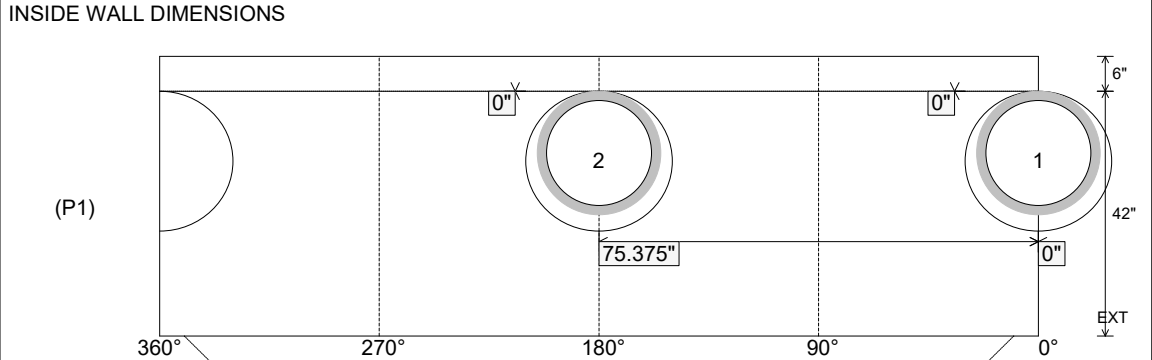

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 42" Height (Ext): 48"	Weight (Net): 3870 lb Volume (Net): 0.99cu.yd
----------------------------------	---------------------------------	--	--	--
