

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 4.94'

Floor Height: 6"

Slack: 1.905"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE Custom Ht - 41"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 24
1) Hole - 14
3) MH Step ML-10-TDS-NCR - 10"

0 lb
1300 lb
3932 lb
442 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 5674 lb

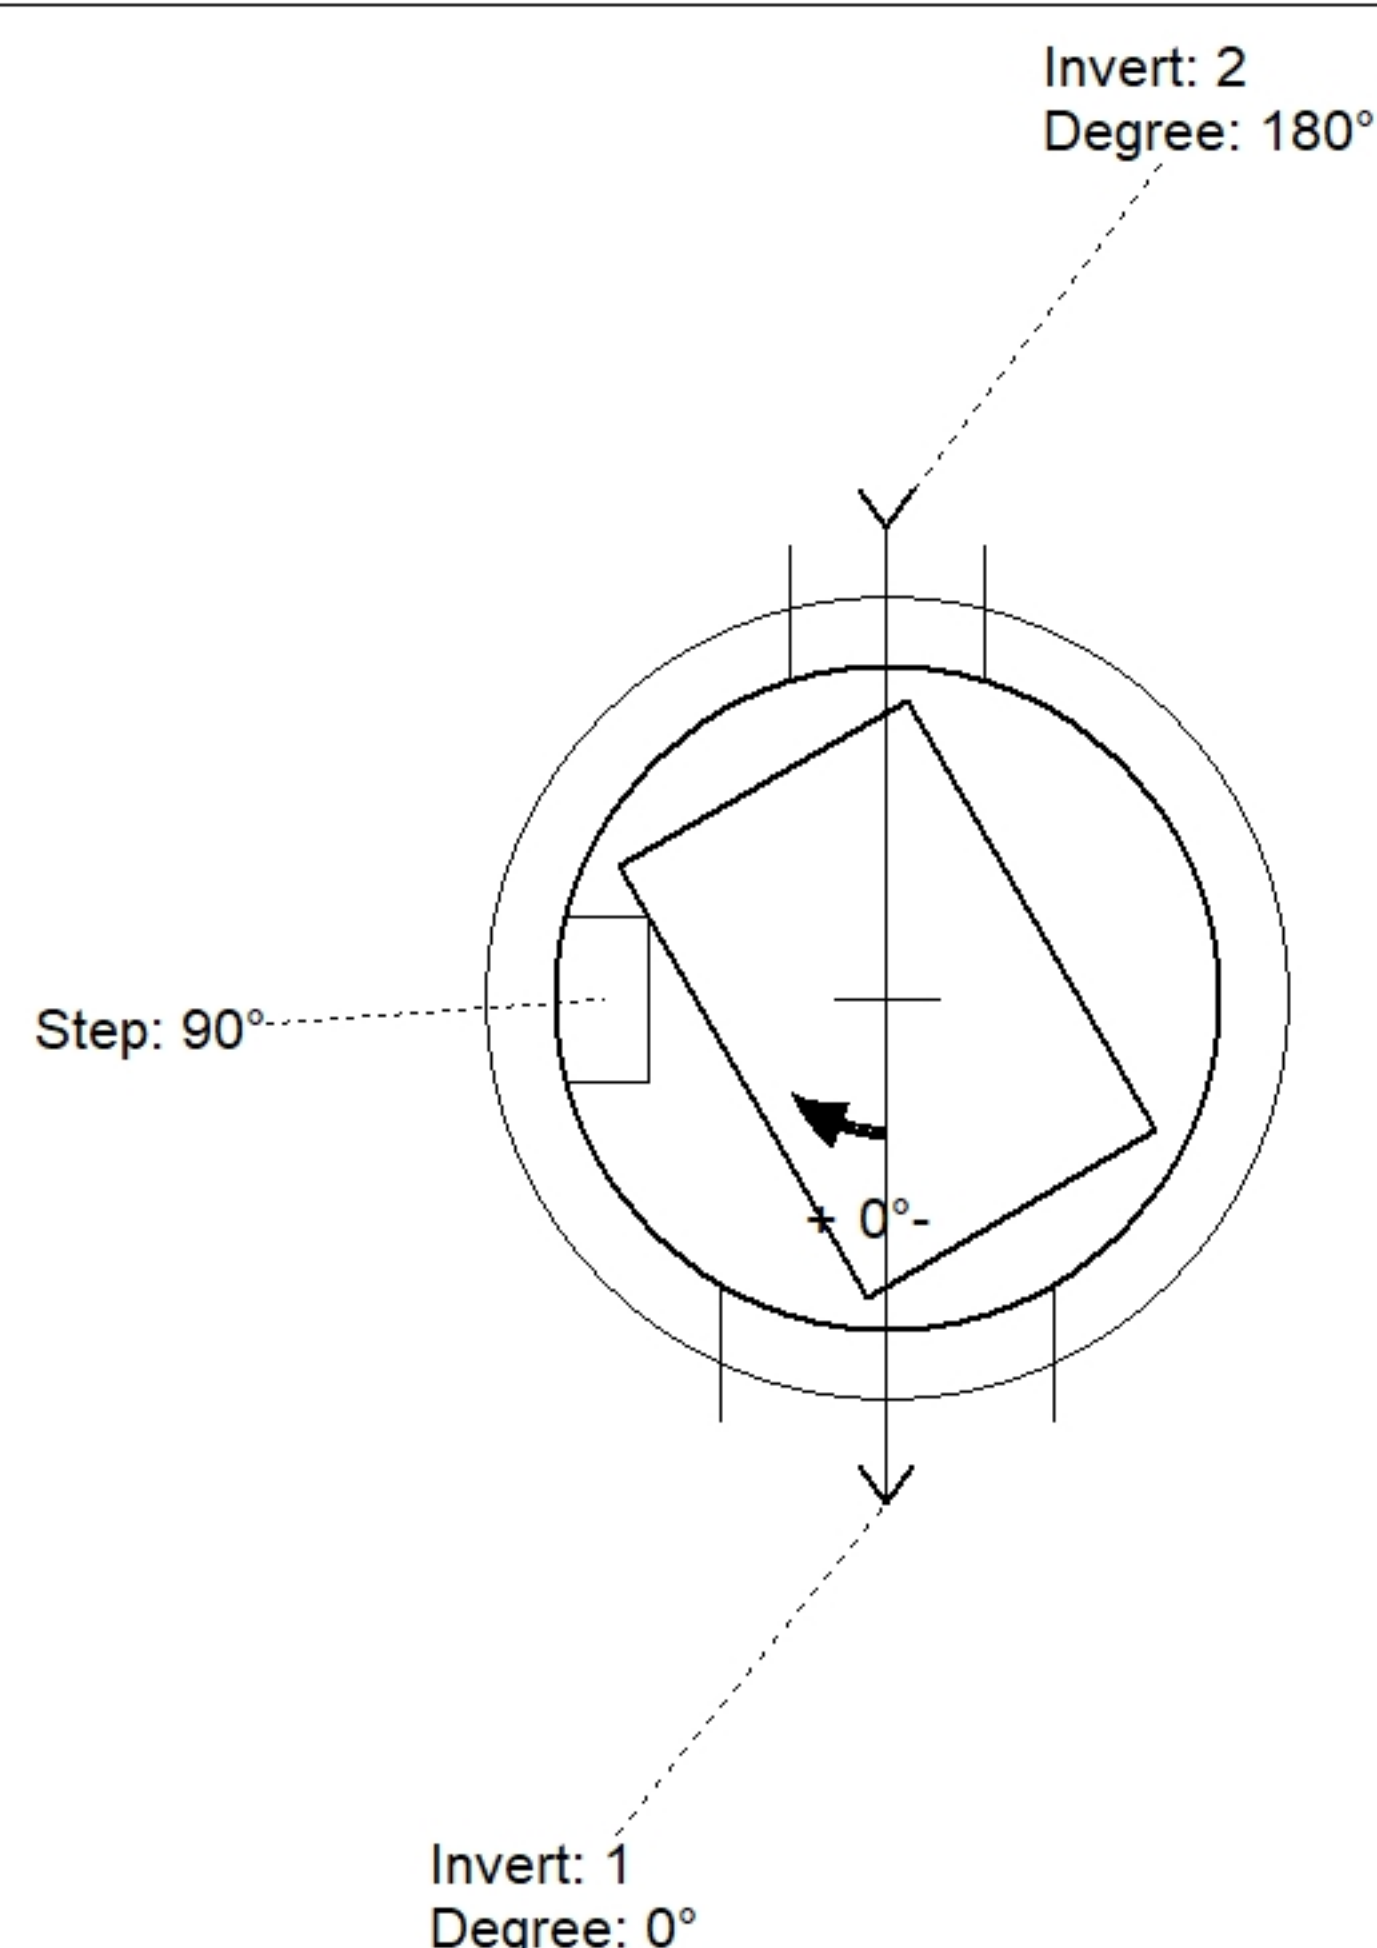

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	935.6'							
Reducer								
Invert 1	930.66'	0°	18" HDPE	21.2"	24"	Hole 24	0.025"	P1
Invert 2	930.76'	180°	10" HDPE	11.4"	14"	Hole 14	2.125"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

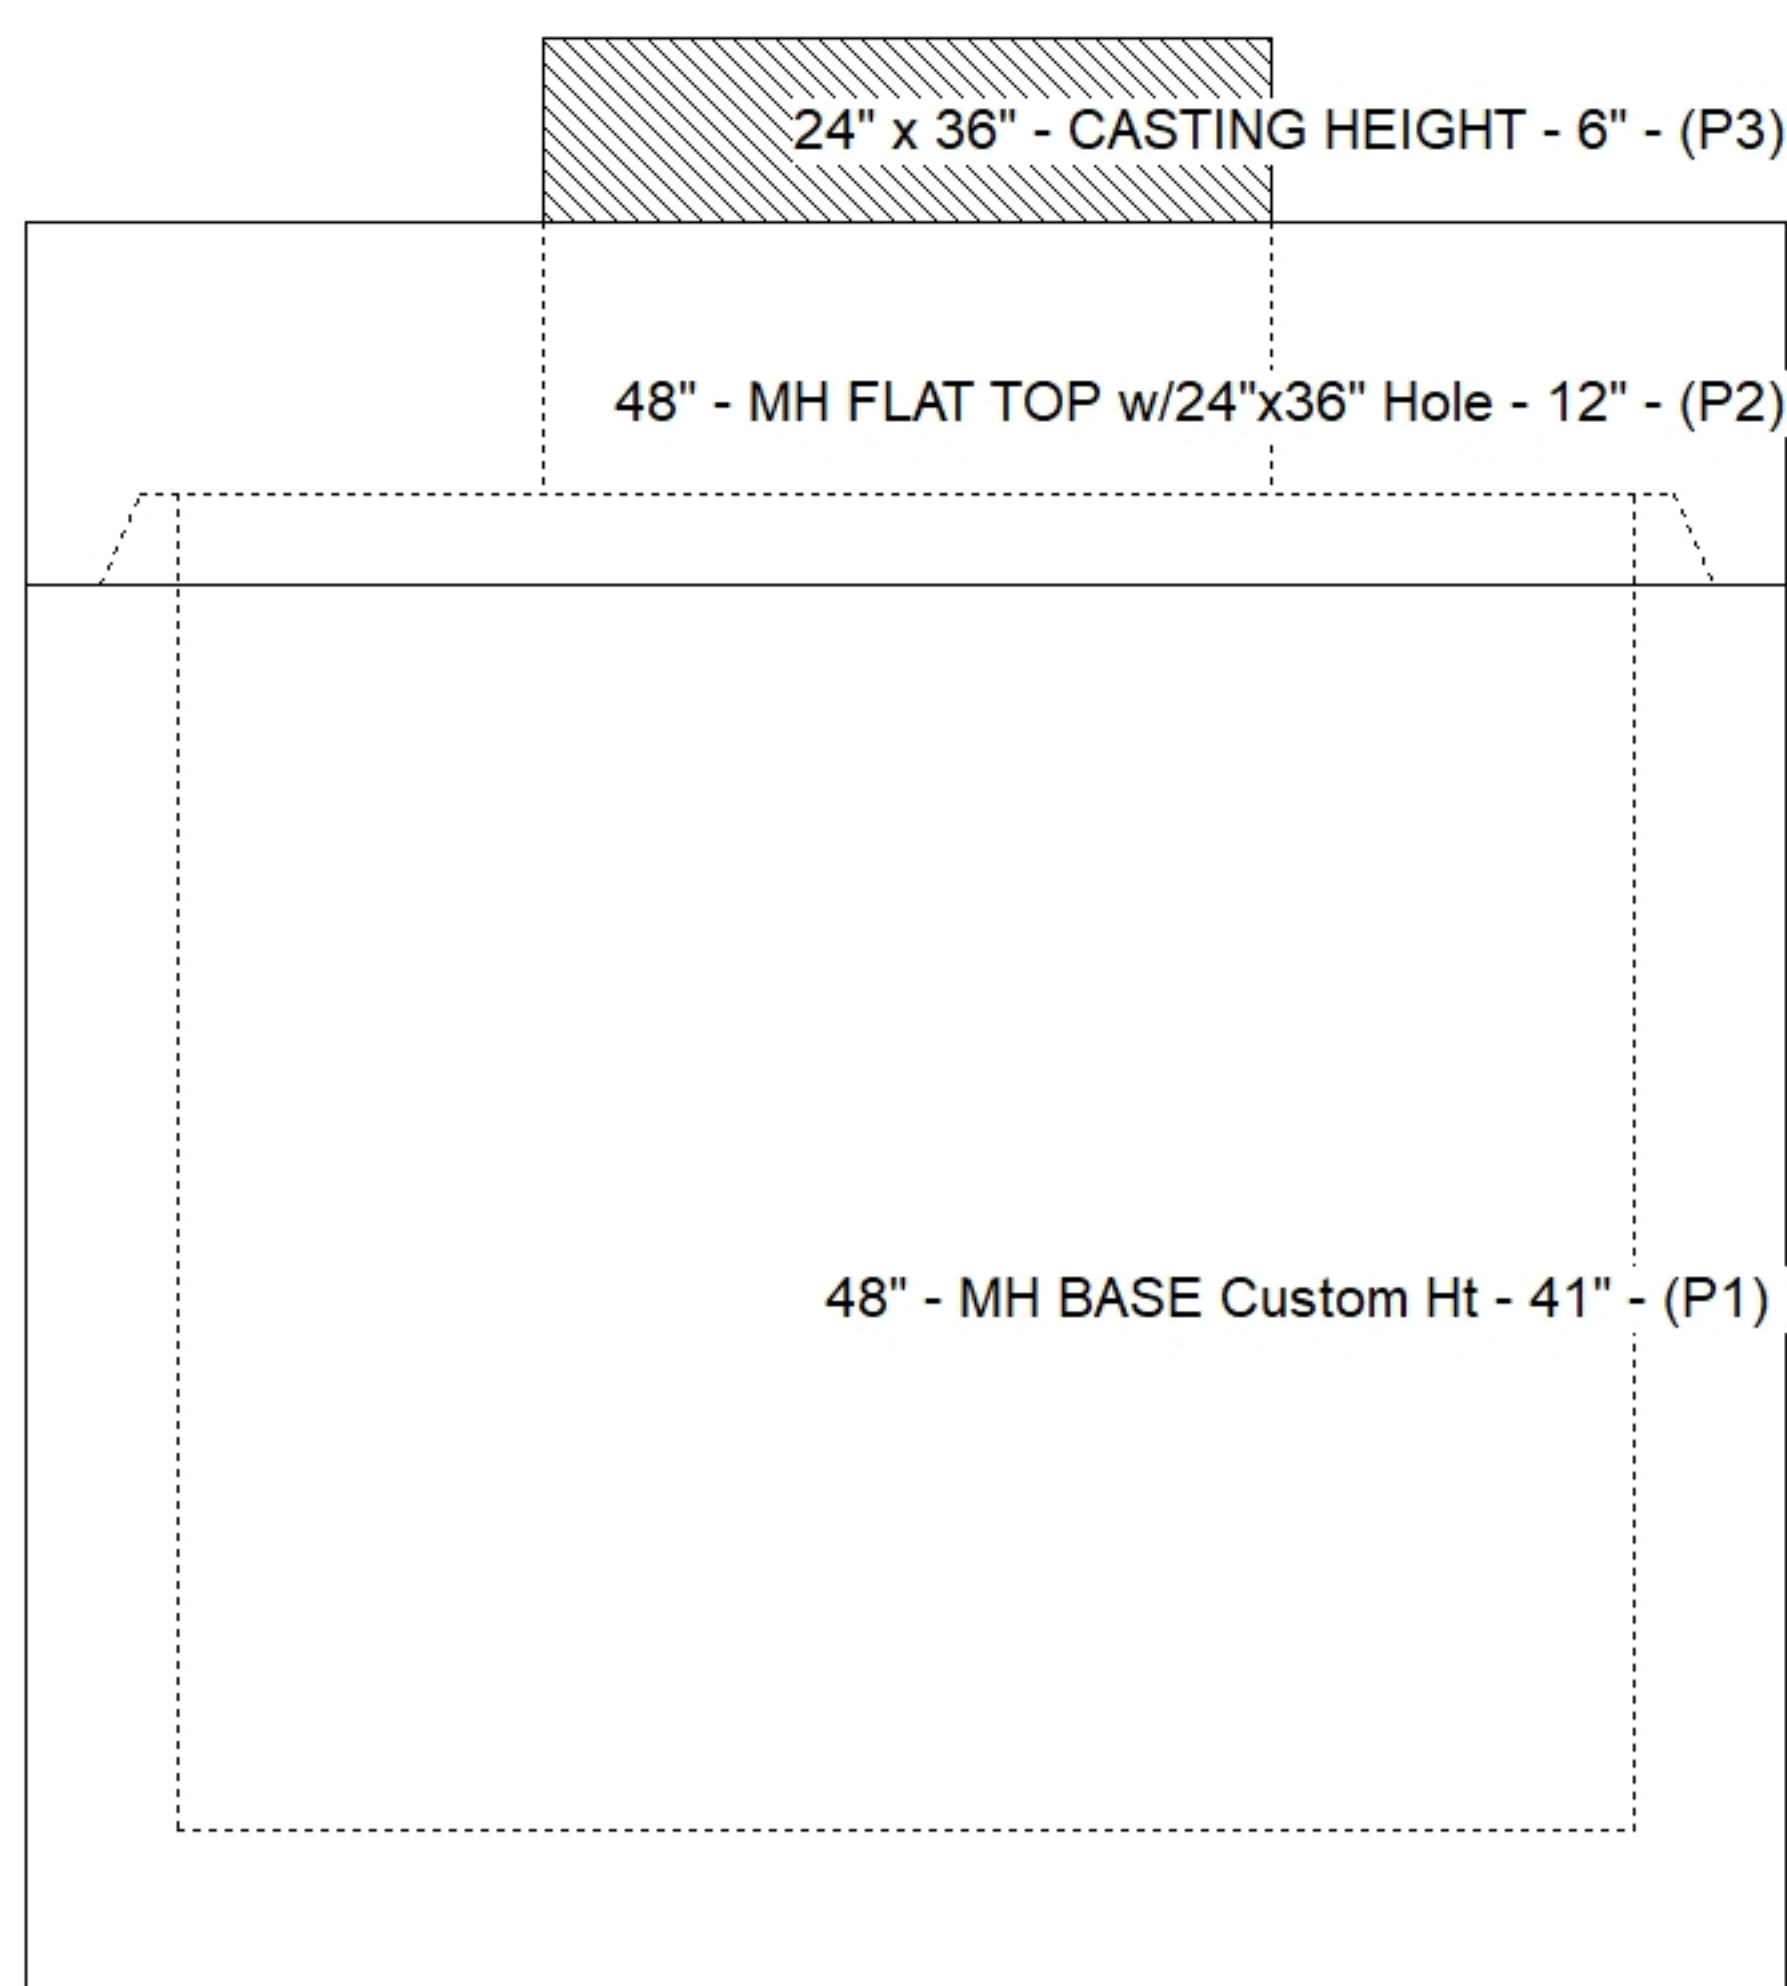

Default - Interior Dimensions

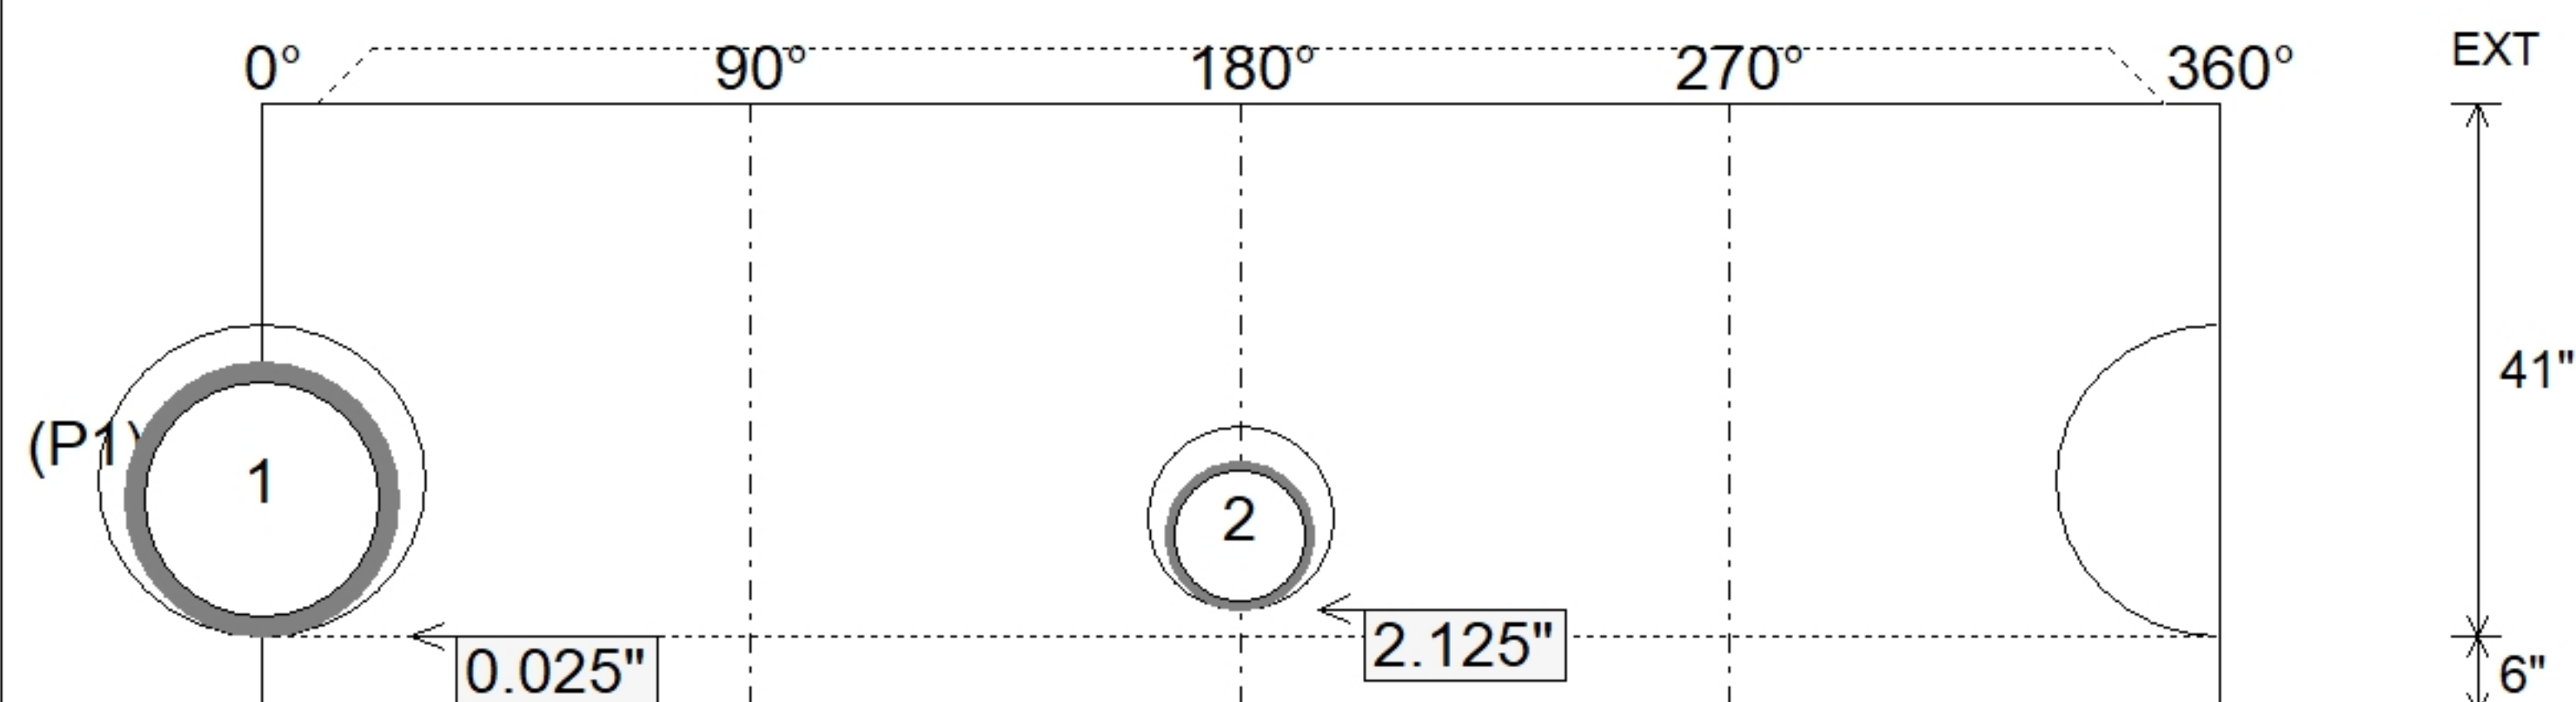

Submittal Drawing
9/29/2026 8:25:42 AM

SUBMITTAL
APPROVED BY:
