



Contractor: KY Earthworks

Plant: 100



Slack: 1.78"

Structure Total:	13900 lb
------------------	----------

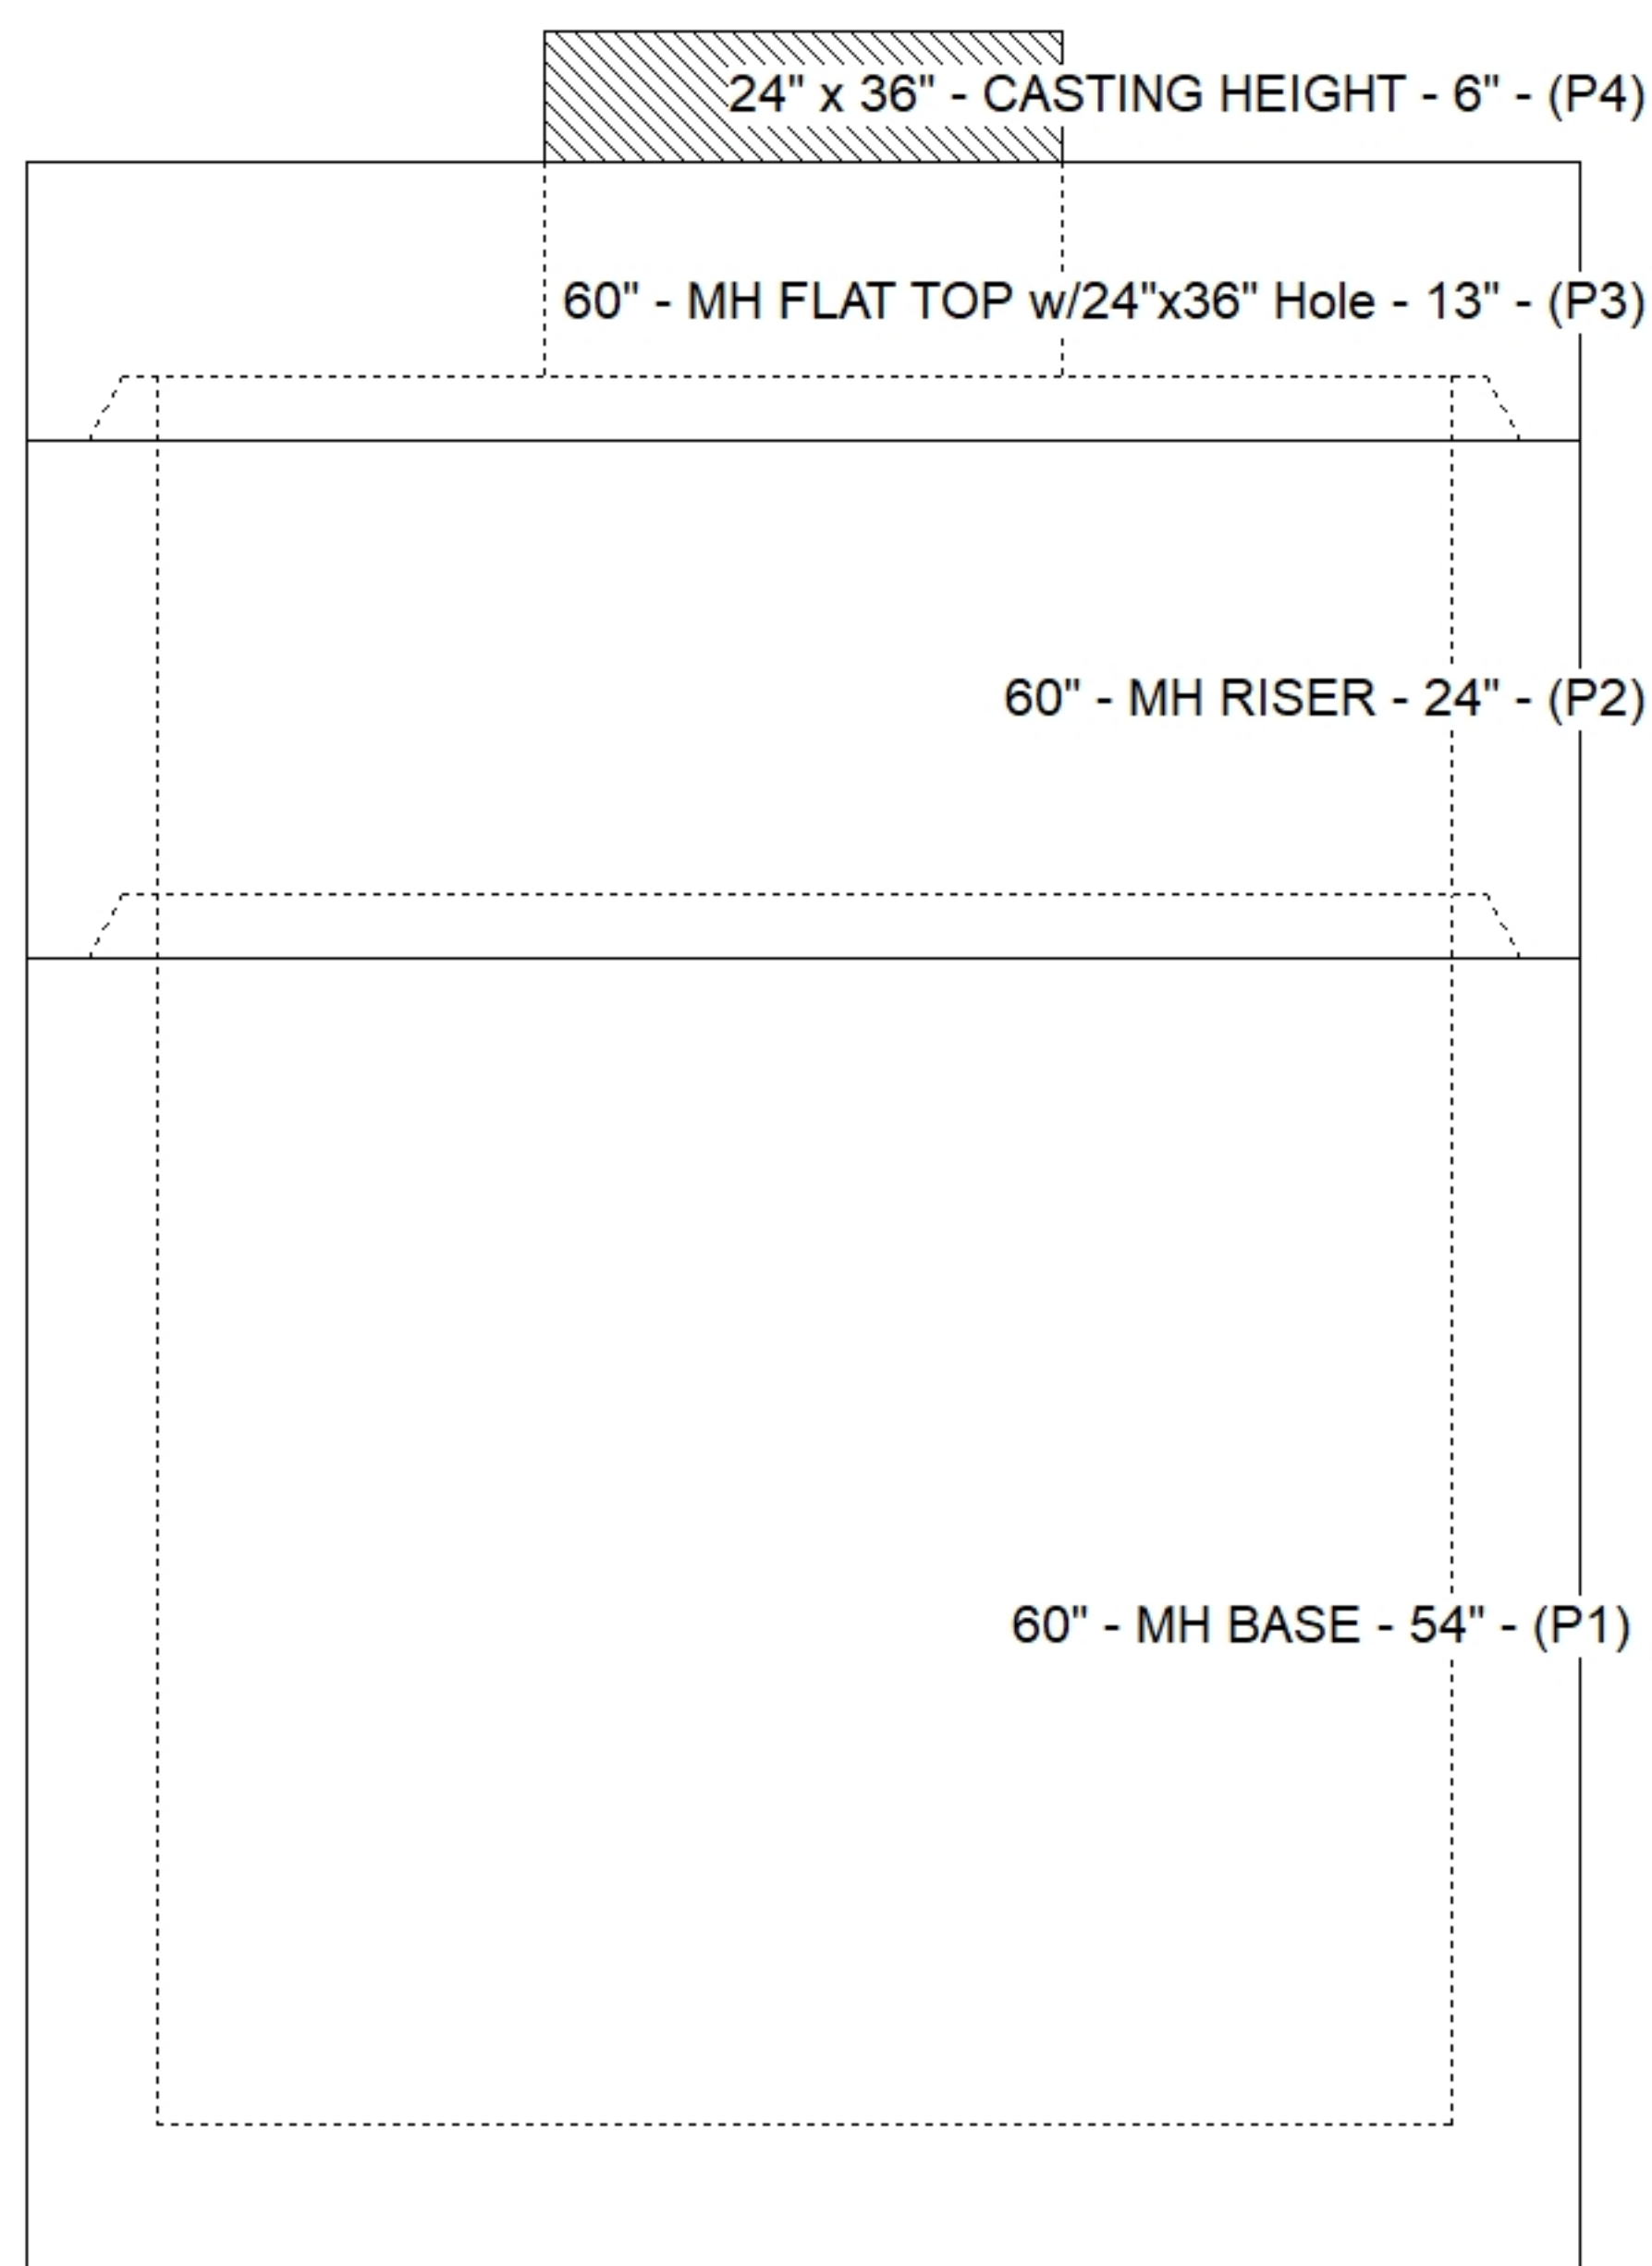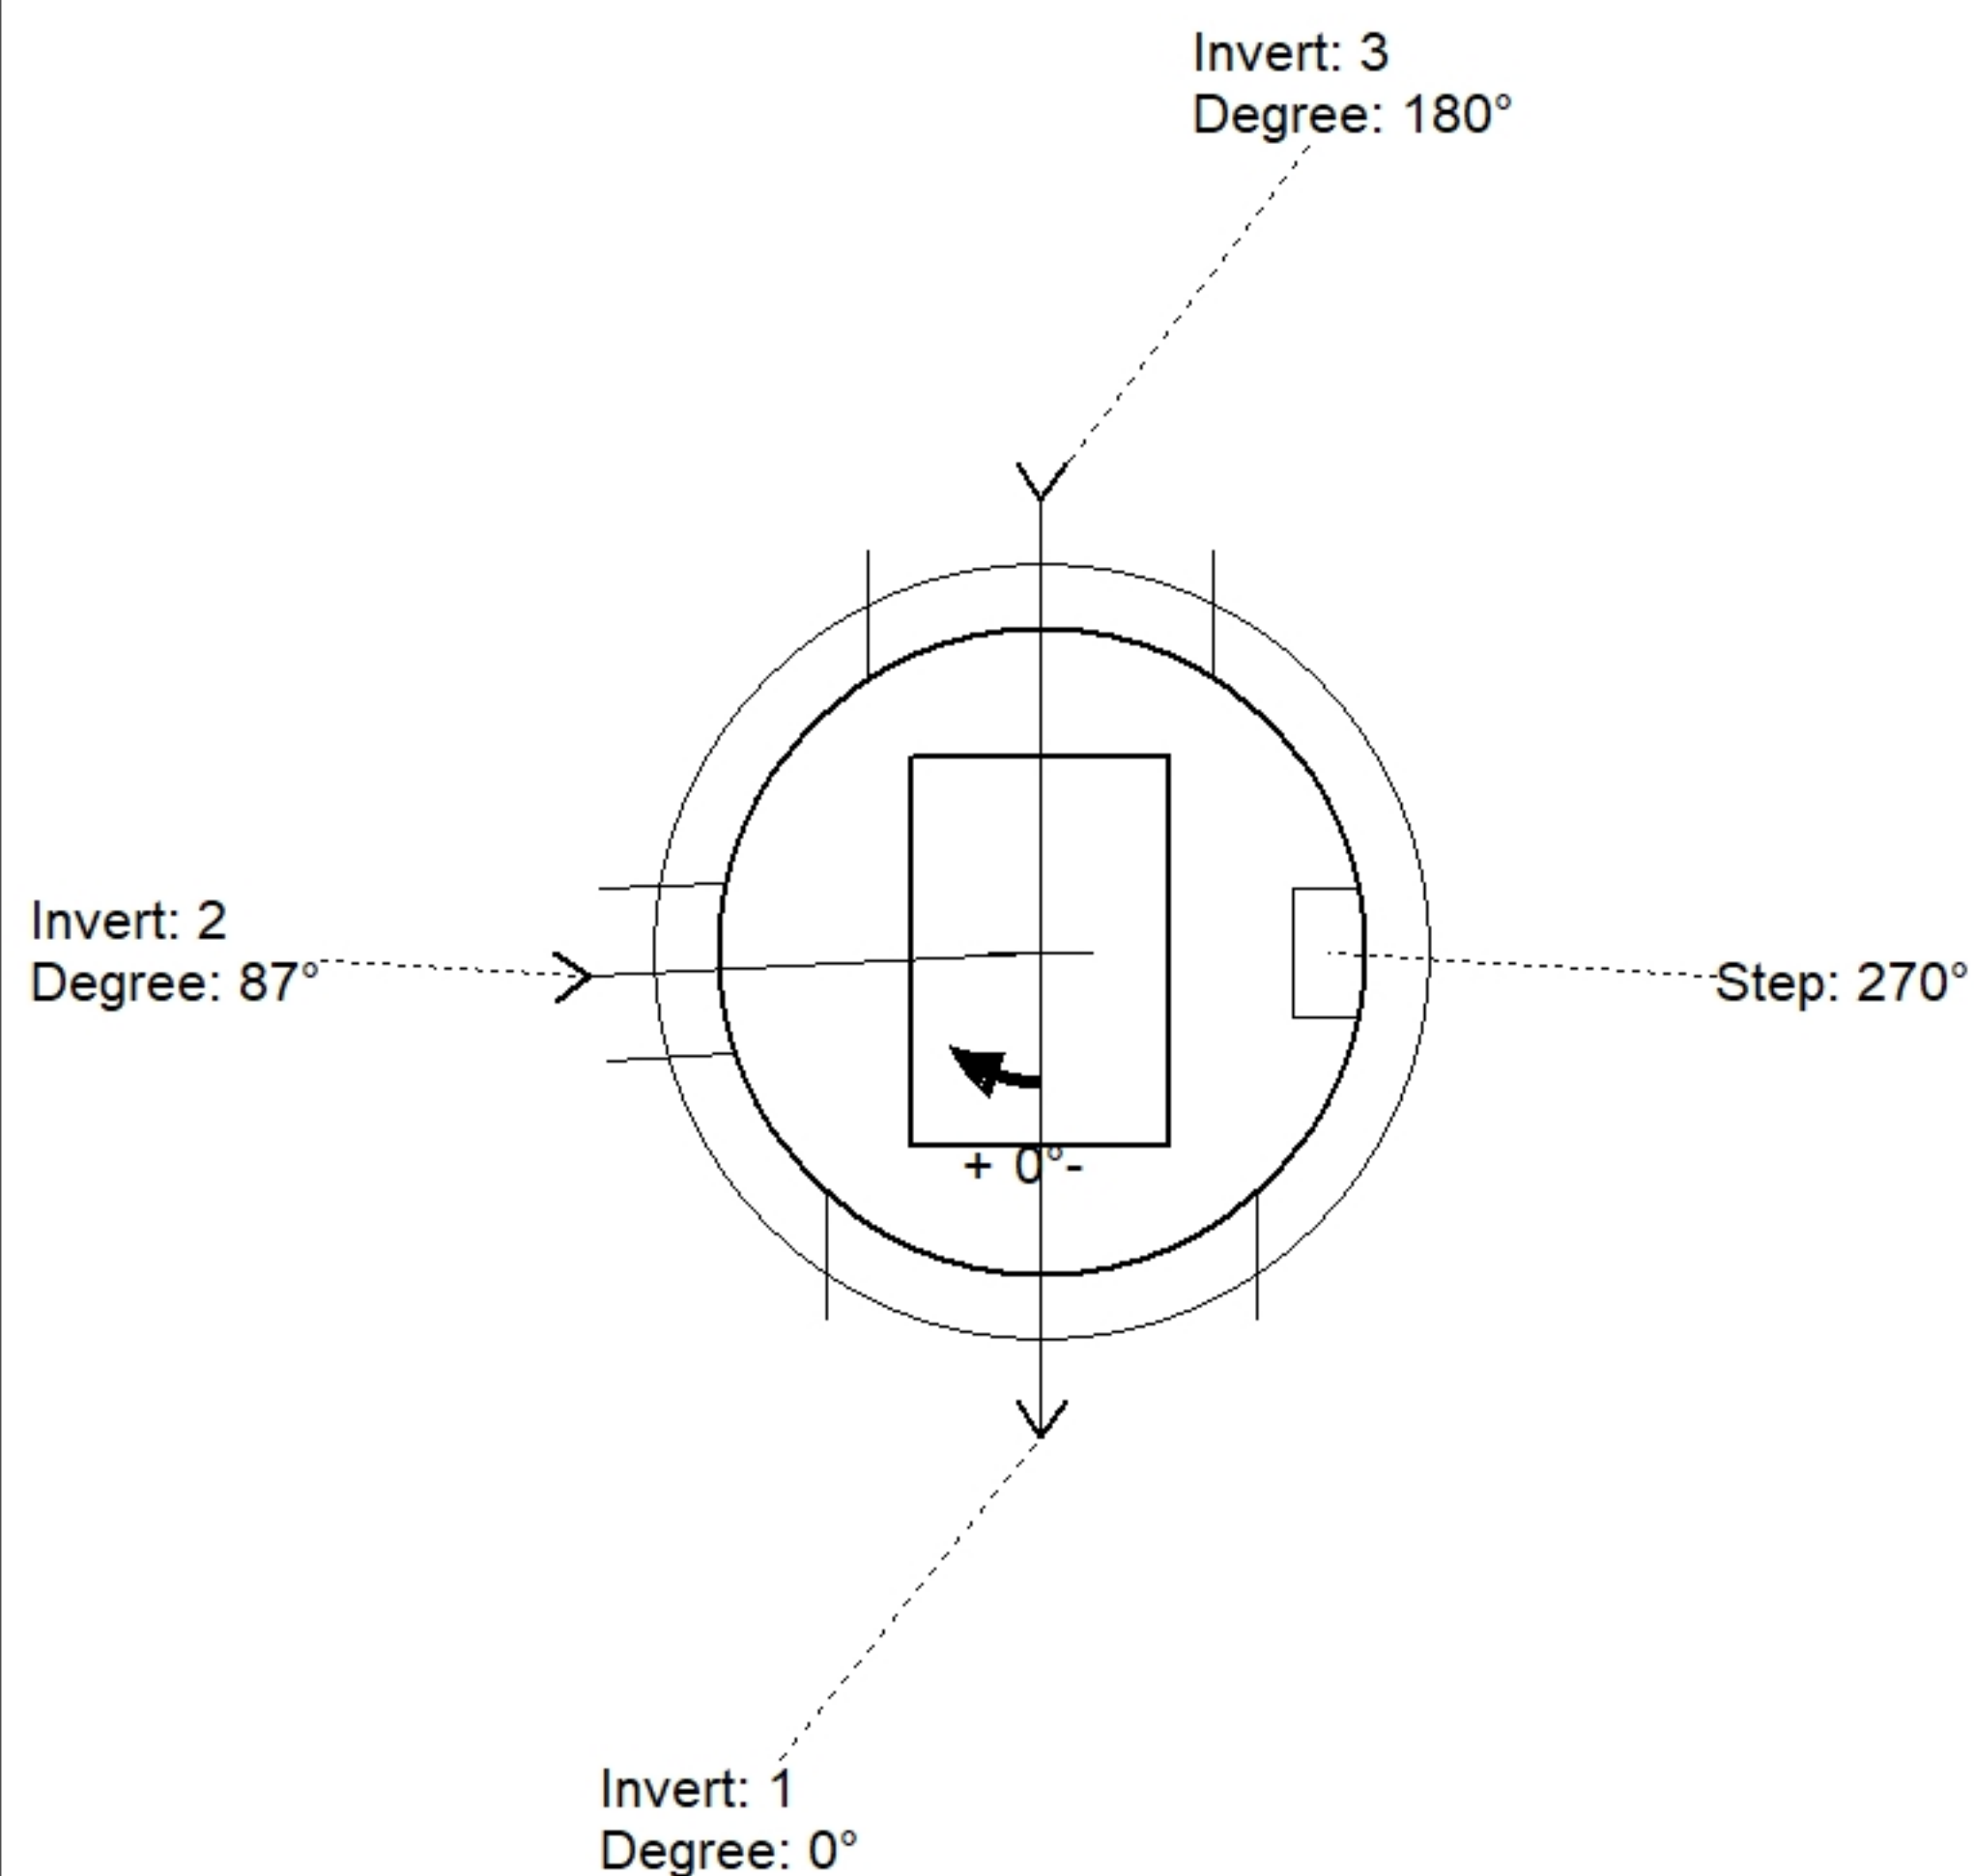

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	935.03'							
Reducer								
Invert 1	927.09'	0°	30" RCP B WALL	37"	40"	Hole 40	0"	P1
Invert 2	927.19'	87°	12" HDPE	14.5"	16"	Hole 16	3.45"	P1
Invert 3	927.09'	180°	24" RCP B WALL	30"	32"	Hole 32	0.5"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
