

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 3.87'

Floor Height: 8"


Slack: 0.19"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 30" - CASTING HEIGHT - 3.75"
P2) 60" - MH FLAT TOP w/24"x30" Hole - 8"
P1) 60" - MH BASE Custom Ht - 38"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
1) 60" - Conseal CS-102 1.00"
1) 24" x 30" - Conseal CS-102 1.00"
2) DOGHOUSE INVRTD - 40"x37"
1) DOGHOUSE INVRTD - 32"x31"



0 lb
2250 lb
3645 lb
421 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 6315 lb

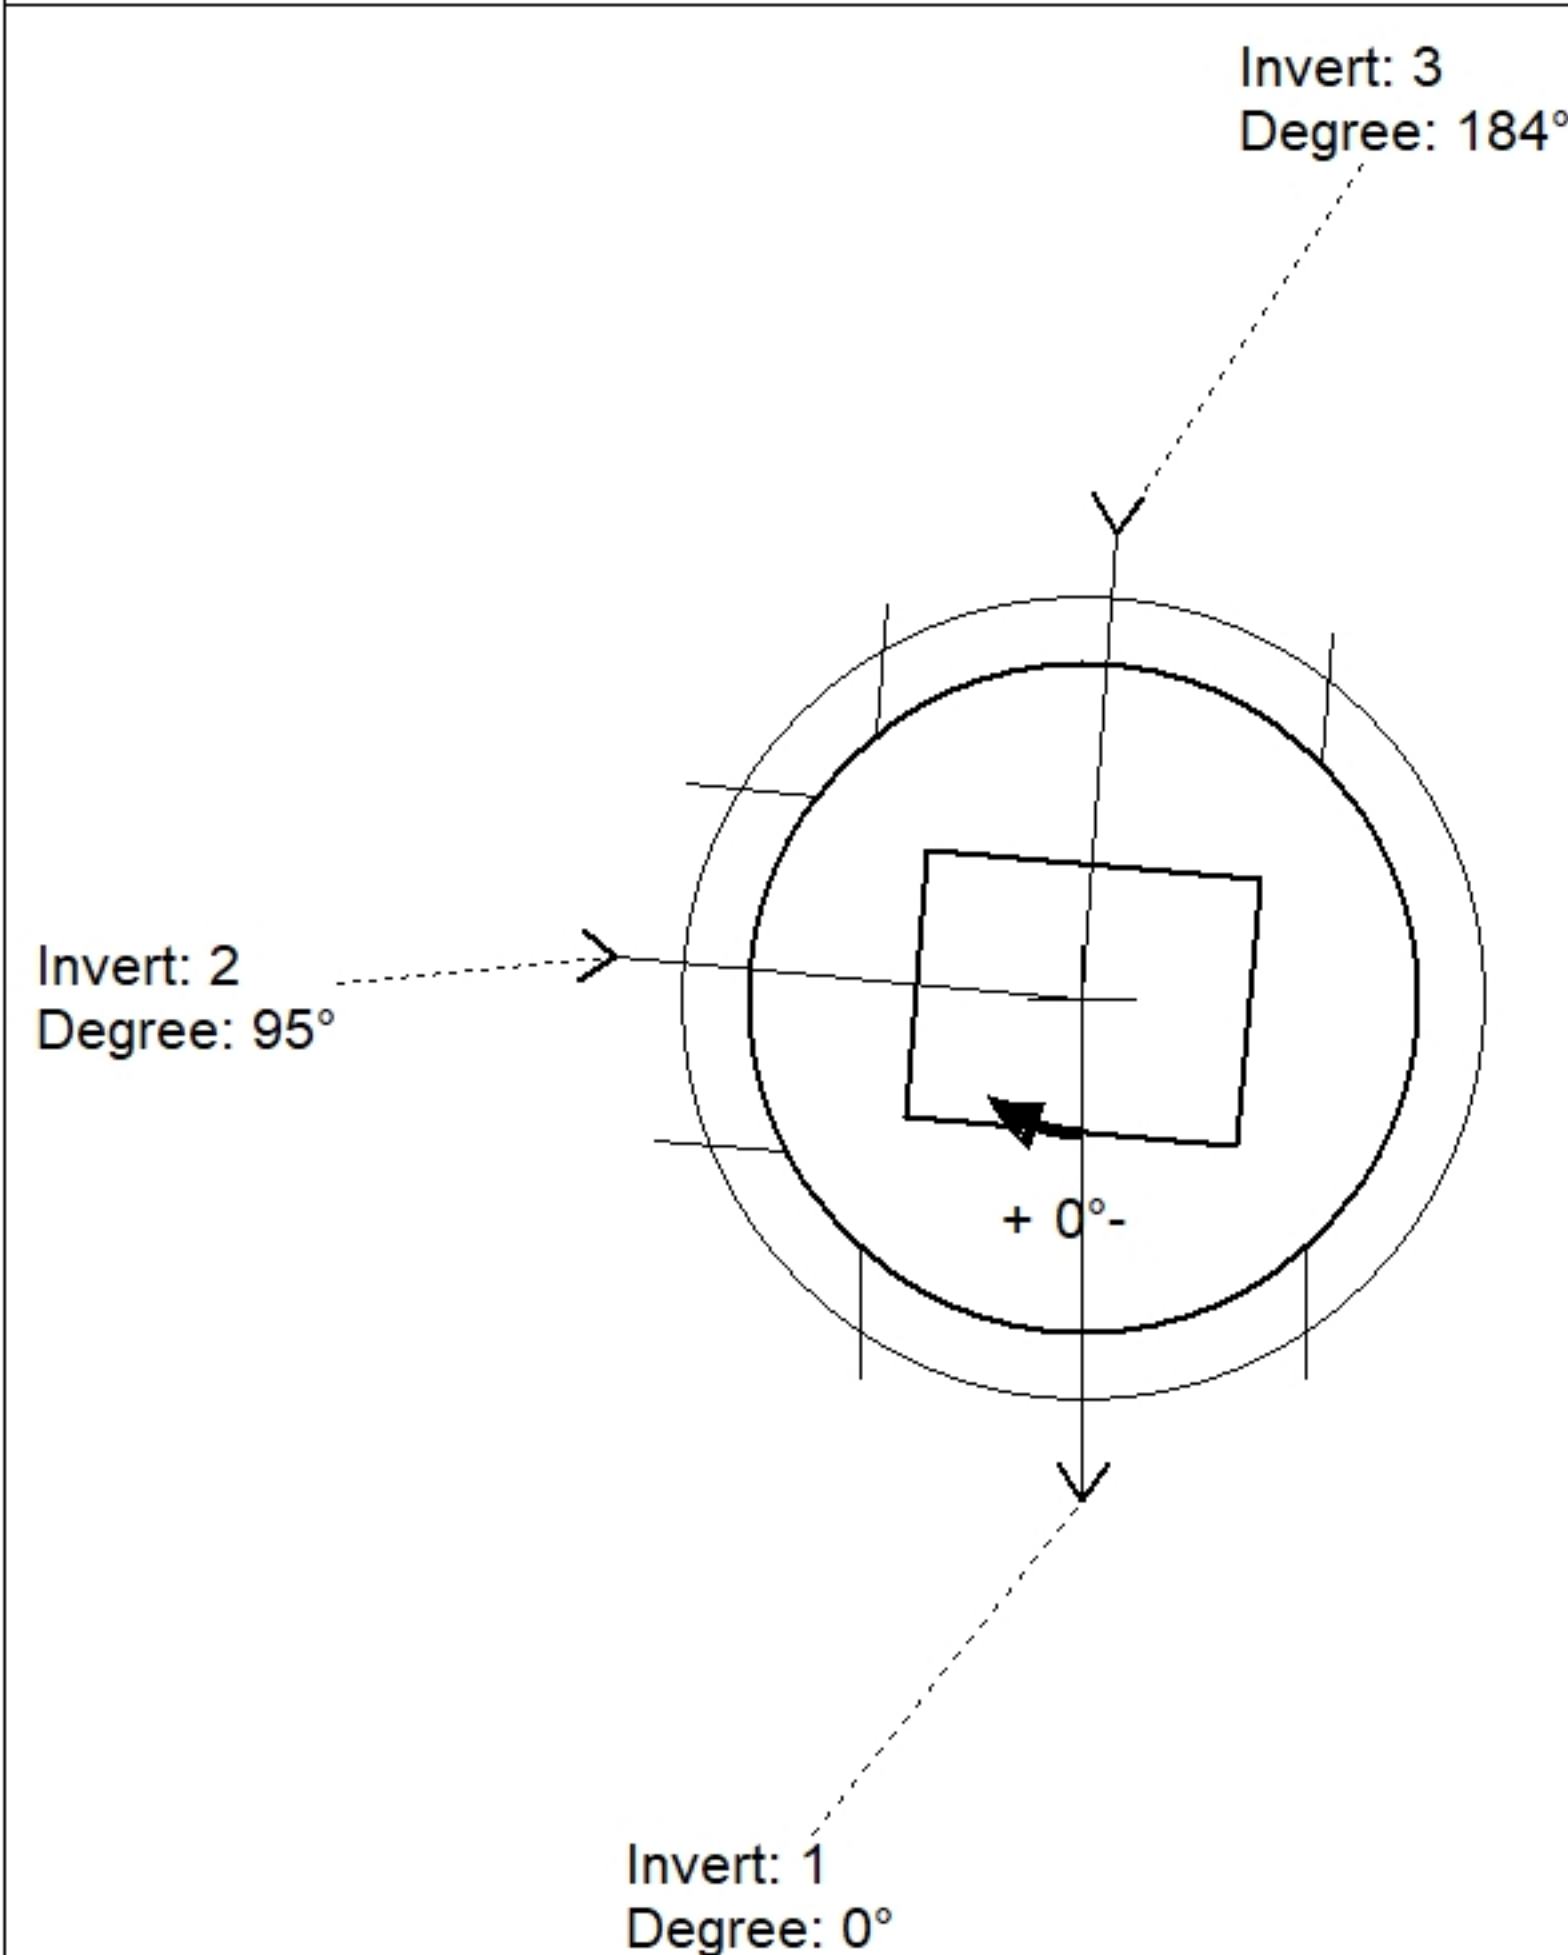

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	933.04'							
Reducer								
Invert 1	929.17'	0°	30" RCP B WALL	37"	40" x 37"	DOGHOUSE INVRTD 40"x37"	0"	P1
Invert 2	929.67'	95°	24" RCP B WALL	30"	32" x 31"	DOGHOUSE INVRTD 32"x31"	6.5"	P1
Invert 3	929.17'	184°	30" RCP B WALL	37"	40" x 37"	DOGHOUSE INVRTD 40"x37"	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

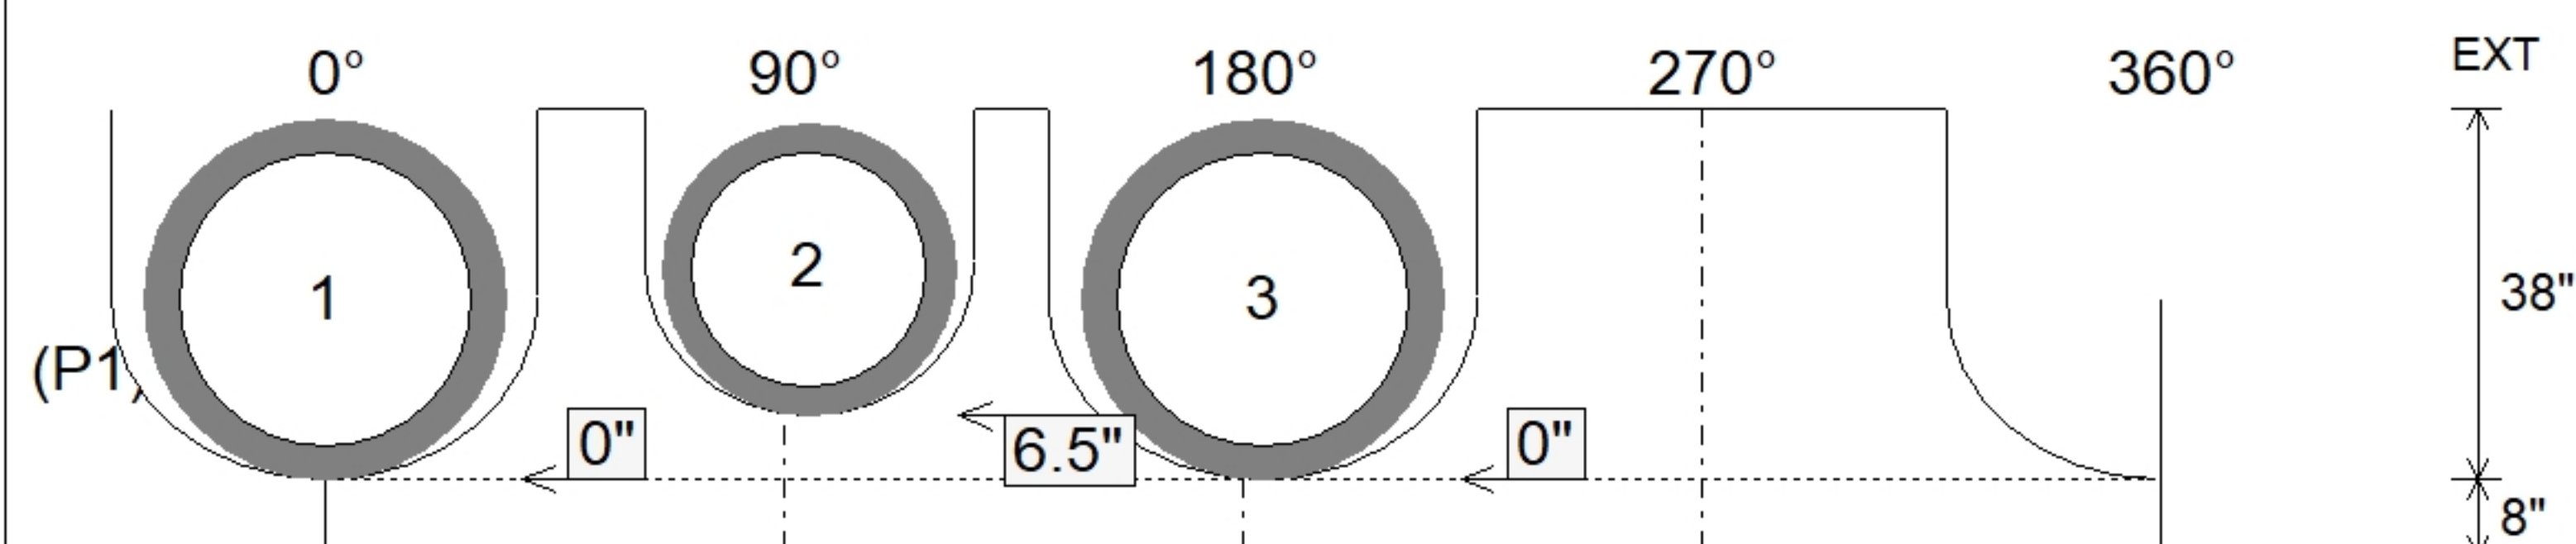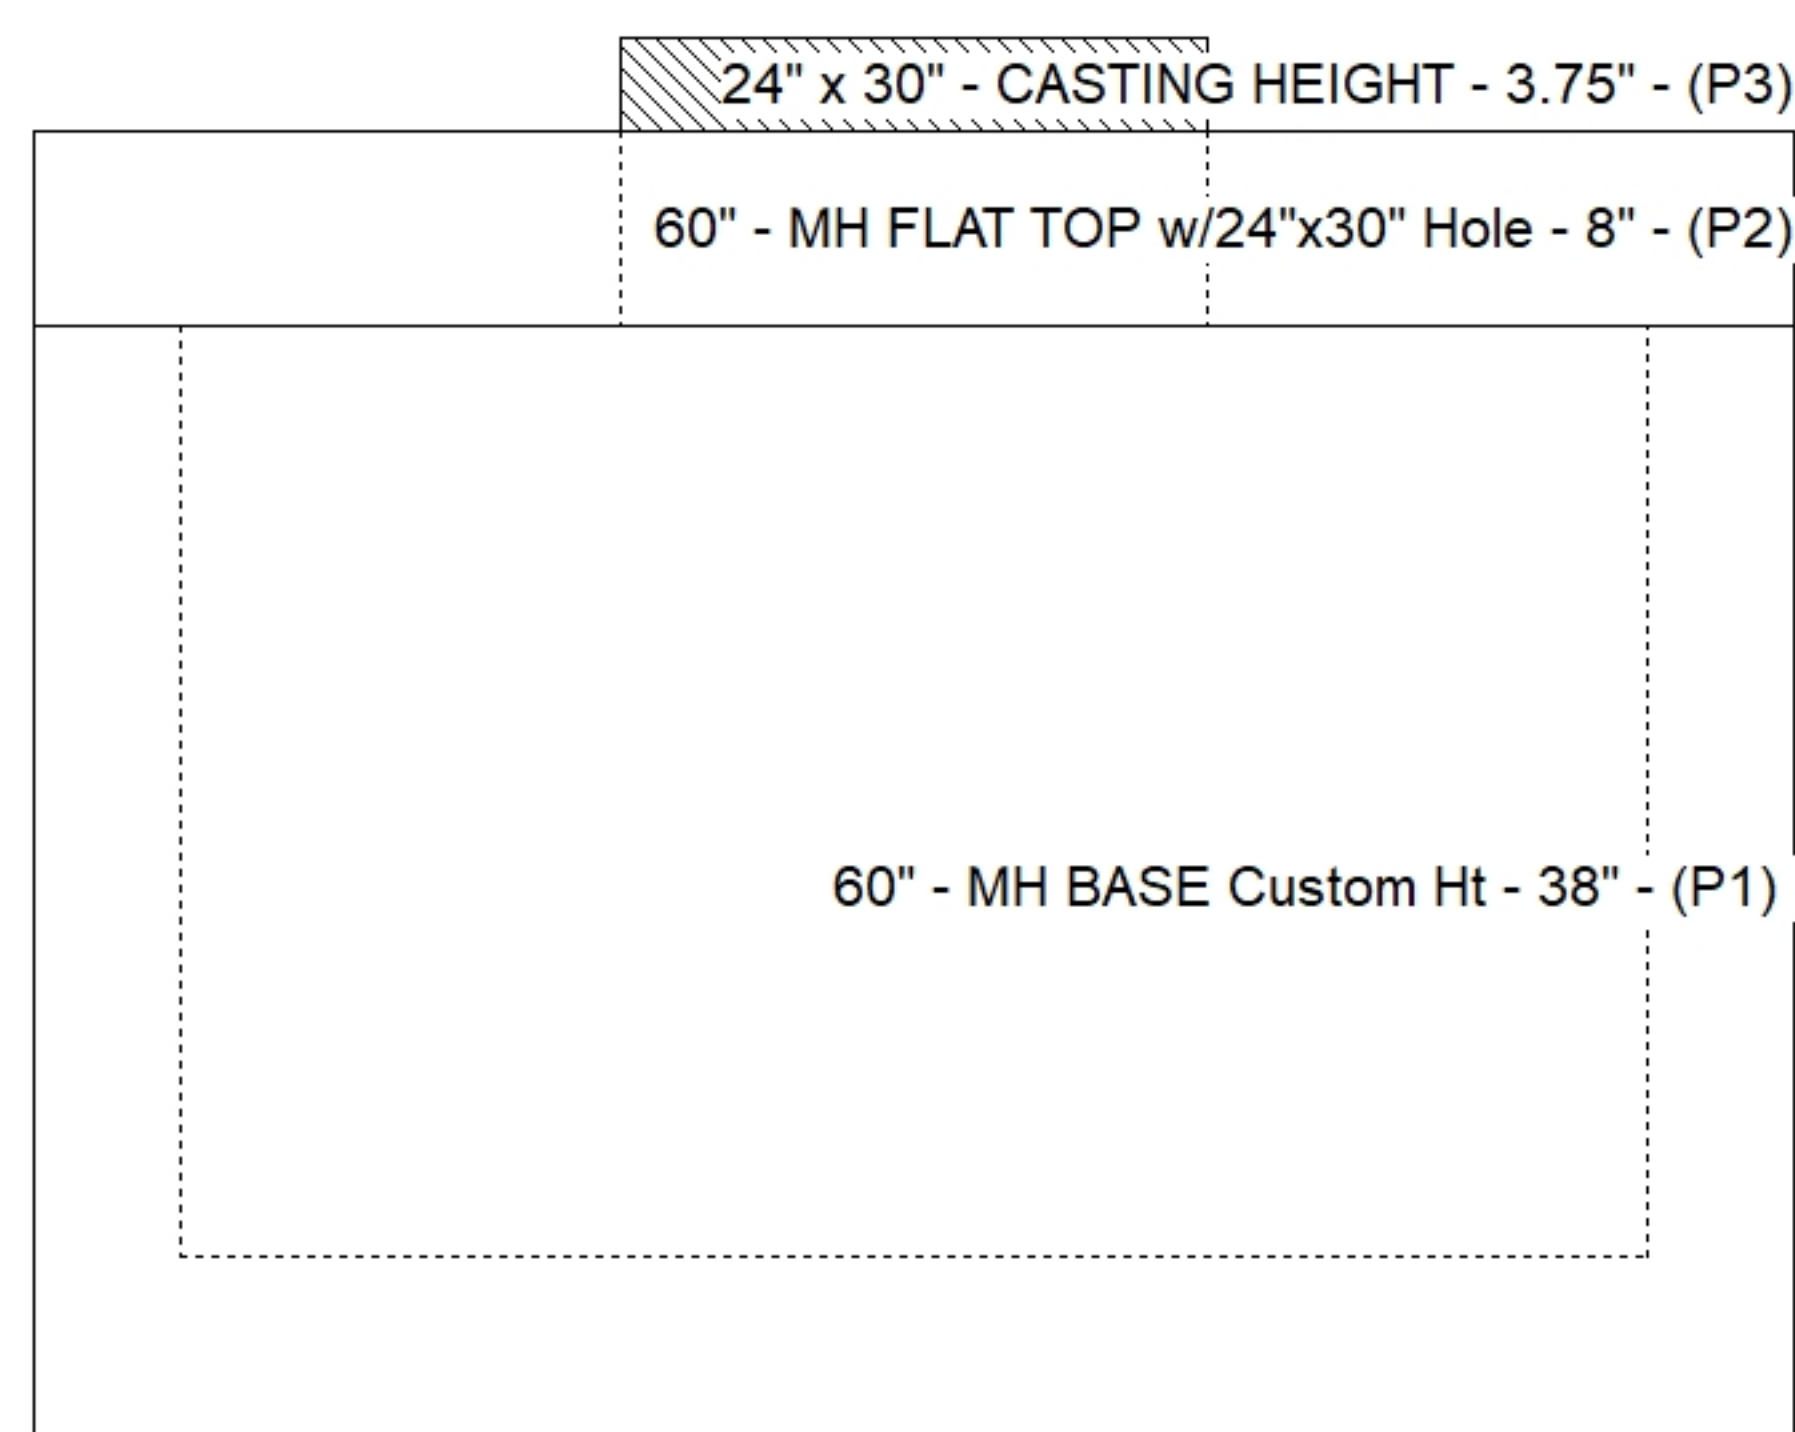

Submittal Drawing
9/29/2026 8:25:39 AM

SUBMITTAL
APPROVED BY:
