

Contractor: KY Earthworks

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 2.77'

Floor Height: 8"


Slack: 1.74"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 28"
1) CASTING - HOE 525 LV SET (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 26"x28"
1) Hole - 22



0 lb
3562 lb
442 lb
0 lb
0 lb
0 lb

Structure Total: 4004 lb

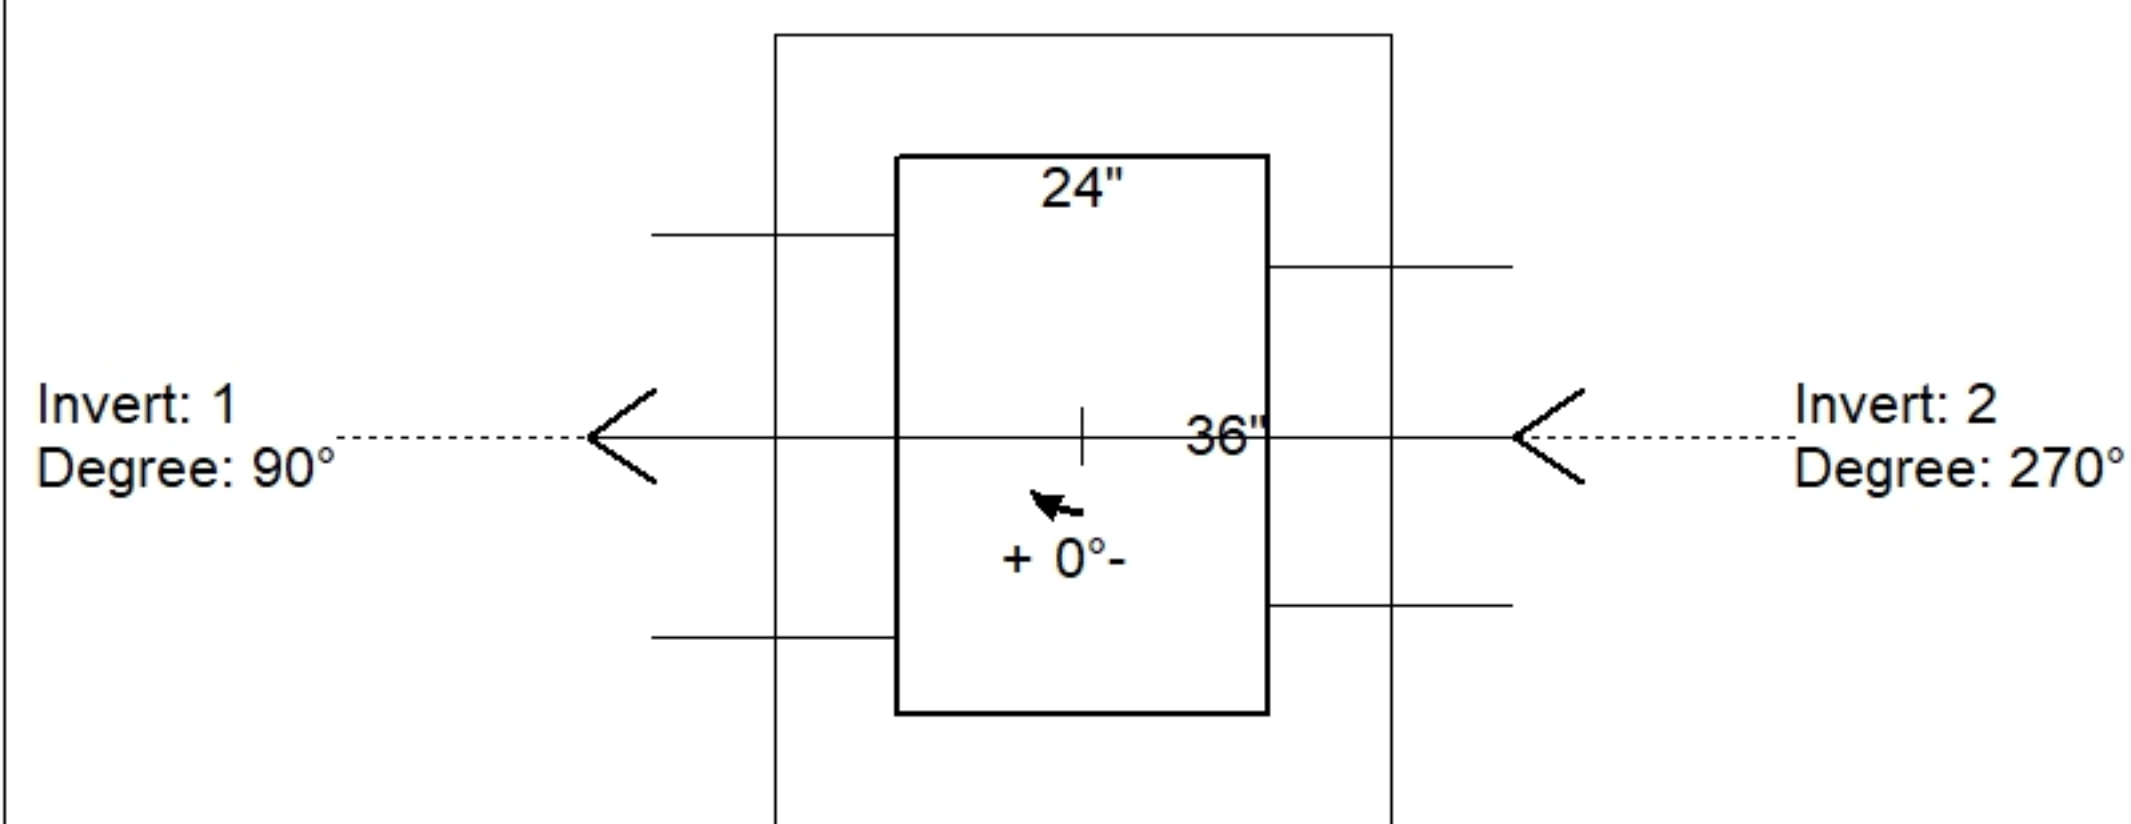

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	934.39'							
Reducer								
Invert 1	931.62'	90°	18" RCP B WALL	23"	26" x 28"	DOGHOUSE INVRTD 26"x28"	0"	P1
Invert 2	931.62'	270°	15" RCP B WALL	19.5"	22"	Hole 22	0.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

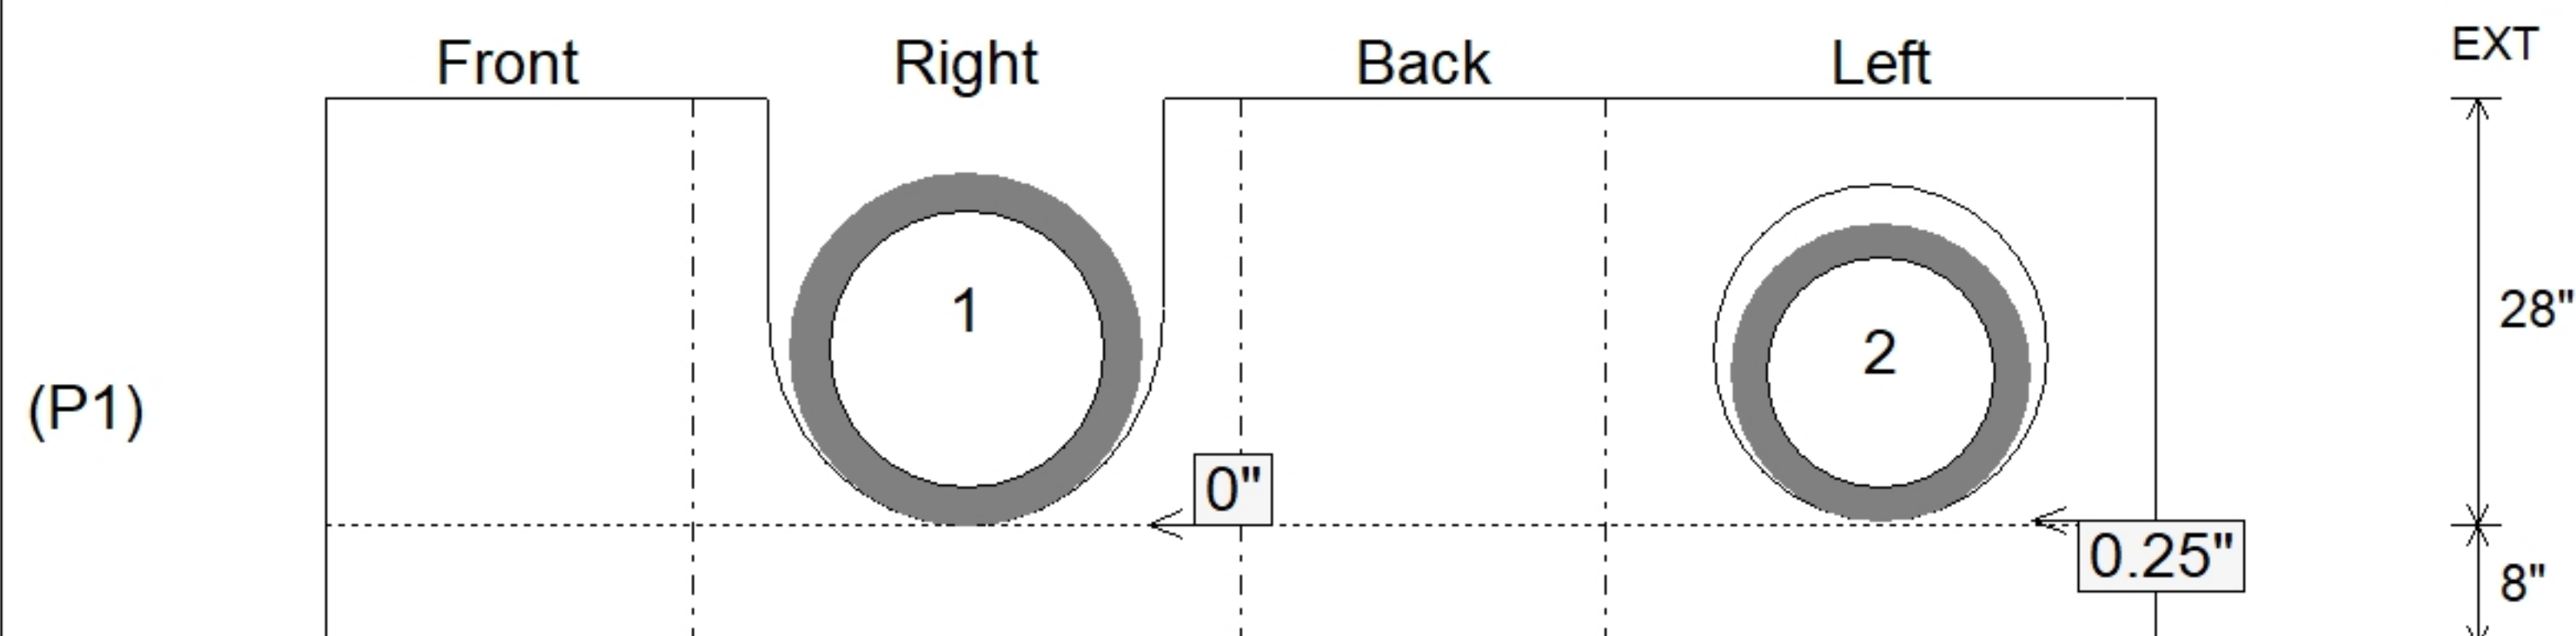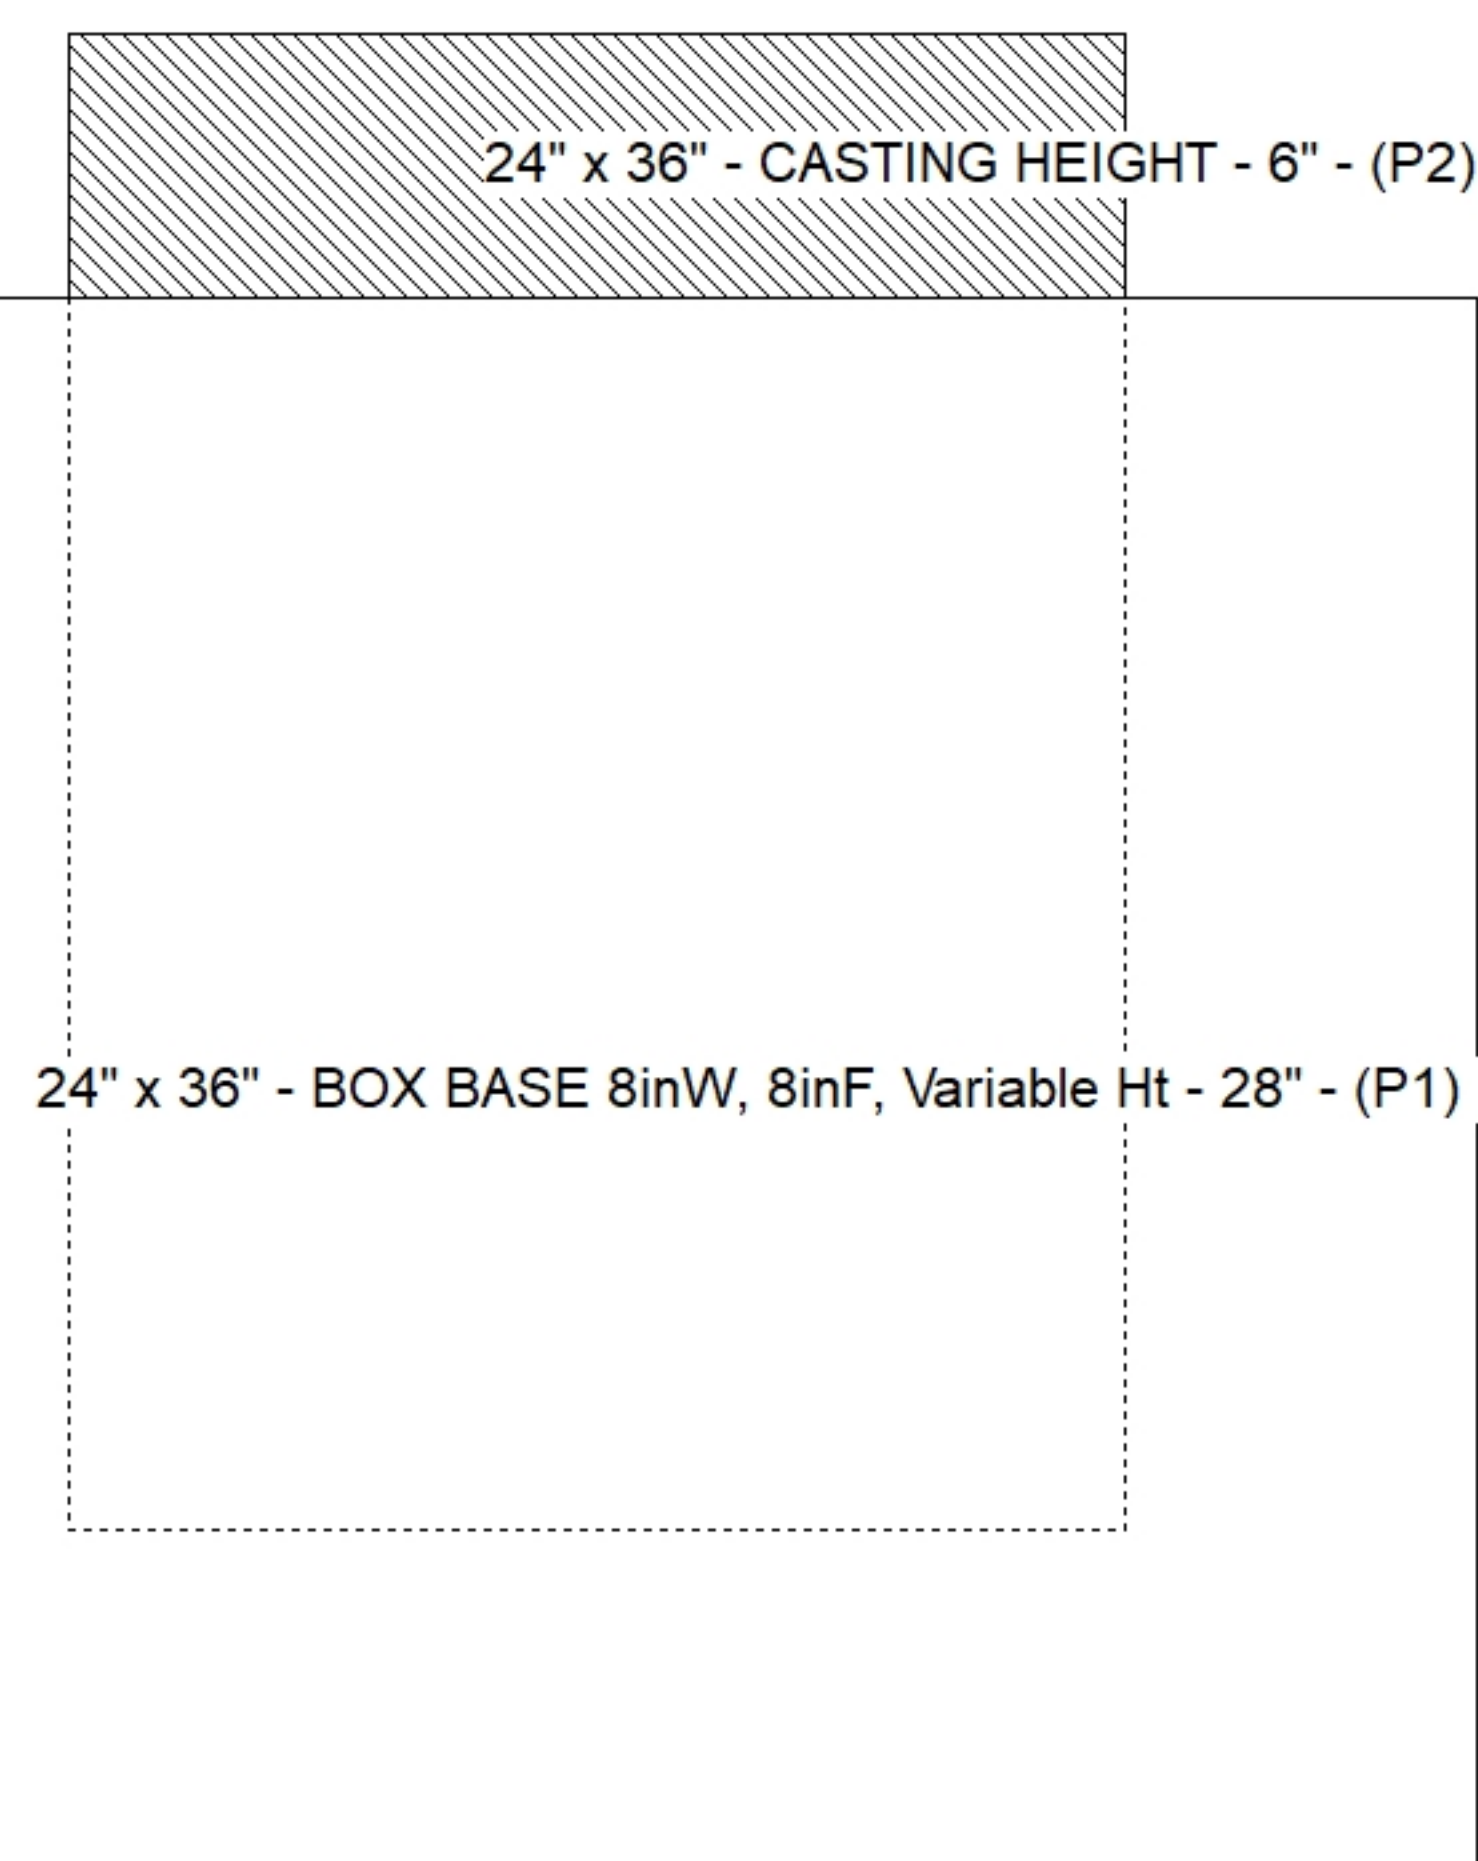

Submittal Drawing
9/29/2026 8:25:37 AM

SUBMITTAL
APPROVED BY:
