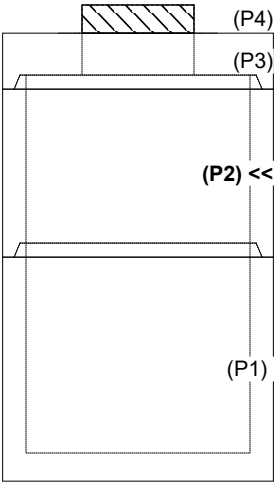





Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC				Plant: 100 6/4/2026 4:38:06 PM		Tech: Jared - F PC: E. Bardley						
Structure ID: 13 ST-CI												
P2 MH048RS36S				MH RISER T/G								
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 42" 1) CASTING - HOE 525 SET FLAT GRATE (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 26 1) Hole - 22						0 lb 1300 lb 2515 lb 3866 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8123 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)). 5. CITY OF BGKY-CBI TYPE F. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 680.83'				Rim to Invert: 8'		Slack: 0"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
INSIDE WALL DIMENSIONS												
												
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd		
