

Contractor: RD Sitework LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 8'

Floor Height: 6"

Slack: 0"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)).
5. CITY OF BGKY-CBI TYPE F.



- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P4) 24" x 36" - CASTING HEIGHT - 6"
P3) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P2) 48" - MH RISER SPECIAL - 36"
P1) 48" - MH BASE - 42"

1) Hole - 22


0 lb

Structure Total: 8123 lb

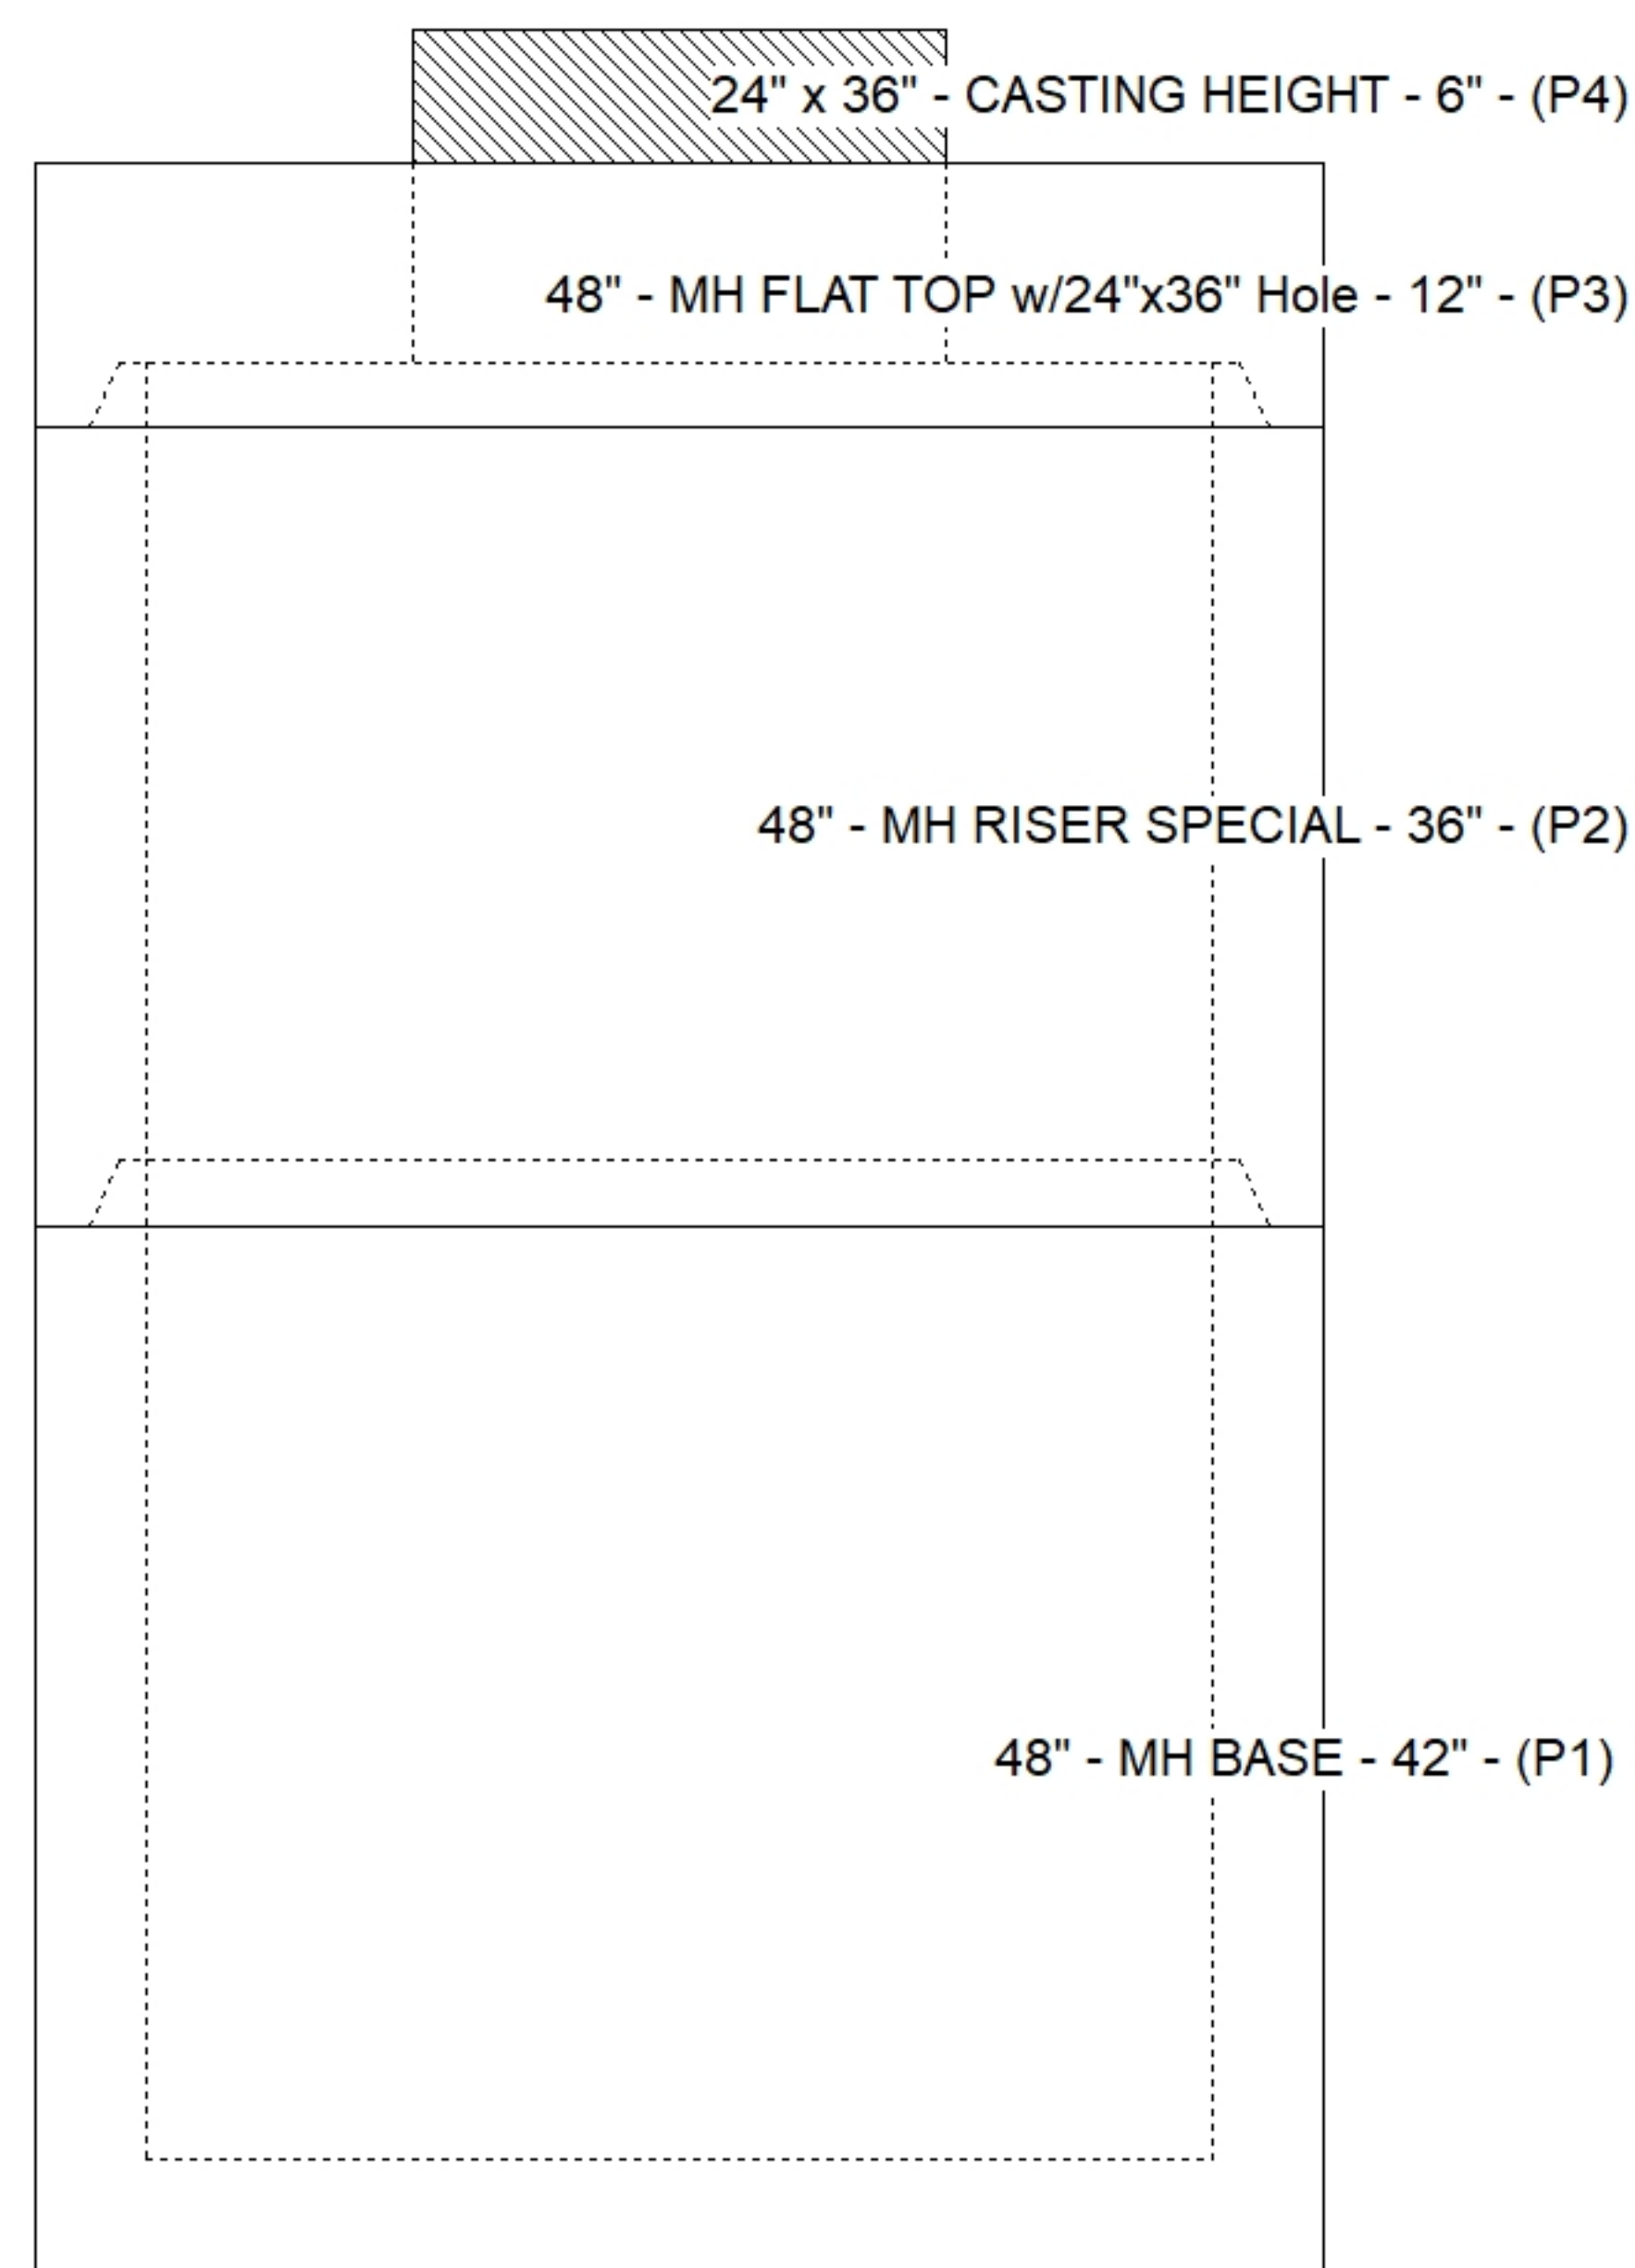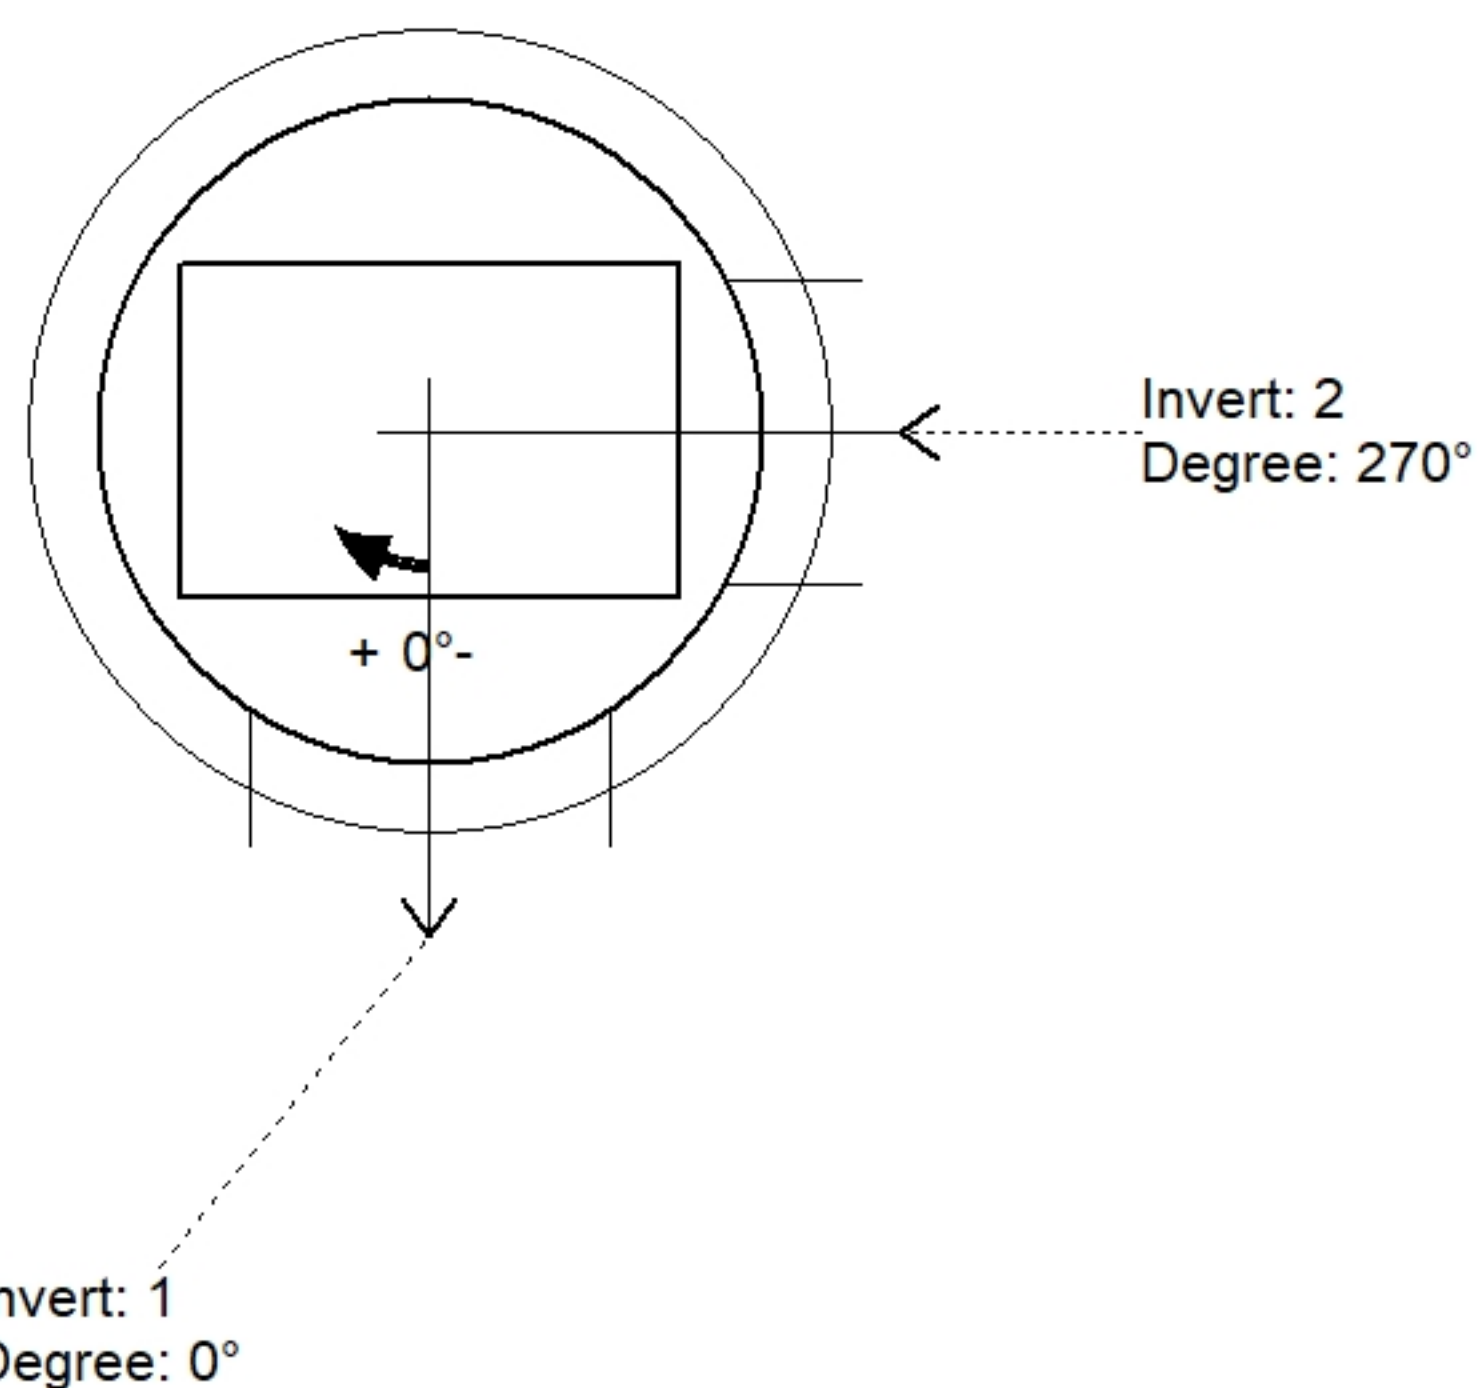

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	680.83'							
Reducer								
Invert 1	672.83'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	672.83'	270°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

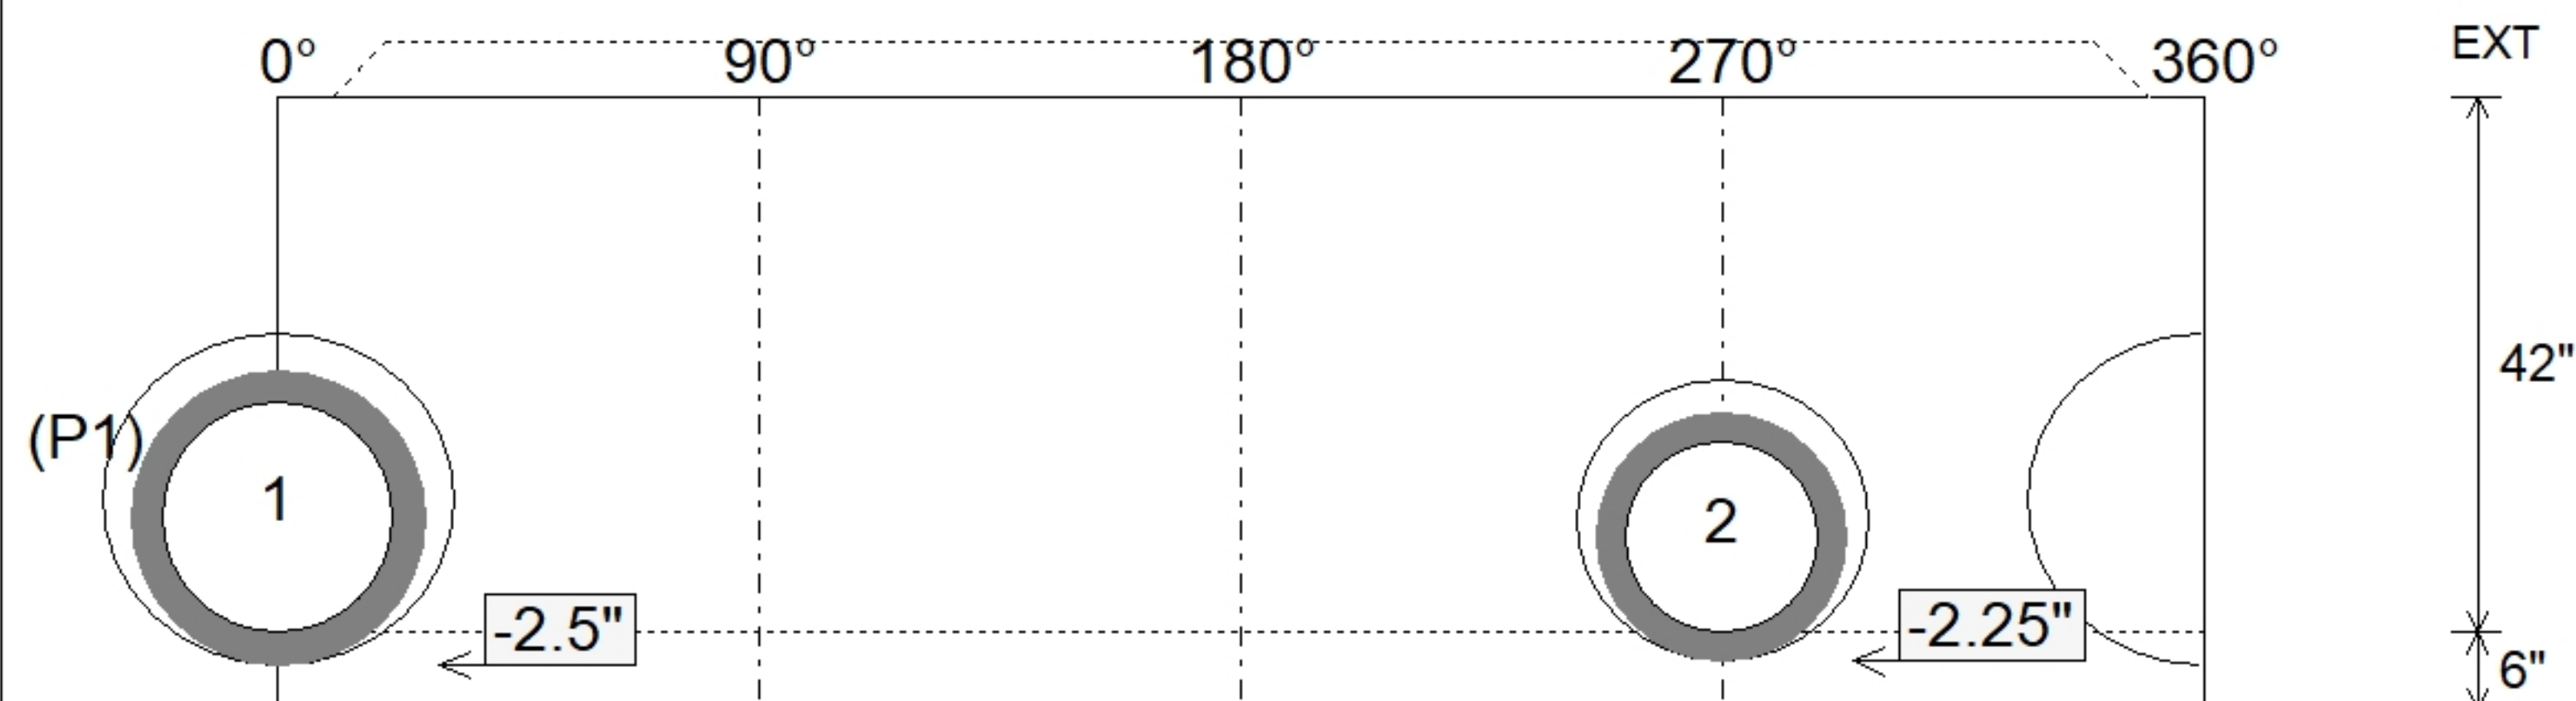

Submittal Drawing
6/8/2026 12:38:50 PM

SUBMITTAL
APPROVED BY:
