



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:04 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 19 ST-DCI											
P1 BX036084-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8" P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" 1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H) 1) 36" x 84" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 26"						0 lb 2911 lb 13368 lb 442 lb 0 lb 0 lb 0 lb ----- 16721 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .47) #5 BARS AT 8" C.C.E.W. - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
Rim: 676.6' Rim to Invert: 6' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	670.6'	0°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 2	670.6'	180°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

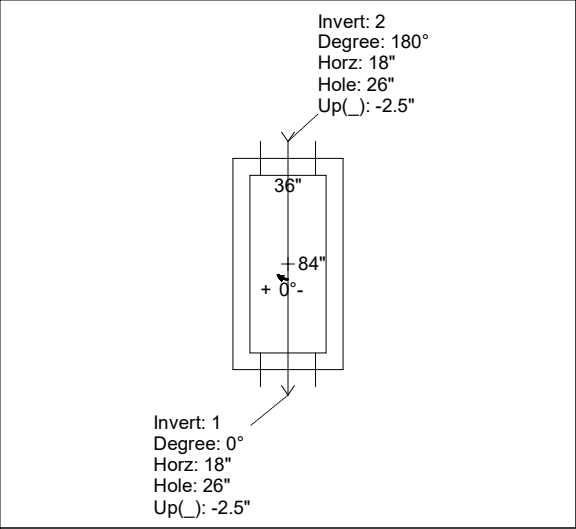


RIGHT-SIDE UP VIEW (int. dimensions)

1ST POUR (FLOOR) = 3,490 LBS
2ND POUR (WALLS) = 9,878 LBS

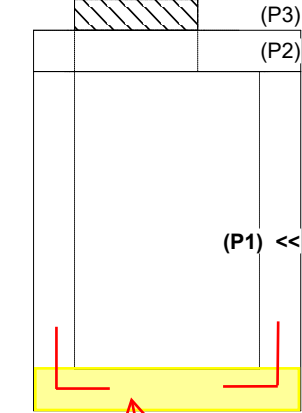

1ST POUR (FLOOR)
STUB #5 L BARS OUT
TOP FLOOR, SPA AT
12" C/C FOR
CONNECTING WALLS

INSIDE WALL DIMENSIONS

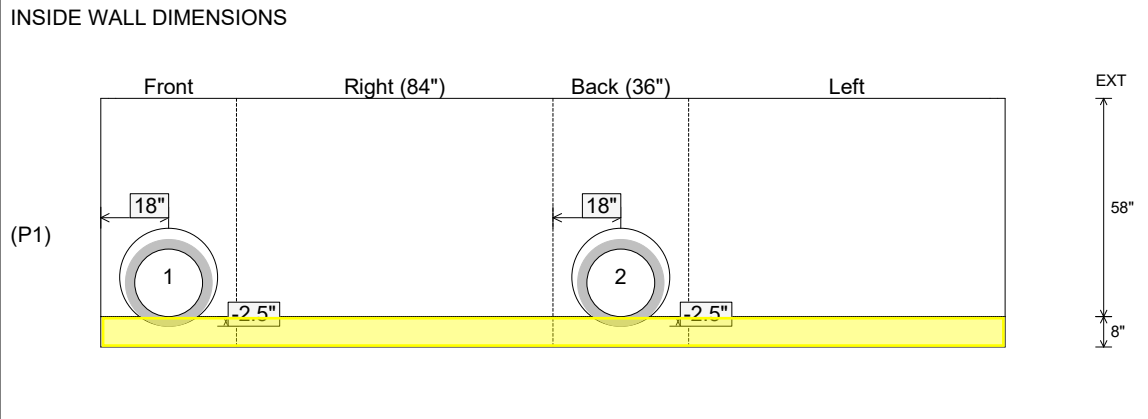


INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 58" Height (Ext): 66"	Weight (Net): 13368 lb Volume (Net): 3.42cu.yd
----------------------------------	-------------------------------	--	--	---


Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:04 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 19 ST-DCI											
P1 BX036084-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8" P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" 1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H) 1) 36" x 84" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 26"						0 lb 2911 lb 13368 lb 442 lb 0 lb 0 lb 0 lb ----- 16721 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .47) #5 BARS AT 8" C.C.E.W. - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
Rim: 676.6' Rim to Invert: 6' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	670.6'	0°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 2	670.6'	180°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

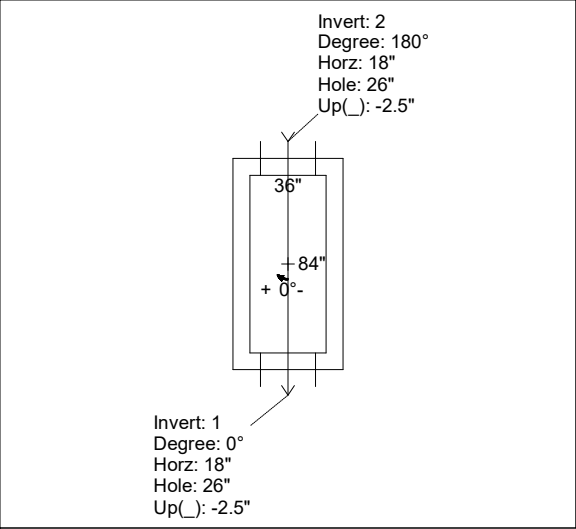


UPSIDE-DOWN VIEW (int. dimenions)

1ST POUR (FLOOR) = 3,490 LBS
2ND POUR (WALLS) = 9,878 LBS

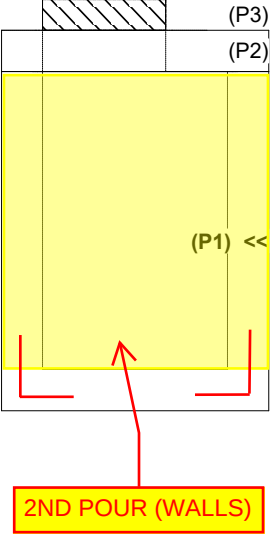

INSIDE WALL DIMENSIONS

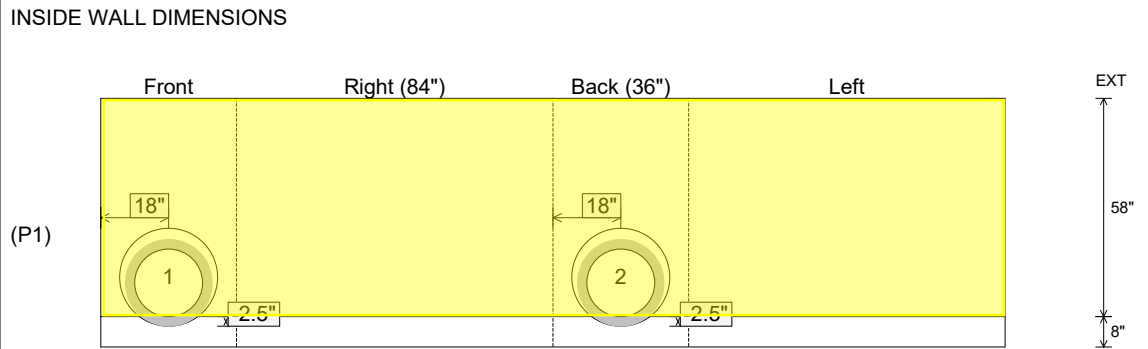

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 58" Height (Ext): 66"	Weight (Net): 13368 lb Volume (Net): 3.42cu.yd
----------------------------------	-------------------------------	--	--	---
