



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC				Plant: 100 6/4/2026 4:34:13 PM		Tech: Jared - F PC: E. Bardley					
Structure ID: 38 ST-DCI											
P1 BX036084-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n							
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8" P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" 1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H) 1) 36" x 84" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 62"x62" 2) Hole - 32 1) Hole - 46						0 lb 2911 lb 9541 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 12893 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .47) #5 BARS AT 8" C.C.E.W. - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
Rim: 693.34'				Rim to Invert: 6'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector		Hole	Horz Size	Up (_)	Offset
Invert 1	687.34'	90°	50"	48" RCP B WALL	58"	DOGHOUSE INVRTD 62"x62"		62" x 62"	62"	-5"	0"
Invert 2	687.34'	180°	26"	24" RCP B WALL	30"	Hole 32		32"	32"	-3"	0"
Invert 3	687.34'	270°	50"	36" RCP B WALL	44"	Hole 46		46"	46"	-4"	0"
Invert 4	687.34'	0°	26"	24" RCP B WALL	30"	Hole 32		32"	32"	-3"	0"
Invert 5											
Invert 6											
Invert 7											
Invert 8											

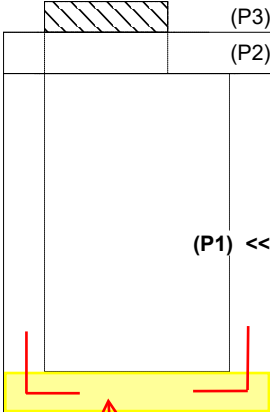

(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

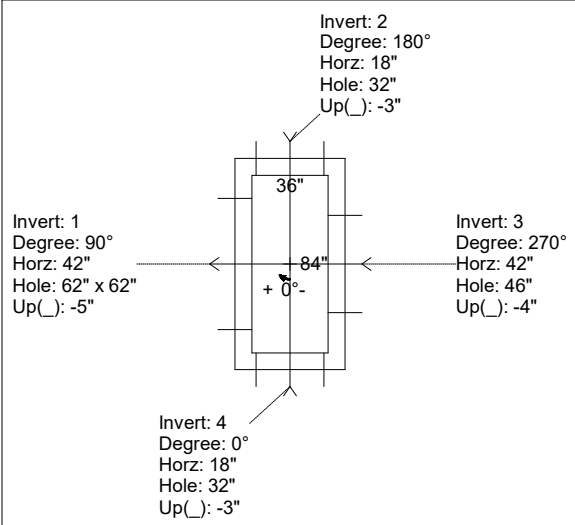

Invert: 2
Degree: 180°
Horz: 18"
Hole: 32"
Up(_): -3"

Invert: 1
Degree: 90°
Horz: 42"
Hole: 62" x 62"
Up(_): -5"


Invert: 3
Degree: 270°
Horz: 42"
Hole: 46"
Up(_): -4"

Invert: 4
Degree: 0°
Horz: 18"
Hole: 32"
Up(_): -3"

UPSIDE-DOWN VIEW (int. dimenions)

1ST POUR (FLOOR) = 3,490 LBS
2ND POUR (WALLS) = 6,051 LBS

INSIDE WALL DIMENSIONS

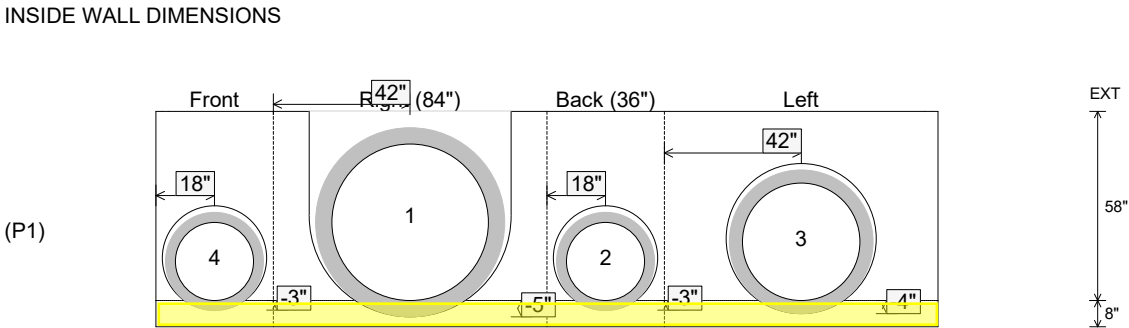

Front: 42" (84")
Back (36")
Left: 42"

18" 18" 42"

1 2 3 4

-3" -3" -3" 4"

(P1)

EXT 58" 8"

1ST POUR (FLOOR)
STUB #5 L BARS OUT
TOP FLOOR, SPA AT
12" C/C FOR
CONNECTING WALLS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 58" Height (Ext): 66"	Weight (Net): 9541 lb Volume (Net): 2.44cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 26-1899 - Gateway 65 Industrial Road

Job Location: Franklin, KY

Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:34:13 PM

Tech: Jared - F

PC: E. Bardley



Structure ID: 38 ST-DCI

P1 BX036084-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P3) 24" x 36" - CASTING HEIGHT - 6"

P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8"

P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58"

1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H)

1) 36" x 84" - Conseal CS-102 1.00"

1) 24" x 36" - Conseal CS-102 1.00"

1) DOGHOUSE INVRTD - 62"x62"

2) Hole - 32

1) Hole - 46

0 lb

2911 lb

9541 lb

442 lb

0 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 12893 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. NO STEPS AND NO INVERT CHANNEL.

4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .47) #5 BARS AT 8" C.C.E.W.

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 693.34'

Rim to Invert: 6'


Slack: 0"

Sump: 0"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	687.34'	90°	50"	48" RCP B WALL	58"	DOGHOUSE INVRTD 62"x62"	62" x 62"	62"	-5"	0"
Invert 2	687.34'	180°	26"	24" RCP B WALL	30"	Hole 32	32"	32"	-3"	0"
Invert 3	687.34'	270°	50"	36" RCP B WALL	44"	Hole 46	46"	46"	-4"	0"
Invert 4	687.34'	0°	26"	24" RCP B WALL	30"	Hole 32	32"	32"	-3"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimenions)

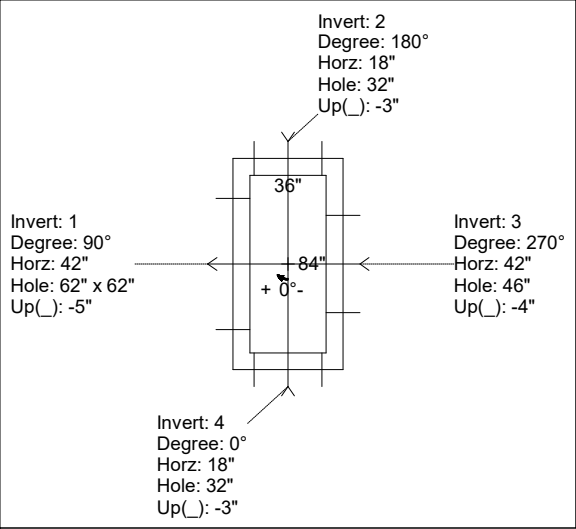

UPSIDE-DOWN VIEW (int. dimenions)


1ST POUR (FLOOR) = 3,490 LBS

2ND POUR (WALLS) = 6,051 LBS

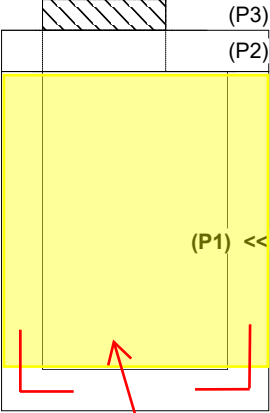

2ND POUR (WALLS)

INSIDE WALL DIMENSIONS

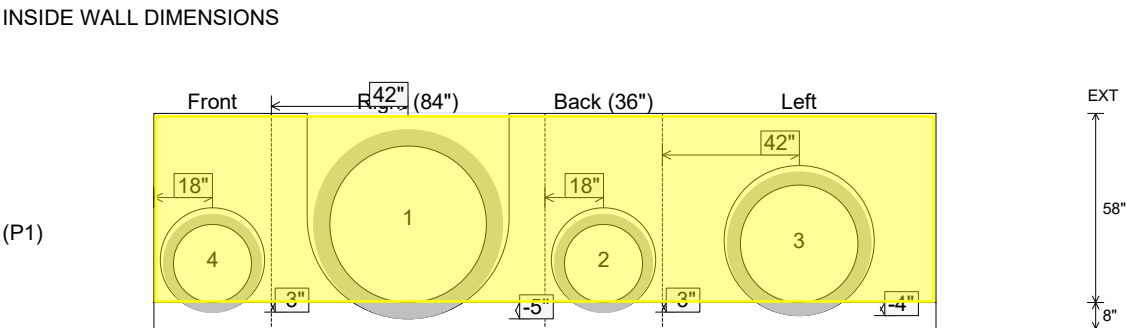

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 58"

Height (Ext): 66"

Weight (Net): 9541 lb

Volume (Net): 2.44cu.yd
