

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:39:06 PM

Tech: Jared - F
PC: E. Bardley



Structure ID: 4 ST-CI

P2 MH048LD12-24X36RECT

MH FLAT TOP w/24"x36" Hole F/G

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 38"
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
3) Hole - 22


Structure Total:

0 lb
1300 lb
3491 lb
442 lb
0 lb
0 lb
0 lb

5233 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)).
 5. CITY OF BGKY-CBI TYPE F.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

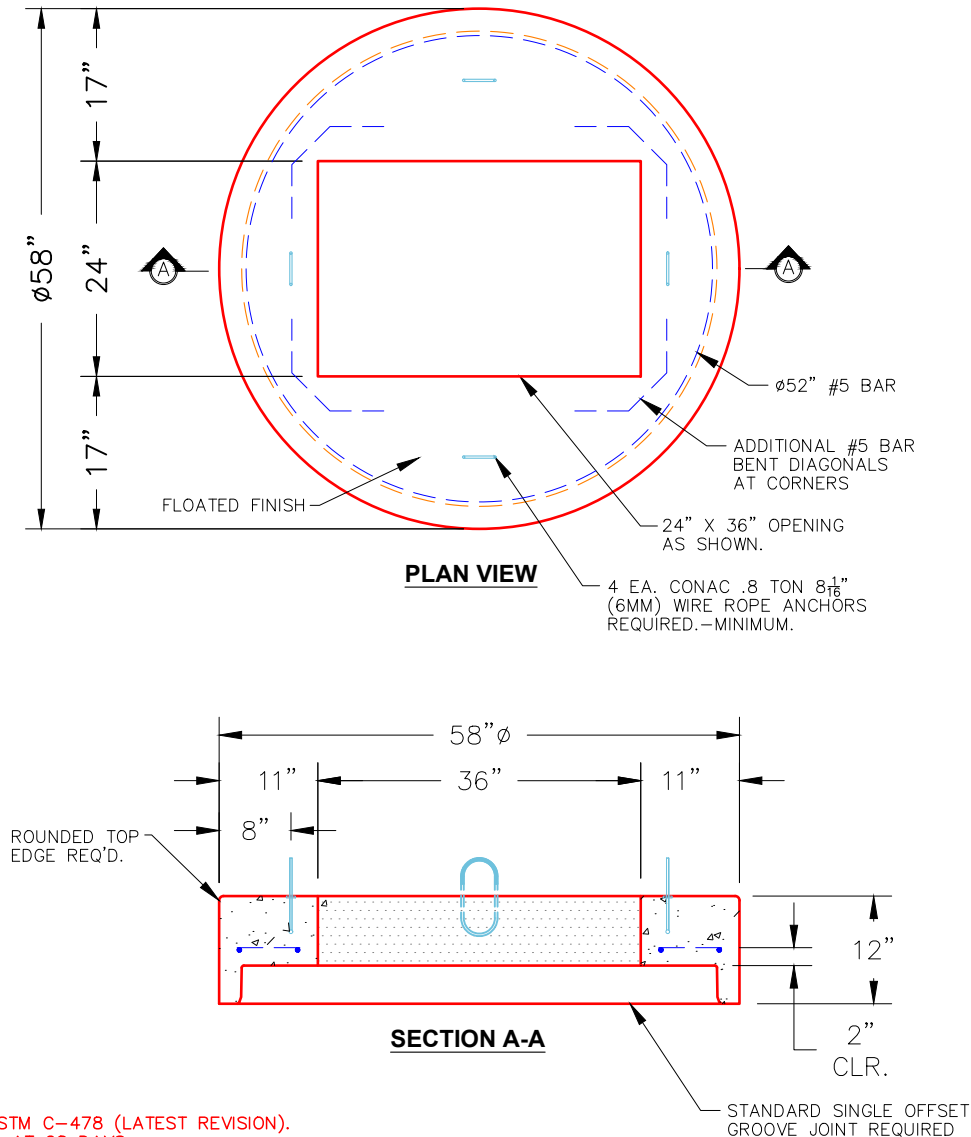

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
