


Contractor: RD Sitework LLC

Plant: 100



Slack: 0.4"

Structure Total: 5143 lb

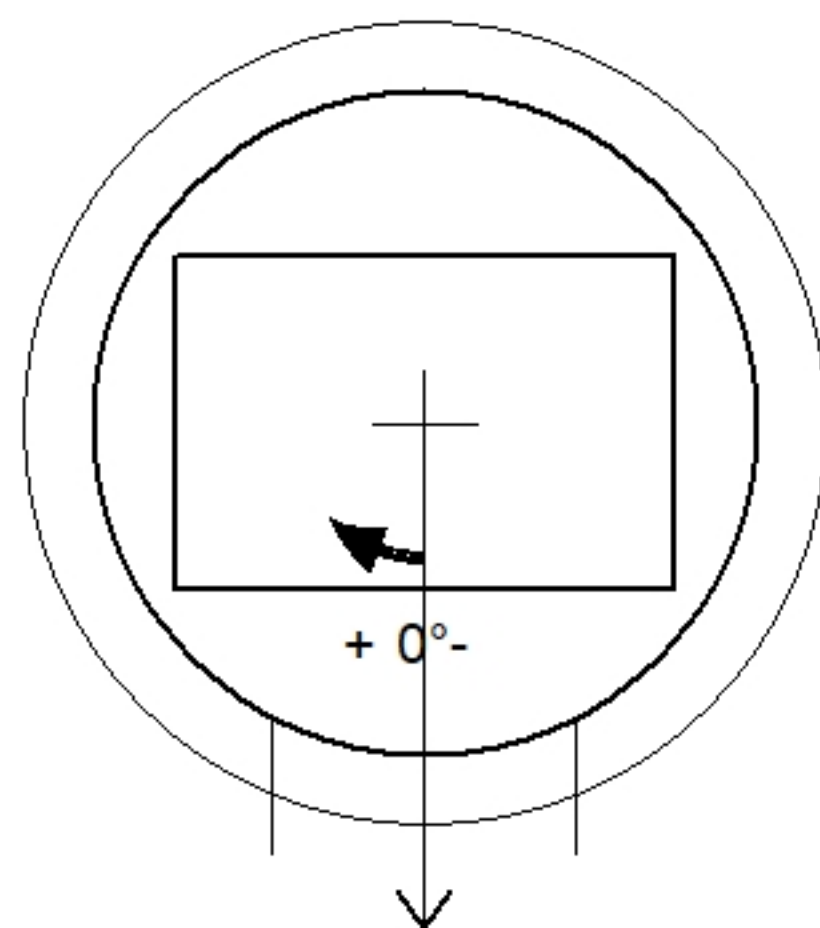

Invert: 1
Degree: 0°


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	693.21'							
Reducer								
Invert 1	689.01'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 12" - (P2)

48" - MH BASE Custom Ht - 32" - (P1)

The diagram illustrates the vertical assembly of a manhole. At the top is a hatched rectangular casting (P3) with dimensions 24 inches by 36 inches and a height of 6 inches. Below it is a flat top (P2) with a 12-inch height and a central rectangular hole matching the casting's footprint. The base (P1) is a larger rectangular section with a height of 32 inches. Dashed lines indicate the alignment and fit of the components.

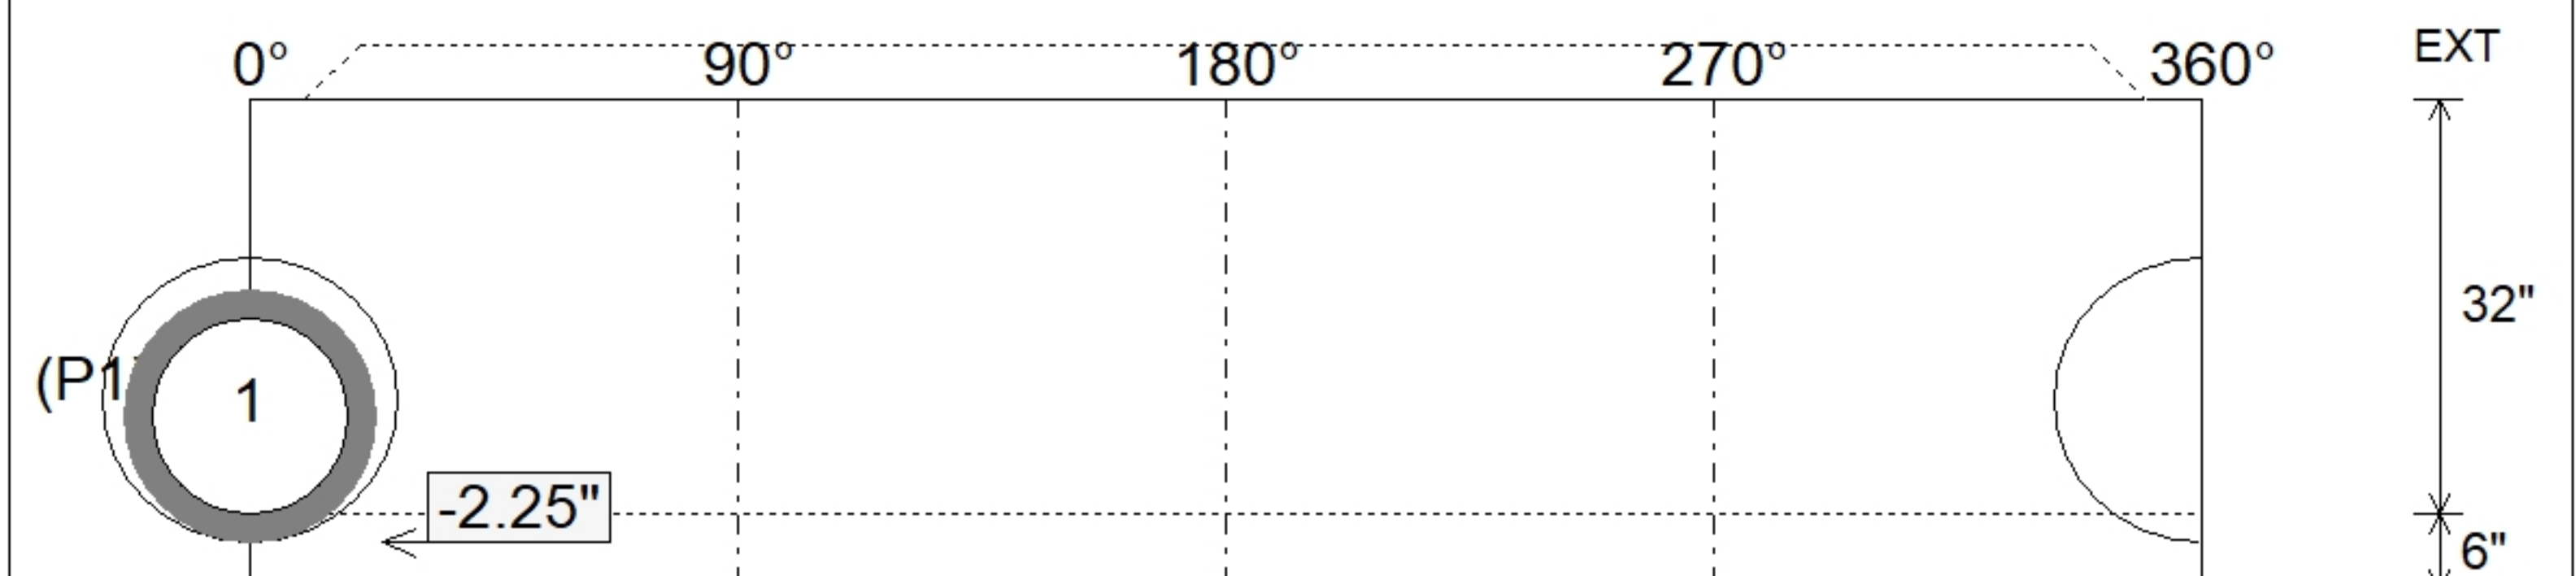

SUBMITTAL
APPROVED BY:
