

Contractor: RD Sitework LLC

TECH: Jared - F

Plant: 100



Size: 36" x 84"

Rim to Invert: 4.26'

Floor Height: 8"


Slack: 0.12"

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

P3) 24" x 36" - CASTING HEIGHT - 6"	0 lb
P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) - 8"	2911 lb
P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht - 37"	9991 lb
1) SECONDARY POUR - WALLS	0 lb
1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H)	442 lb
1) 36" x 84" - Conseal CS-102 1.00"	0 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb


Structure Total: 13344 lb

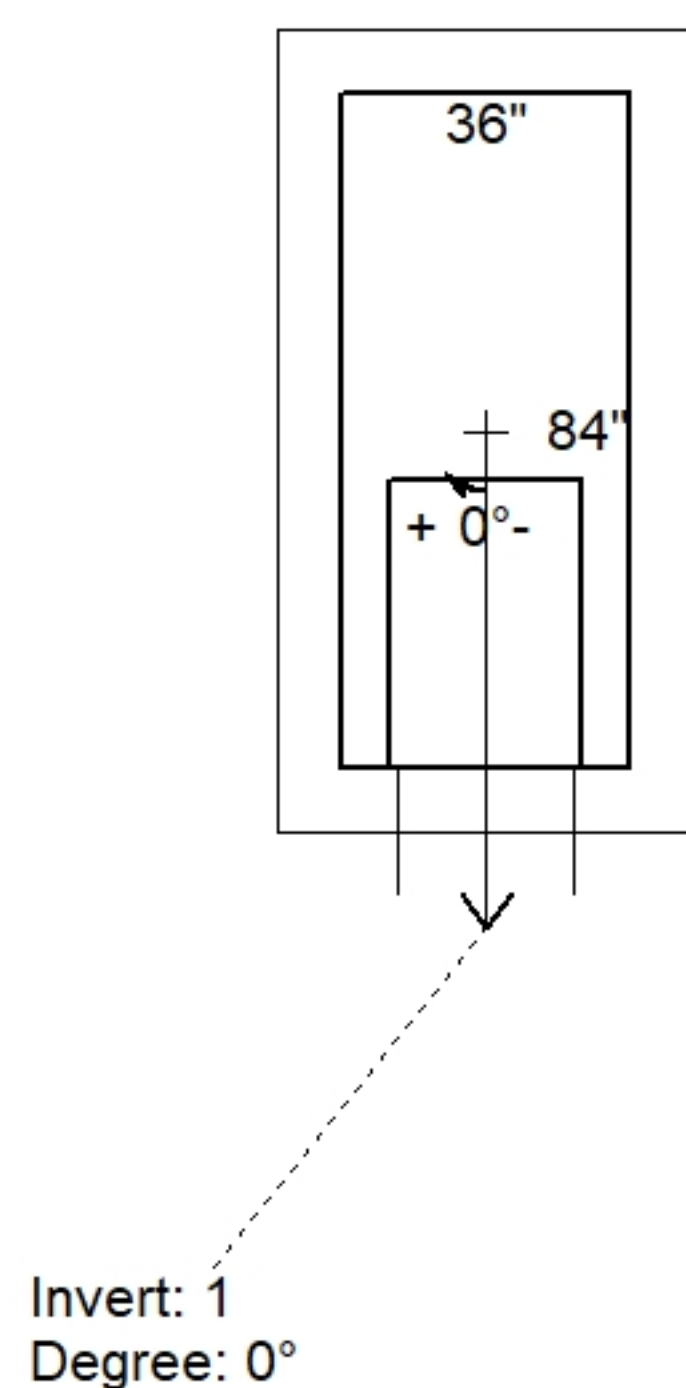

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	696.86'							
Reducer								
Invert 1	692.6'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

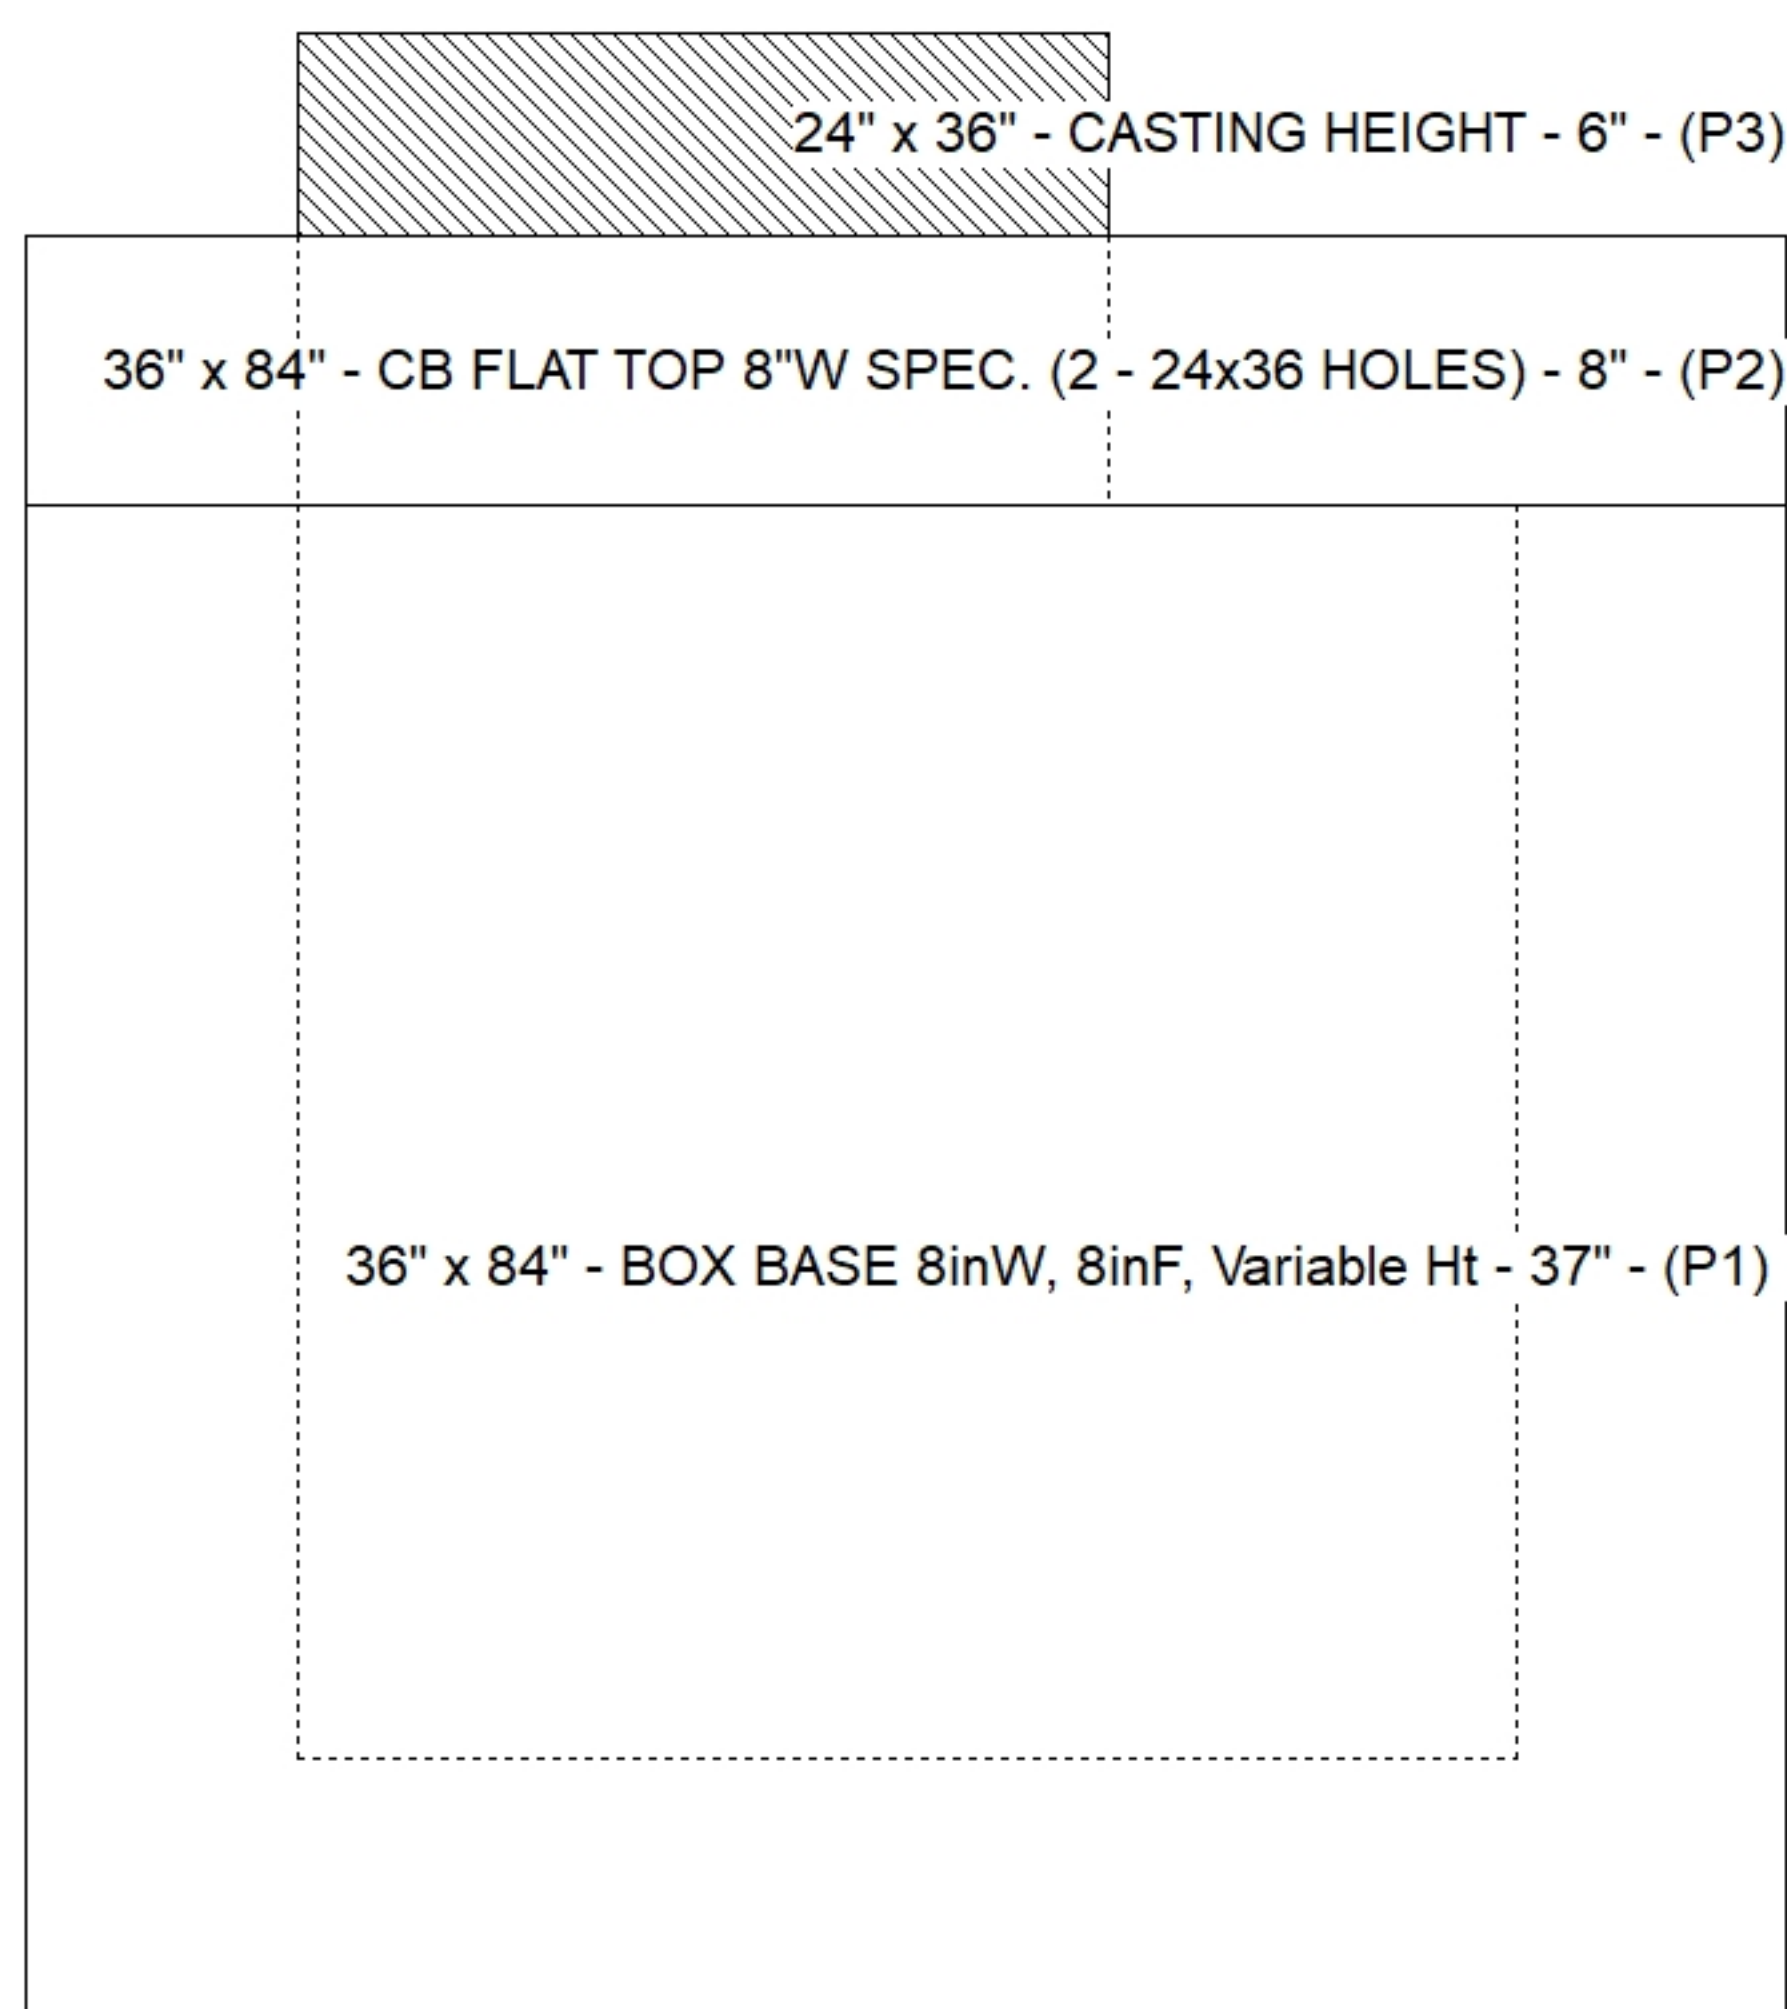

Default - Interior Dimensions

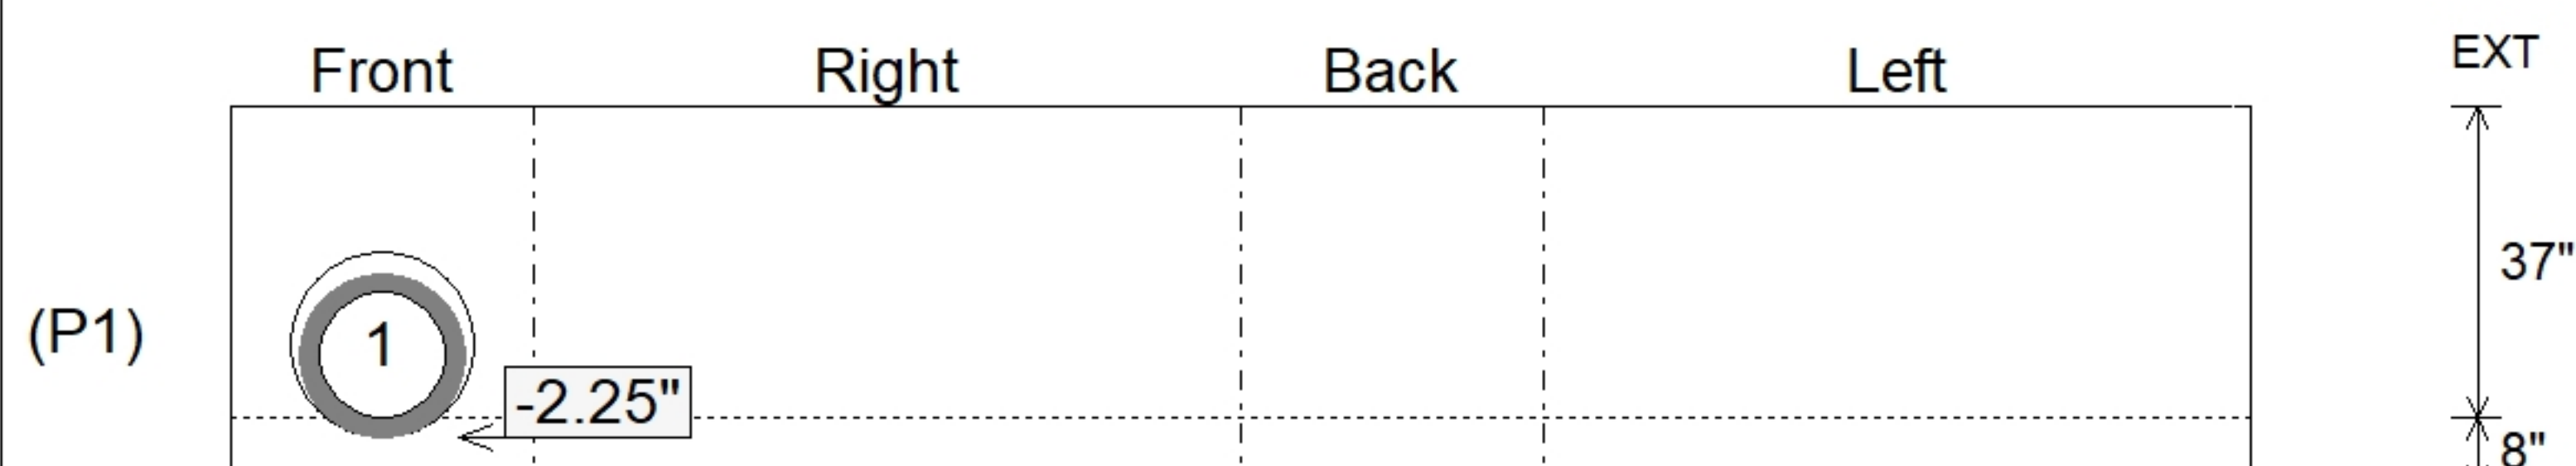

Submittal Drawing
6/8/2026 12:39:04 PM

SUBMITTAL
APPROVED BY:
