


Contractor: RD Sitework LLC

Plant: 100



Slack: 0.92"

Structure Total:	5095 lb
------------------	---------

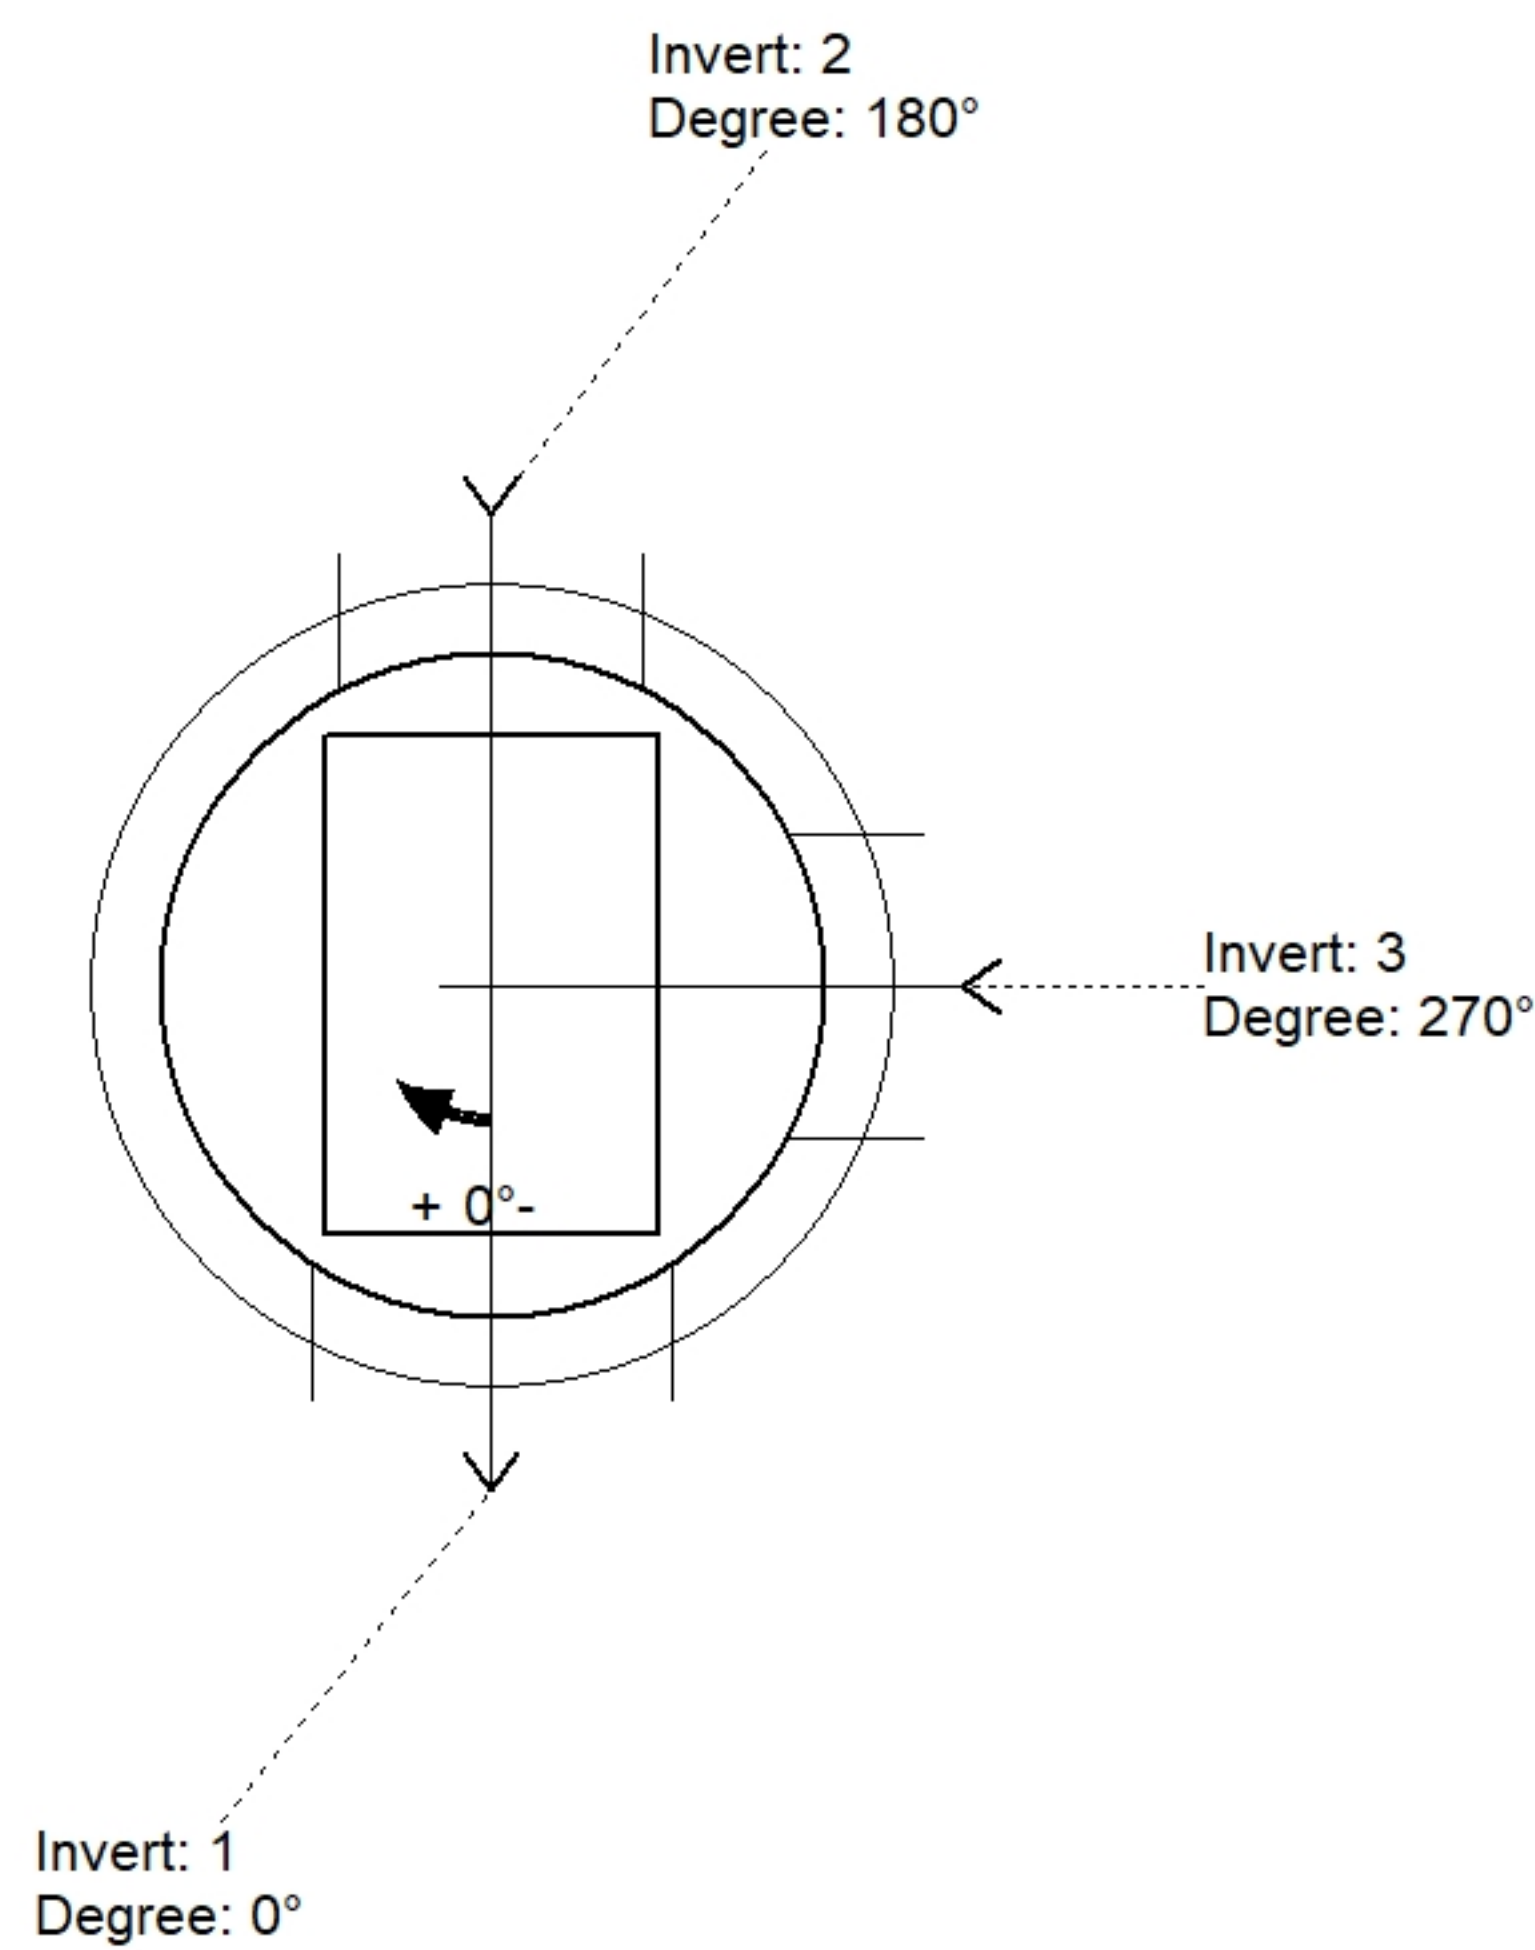


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	710.99'							
Reducer								
Invert 1	706.33'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	706.33'	180°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3	706.33'	270°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 12" - (P2)

48" - MH BASE Custom Ht - 37" - (P1)

The diagram illustrates a manhole assembly with three distinct parts. At the top is a rectangular casting, shaded with diagonal lines, measuring 24 inches by 36 inches with a height of 6 inches, labeled (P3). Below this is a flat top section, 48 inches wide, featuring a central rectangular hole that matches the casting's dimensions (24 inches by 36 inches). This section has a height of 12 inches and is labeled (P2). The bottom section is the manhole base, also 48 inches wide, with a custom height of 37 inches, labeled (P1). Dashed lines indicate the alignment and fit between the components.

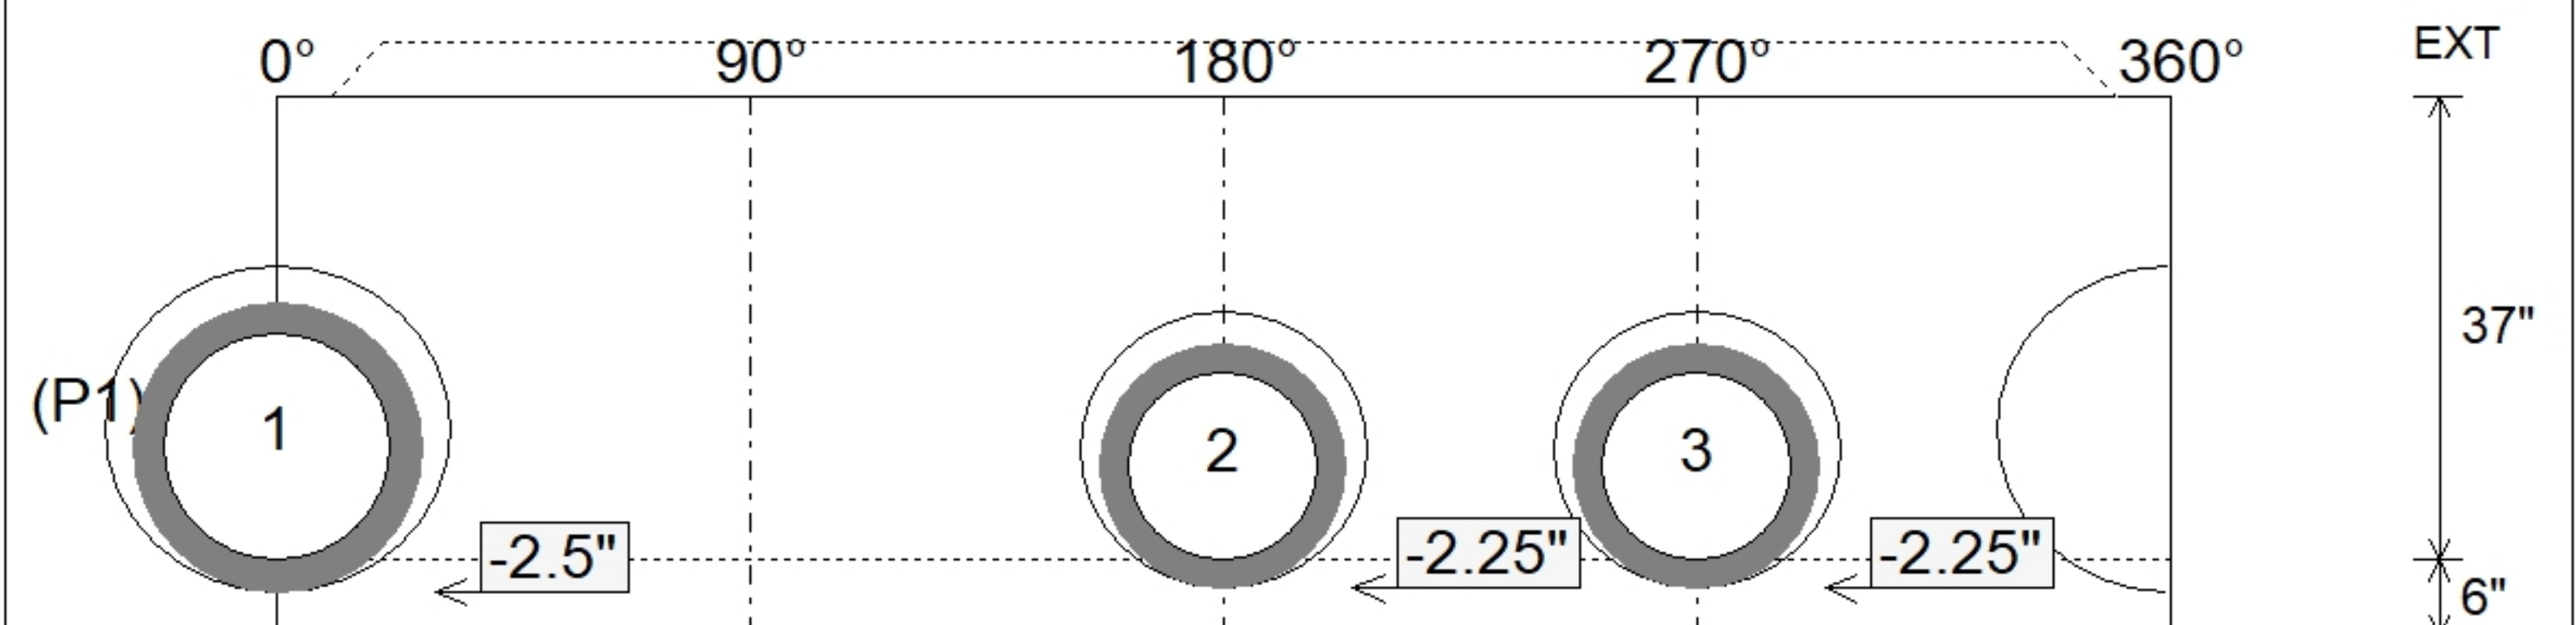

SUBMITTAL
APPROVED BY:
