

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100
7/10/2026 10:21:01 AM

Tech: Jared - F
PC: E. Bardley



Structure ID: QL70-2 POND1

P1 BX4848-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 48" x 48" - BX FLAT LID 8inW w/CC 24"x24" HOLE - 8"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 36"
1) CASTING - HOE-326-BH F/G
1) 48" x 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 0

Structure Notes:
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE-326-BH F/G OR EJ 6626).
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Structure Total:




0 lb
2363 lb
8163 lb
289 lb
0 lb
0 lb
0 lb
10815 lb

Rim: 652' Rim to Invert: 4' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	648'	0°	32"	0" No Hole	0.01"	Hole 0	0"	0"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

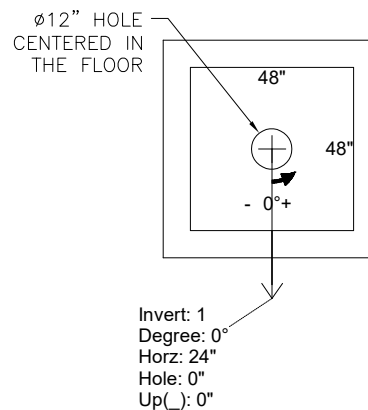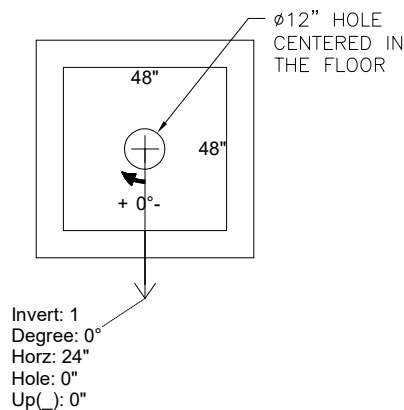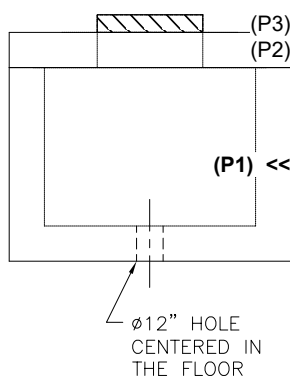

INSIDE WALL DIMENSIONS

(P1)



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 8163 lb
Volume (Net): 2.08cu.yd
