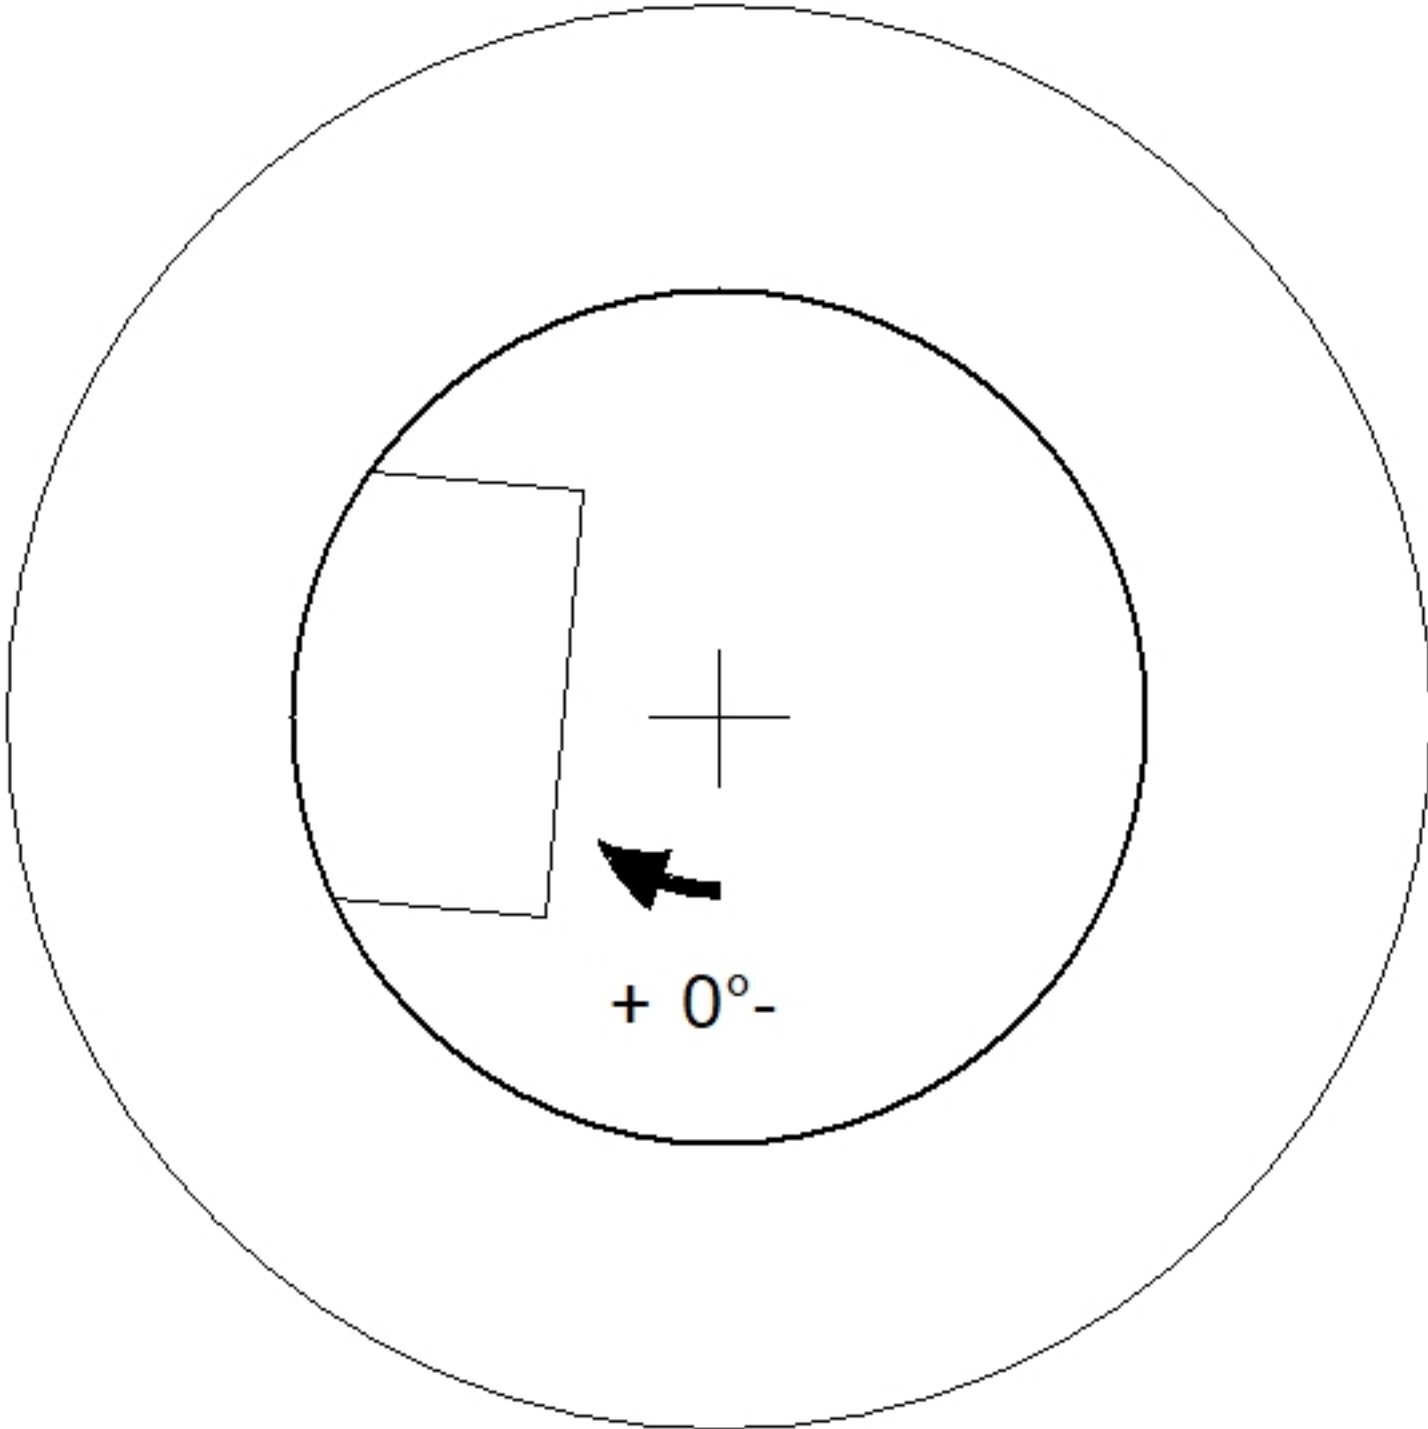


Job Name: 26-1952 - HCWD 2 Fire Station Sanitary Sewer Extension Job Location: Glendale, KY Contractor: Phillips Bros. Construction, LLC		Plant: 100 5/27/2026 10:50:14 AM	Tech: J. Horsley PC: T. Ryan	
Structure ID: A SS-MHD				
P5 GR4CDARED		GRADE RING w/ConBlock-CDA Red F/F		
P6) 24" - CASTING HEIGHT - 7" P5) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P4) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 12" P3) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 48" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Elbow - 8" PVC 1) Drop Tee - 8" PVC 9) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 1580 lb 2491 lb 3353 lb 3354 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 8 lb 0 lb 0 lb 0 lb ----- 12754 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-315 F/C SANITARY). 4. EXTERERIOR DROPE ASSEMBLY AT 190° . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
24" - GRADE RING w/ConBlock-CDA Red F/F - 4" - (P5)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 4"	Weight (Net): 270 lb Volume (Net): 0.07cu.yd
