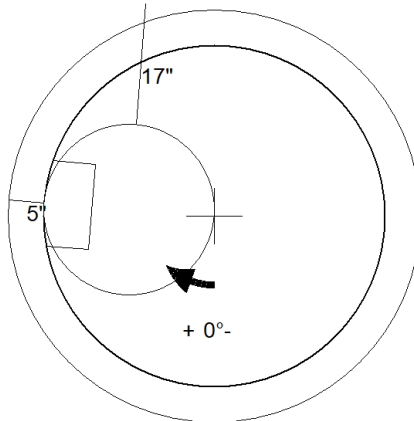



Job Name: 26-1952 - HCWD 2 Fire Station Sanitary Sewer Extension		Plant: 100	Tech: J. Horsley	
Job Location: Glendale, KY		5/20/2026 3:40:56 PM	PC: T. Ryan	
Contractor: Phillips Bros. Construction, LLC				
Structure ID: B SS-MHD				
P3	MH048CN36CDARED	ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P5) 24" - CASTING HEIGHT - 7"		0 lb	Structure Notes:	
P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3"		202 lb	1. PER ASTM C478 SPECIFICATIONS.	
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36"		2251 lb	2. CONCRETE = 4,000 PSI AT 28 DAYS.	
P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60"		4192 lb	3. CASTING BY OTHERS (HOE MC-315 F/C SANITARY)	
P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 48"		4604 lb	4. EXTERIOR DROP ASSEMBLY AT 189°.	
1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212		0 lb	.	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)		0 lb	REINFORCING PER ASTM A615 (GRADE 60).	
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT		1440 lb	- CONE (As .12)	
1) CASTING - HOE MC-315 F/C Sanitary		258 lb	- RISER/WALLS (As .12)	
2) 48" - Conseal CS-102 1.00" (Double)		0 lb	- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
2) 24" - Conseal CS-102 1.00" (Double)		1 lb		
1) A-Lok - 0285		0 lb		
1) Drop Elbow - 8" PVC		0 lb		
1) Drop Tee - 8" PVC		0 lb		
12) MH Step ML-10-TDS-NCR - 10"		0 lb		
Structure Total:		12948 lb		
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
