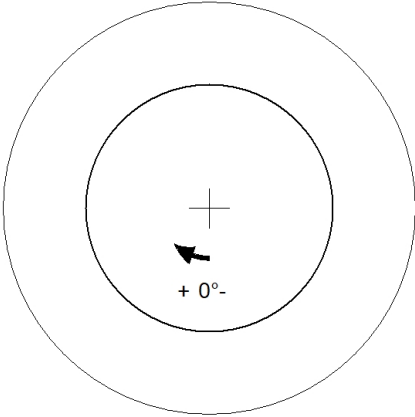


Job Name: 26-1952 - HCWD 2 Fire Station Sanitary Sewer Extension Job Location: Glendale, KY Contractor: Phillips Bros. Construction, LLC		Plant: 100 5/20/2026 3:40:56 PM	Tech: J. Horsley PC: T. Ryan	
Structure ID: B SS-MHD				
P4 GR3CDARED		GRADE RING w/ConBlock-CDA Red F/F		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 48" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 0285 1) Drop Elbow - 8" PVC 1) Drop Tee - 8" PVC 12) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 2251 lb 4192 lb 4604 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 1 lb 0 lb 0 lb 0 lb Structure Total: 12948 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-315 F/C SANITARY) 4. EXTERIOR DROP ASSEMBLY AT 189°. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
24" - GRADE RING w/ConBlock-CDA Red F/F - 3" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb Volume (Net): 0.05cu.yd
