

Job Name: 26-1987 Project Nova
Job Location: 200 South, IN 47882
Contractor: McCreary Concrete Products, Inc

Plant: 100
8/7/2026 9:24:04 AM

Tech: Jared - A
PC: Jay Ross Jarvis




Structure ID: STMH-1209A

P2 MH108RS96MH RISER

P6) 24" x 36" - CASTING HEIGHT - 6" P5) 108" - MH FLAT TOP w/24" X 36" HOLE - 17" P4) 108" - MH RISER - 54" P3) 108" - MH RISER - 54" P2) 108" - MH RISER - 96" P1) 108" - MH BASE - 96" 4) 108" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 75 1) Hole - 62 26) MH Step ML-10-TDS-NCR - 10"	0 lb 12900 lb 16798 lb 16798 lb 29863 lb 36119 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 112477 lb	Structure Notes: . **INDOT STATE PROJECT** 1. INDOT MH TYPE M / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .30) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.
Rim: 512.46' Rim to Invert: 26.45' Slack: 0.4" Sump: 6" Step Position: 90°		

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

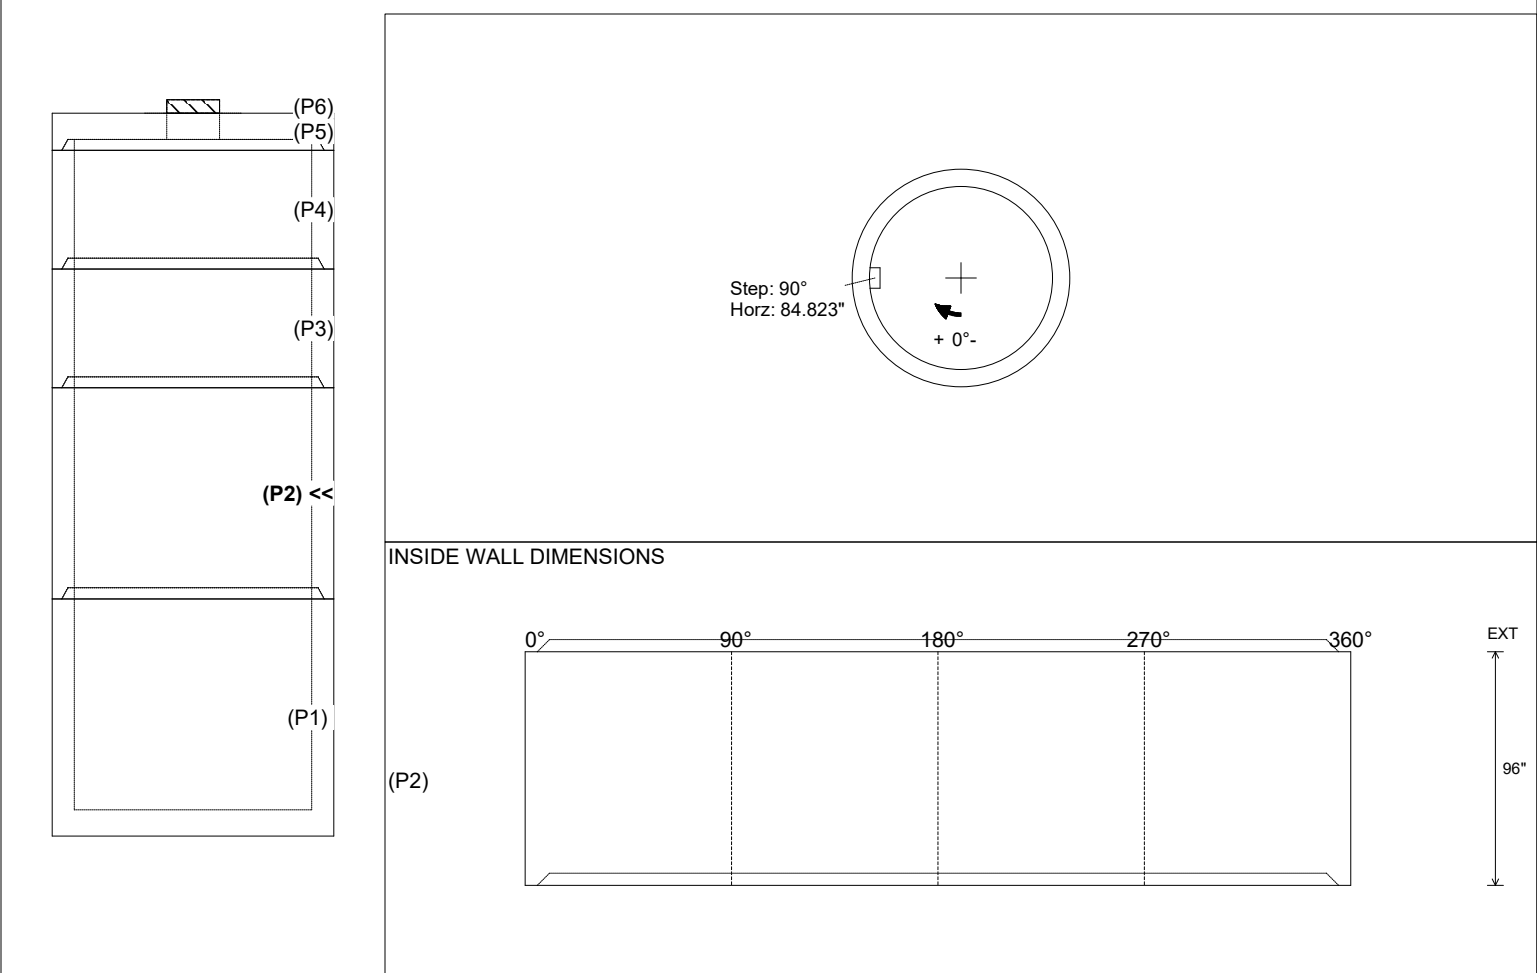

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 29863 lb Volume (Net): 7.63cu.yd
----------------------------------	------------------------------------	---	--	---
