


24" x 24" - CASTING HEIGHT - 0"					0 lb	Structure Notes: . **INDOT STATE PROJECT** 1. INDOT MH TYPE M / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .30) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W. 5. TOP SLAB IS ON HOLD 6. CASTING BY OTHERS
4) 108" - MH FLAT TOP w/24" X 24" HOLE - 17"					13190 lb	
3) 108" - MH RISER - 96"					29768 lb	
2) 108" - MH RISER - 96"					29863 lb	
1) 108" - MH BASE Custom Ht - 96"					30589 lb	
) 108" - Conseal CS-102 1.00"					0 lb	
) 24" x 24" - Conseal CS-102 1.00"					0 lb	
) Hole - 90					0 lb	
) Hole - 6					0 lb	
3) MH Step ML-10-TDS-NCR - 10"					0 lb	
Structure Total:					103409 lb	
Rim: 511.48'	Rim to Invert: 25.55'	Slack: 8.596"	Sump: 6.996"	Step Position: 65°		

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3	506.09'	0°	0"	4" HDPE	4.8"	Hole 6	6"	6.003"	51.516"	0"
Invert 4	506.09'	90°	100.531"	4" HDPE	4.8"	Hole 6	6"	6.003"	51.516"	0"
Invert 5	506.09'	180°	201.062"	4" HDPE	4.8"	Hole 6	6"	6.003"	51.516"	0"
Invert 6	506.09'	270°	301.593"	4" HDPE	4.8"	Hole 6	6"	6.003"	51.516"	0"
Invert 7										
Invert 8										

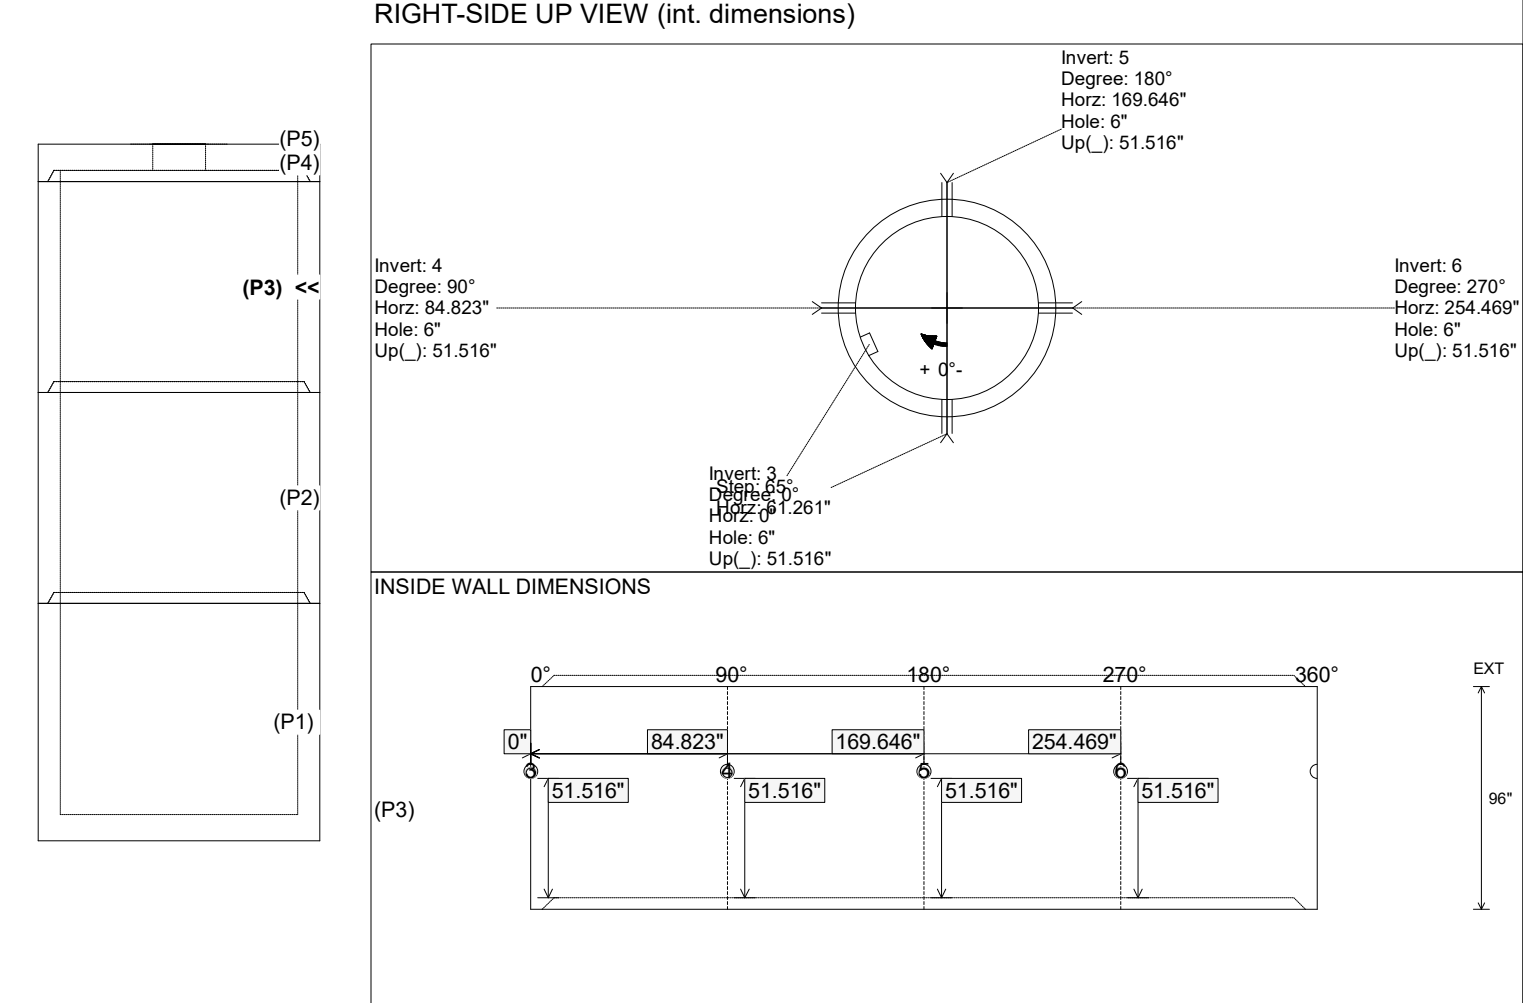

Coating (Int): Coating (Ext):		Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 29768 lb Volume (Net): 7.6cu.yd
---	--	---	--	---	---
