



Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:15:38 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: 1205											
P3 MH108RS54			MH RISER								
P5) 24" x 24" - CASTING HEIGHT - 0" P4) 108" - MH FLAT TOP w/24in X 24in ECC Hole - 17" P3) 108" - MH RISER - 54" P2) 108" - MH RISER - 54" P1) 108" - MH BASE - 90" 3) 108" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 68 1) Hole - 60 1) Hole - 34 4) Hole - 6 17) MH Step ML-10-TDS-NCR - 10"						0 lb 13186 lb 16703 lb 16798 lb 34433 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
Structure Total: 81120 lb											
Rim: 509.63' Rim to Invert: 17.47' Slack: 0.14" Sump: 5.5" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4	506.63'	45°	50.265"	4" HDPE	4.8"	Hole 6	6"	6.003"	29.74"	0"	
Invert 5	506.63'	135°	150.796"	4" HDPE	4.8"	Hole 6	6"	6.003"	29.74"	0"	
Invert 6	506.63'	225°	251.327"	4" HDPE	4.8"	Hole 6	6"	6.003"	29.74"	0"	
Invert 7	506.63'	315°	351.858"	4" HDPE	4.8"	Hole 6	6"	6.003"	29.74"	0"	
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

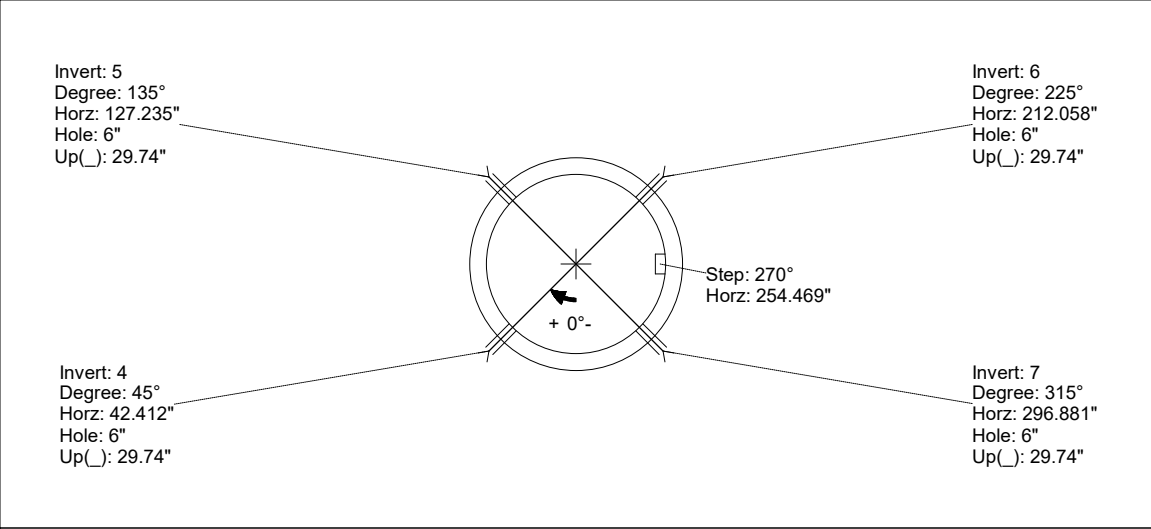

INSIDE WALL DIMENSIONS

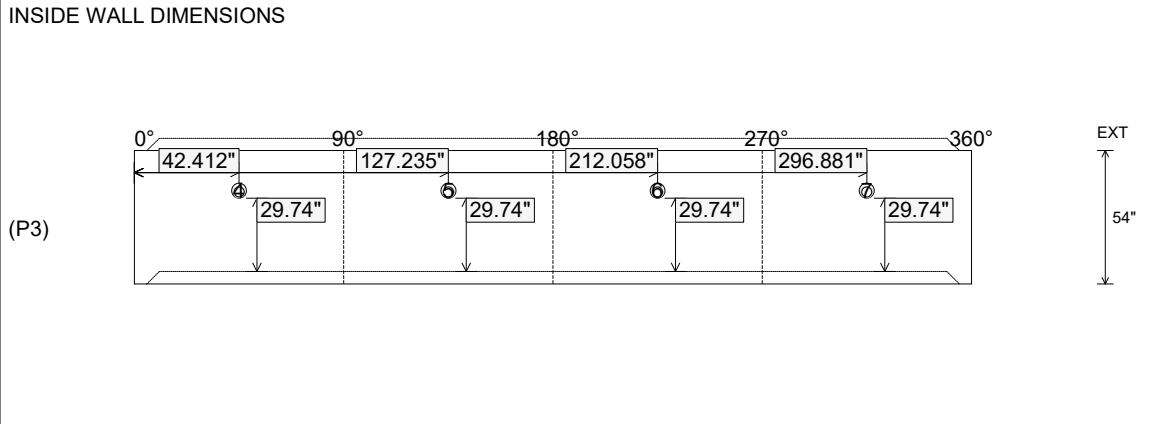

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 54" Height (Ext): 54"	Weight (Net): 16703 lb Volume (Net): 4.27cu.yd
----------------------------------	------------------------------------	---	--	---
