

Job Name: 26-1987P6 - Project Nova
Job Location: Sullivan, IN 47882
Contractor: McCreary Concrete Products, Inc.

Plant: Beaver Dam

9/29/2026 12:38:01 PM

Tech: J. Coppage

PC: M. Sullivan



Structure ID: 1303

P3 MH108RS48

MH RISER

P5) 24" - CASTING HEIGHT - 0"
P4) 108" - MH FLAT TOP w/24" ECC Hole - 17"
P3) 108" - MH RISER - 48"
P2) 108" - MH RISER - 60"
P1) 108" - MH BASE - 96"
3) 108" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
1) Hole - 68
1) Hole - 48
1) Hole - 34
4) Hole - 6
17) MH Step ML-10-TDS-NCR - 10"



0 lb
10472 lb
14836 lb
18664 lb
37227 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Notes: .
1. (CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Structure Total: 81200 lb


Rim: 512.24' Rim to Invert: 18.18' Slack: 2.66" Sump: 5.5" Step Position: 270°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	509.24'	45°	50.265"	4" HDPE	4.8"	Hole 6	6"	6.003"	26.26"	0"
Invert 5	509.24'	135°	150.796"	4" HDPE	4.8"	Hole 6	6"	6.003"	26.26"	0"
Invert 6	509.24'	225°	251.327"	4" HDPE	4.8"	Hole 6	6"	6.003"	26.26"	0"
Invert 7	509.24'	315°	351.858"	4" HDPE	4.8"	Hole 6	6"	6.003"	26.26"	0"
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

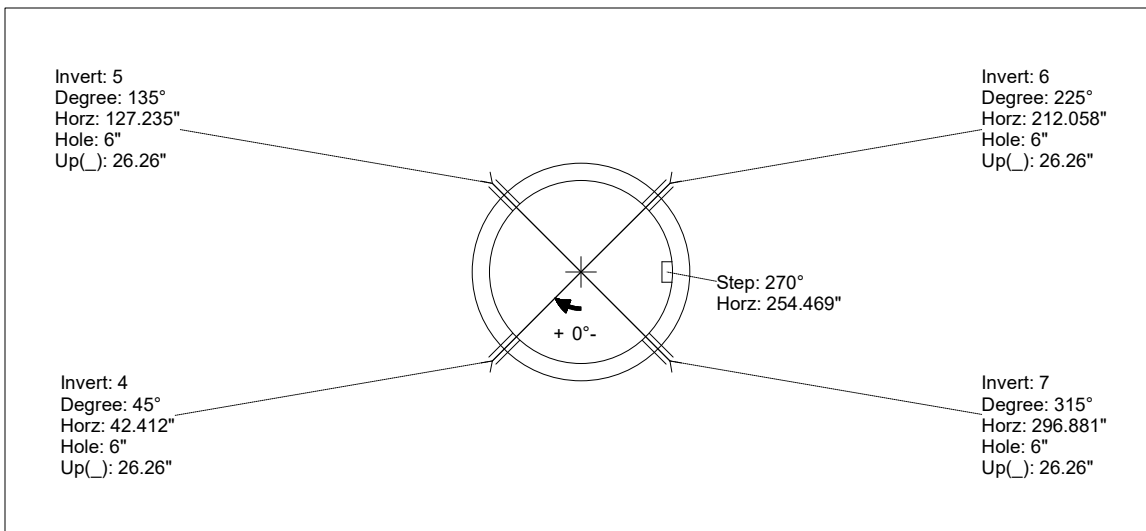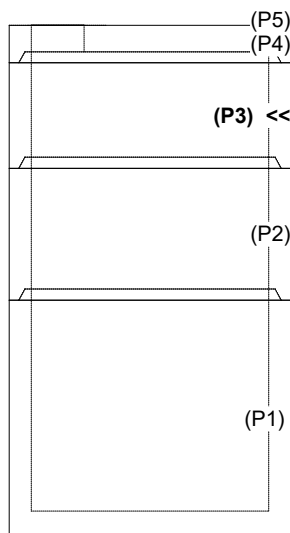

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 10"
Floor Height: 0"

Height (Int): 48"
Height (Ext): 48"

Weight (Net): 14836 lb
Volume (Net): 3.79cu.yd
