





Floor (Bot): 488.937'
Overall Height: 20.167'
Slack: 0.8"

Structure Total: 77824 lb

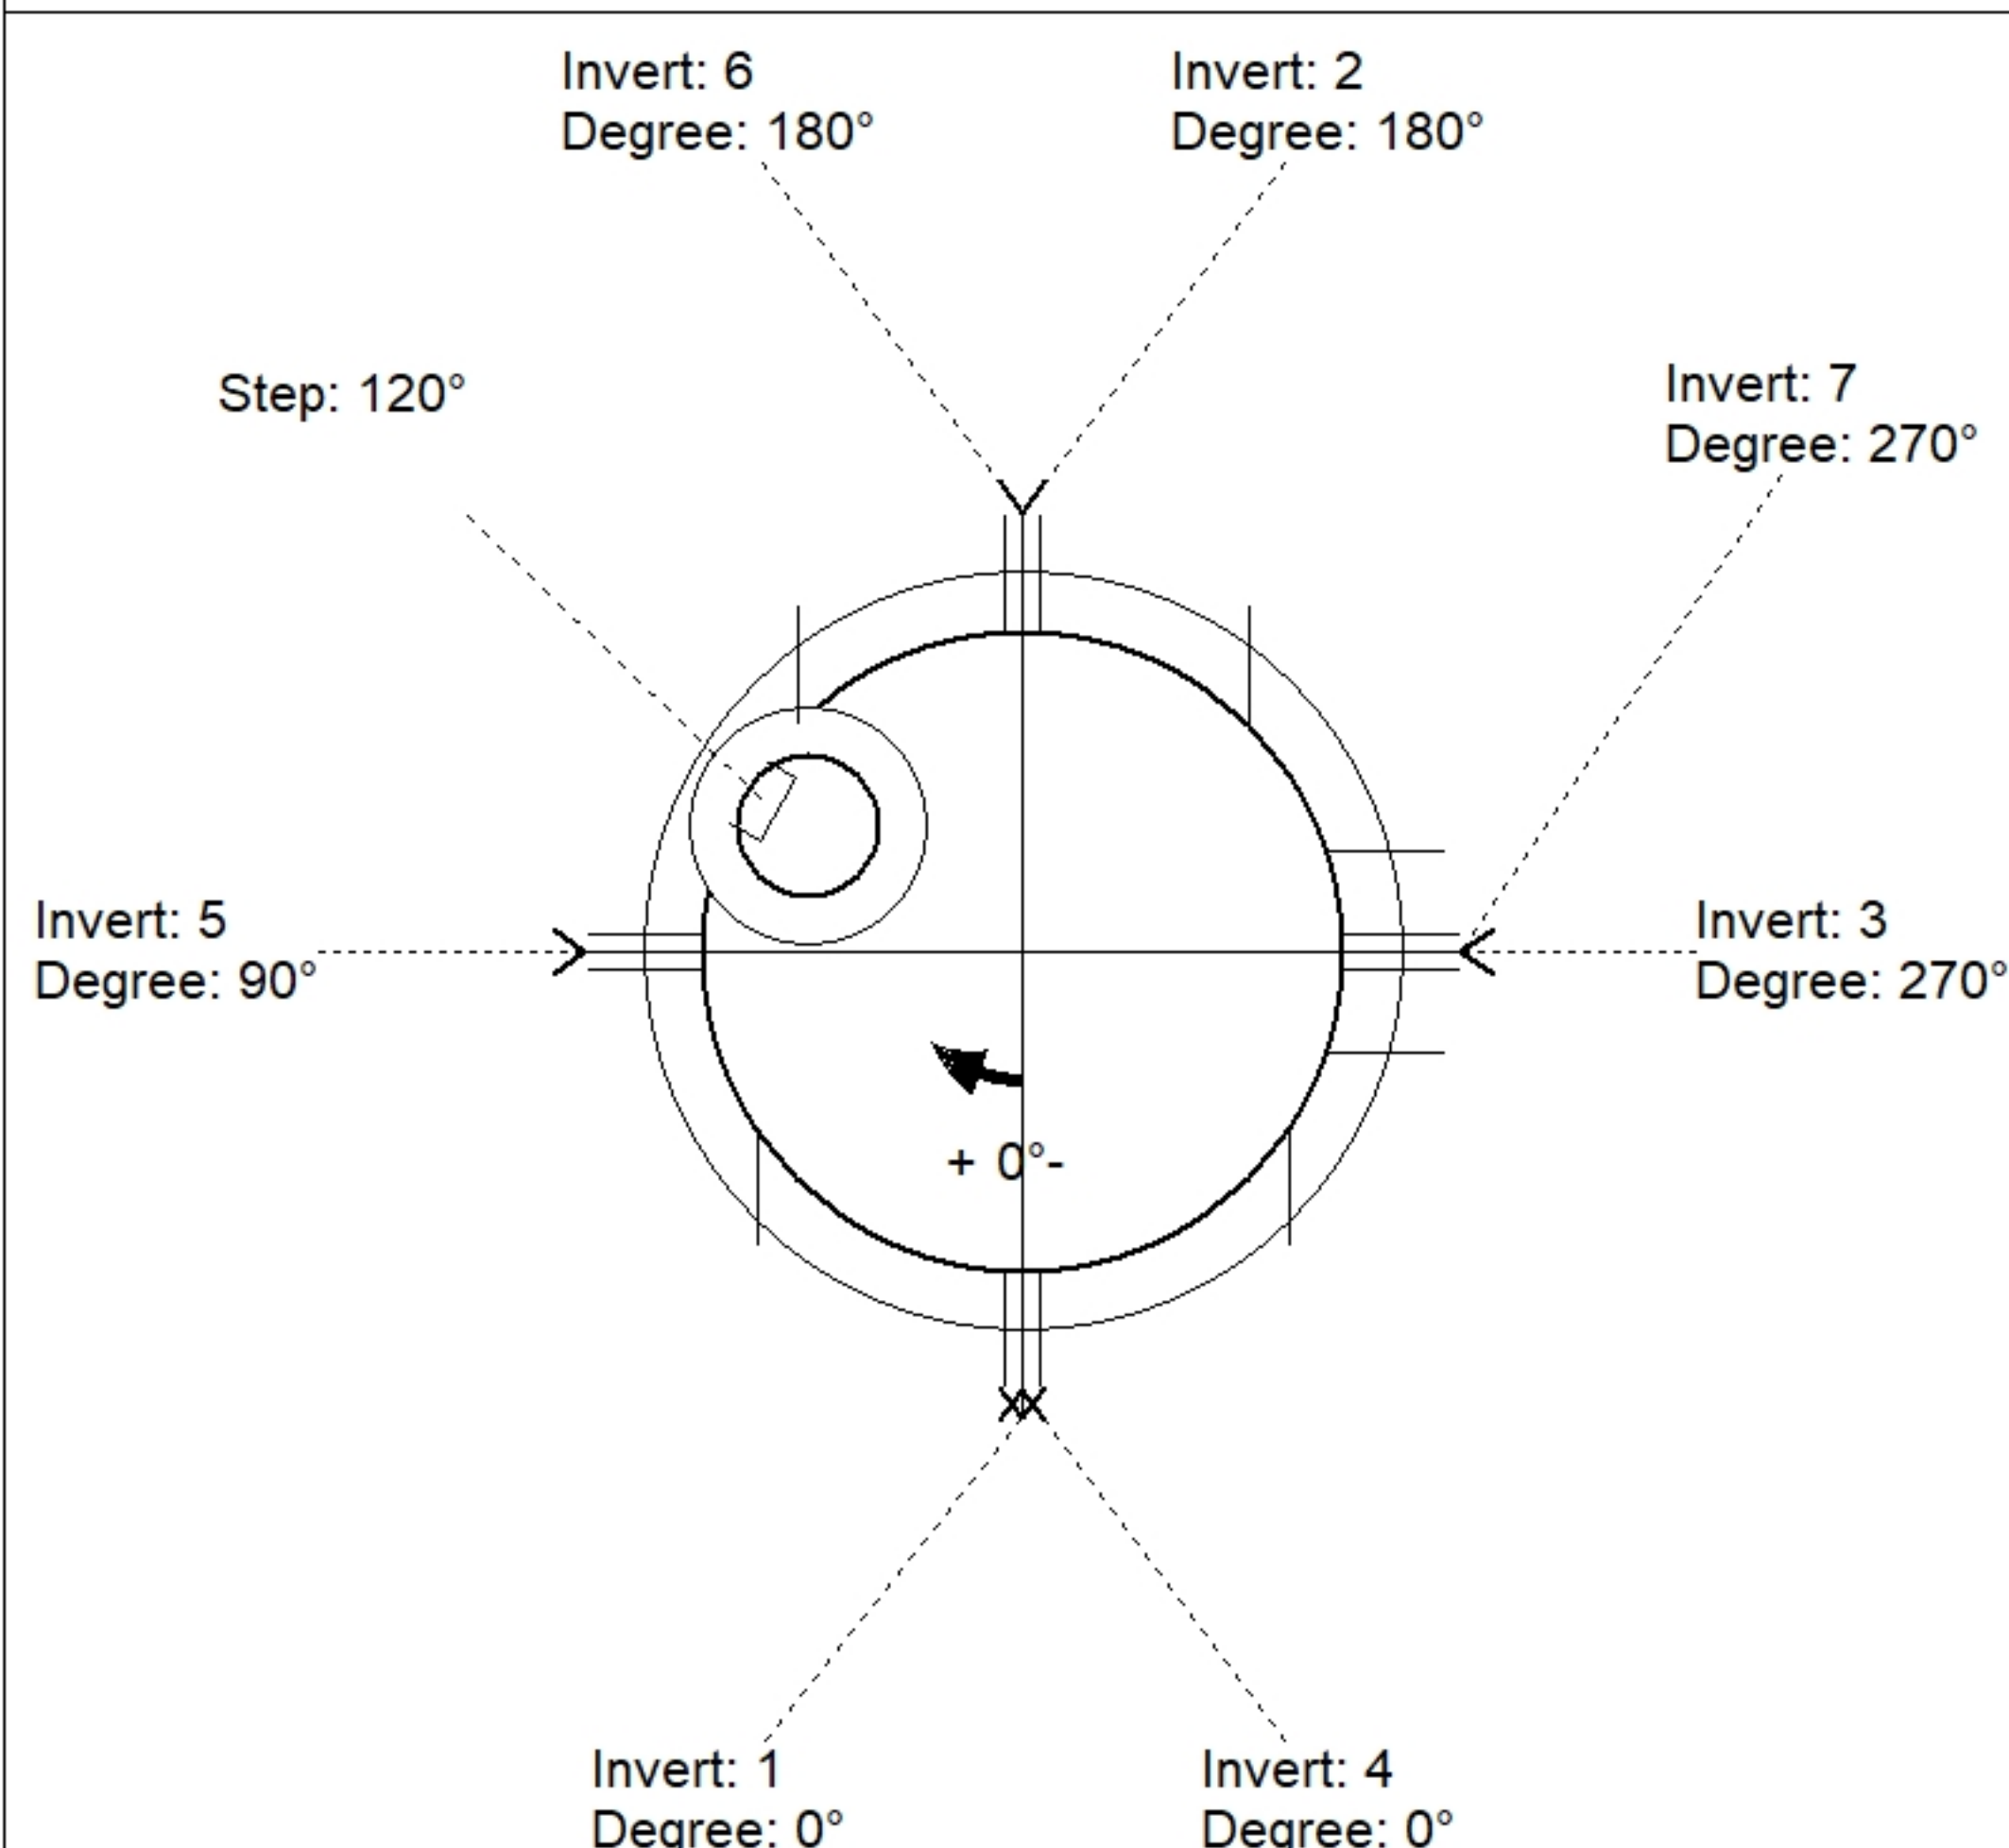

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	509.17'							
Reducer								
Invert 1	490.52'	0°	72" RCP B WALL	86"	90"	Hole 90	0"	P1
Invert 2	490.62'	180°	60" RCP B WALL	72"	76"	Hole 76	2.2"	P1
Invert 3	492.52'	270°	24" RCP B WALL	30"	34"	Hole 34	28"	P1
Invert 4	506.17'	0°	4" HDPE	4.8"	6"	Hole 6	33.4"	P3
Invert 5	506.17'	90°	4" HDPE	4.8"	6"	Hole 6	33.4"	P3
Invert 6	506.17'	180°	4" HDPE	4.8"	6"	Hole 6	33.4"	P3
Invert 7	506.17'	270°	4" HDPE	4.8"	6"	Hole 6	33.4"	P3
Invert 8								

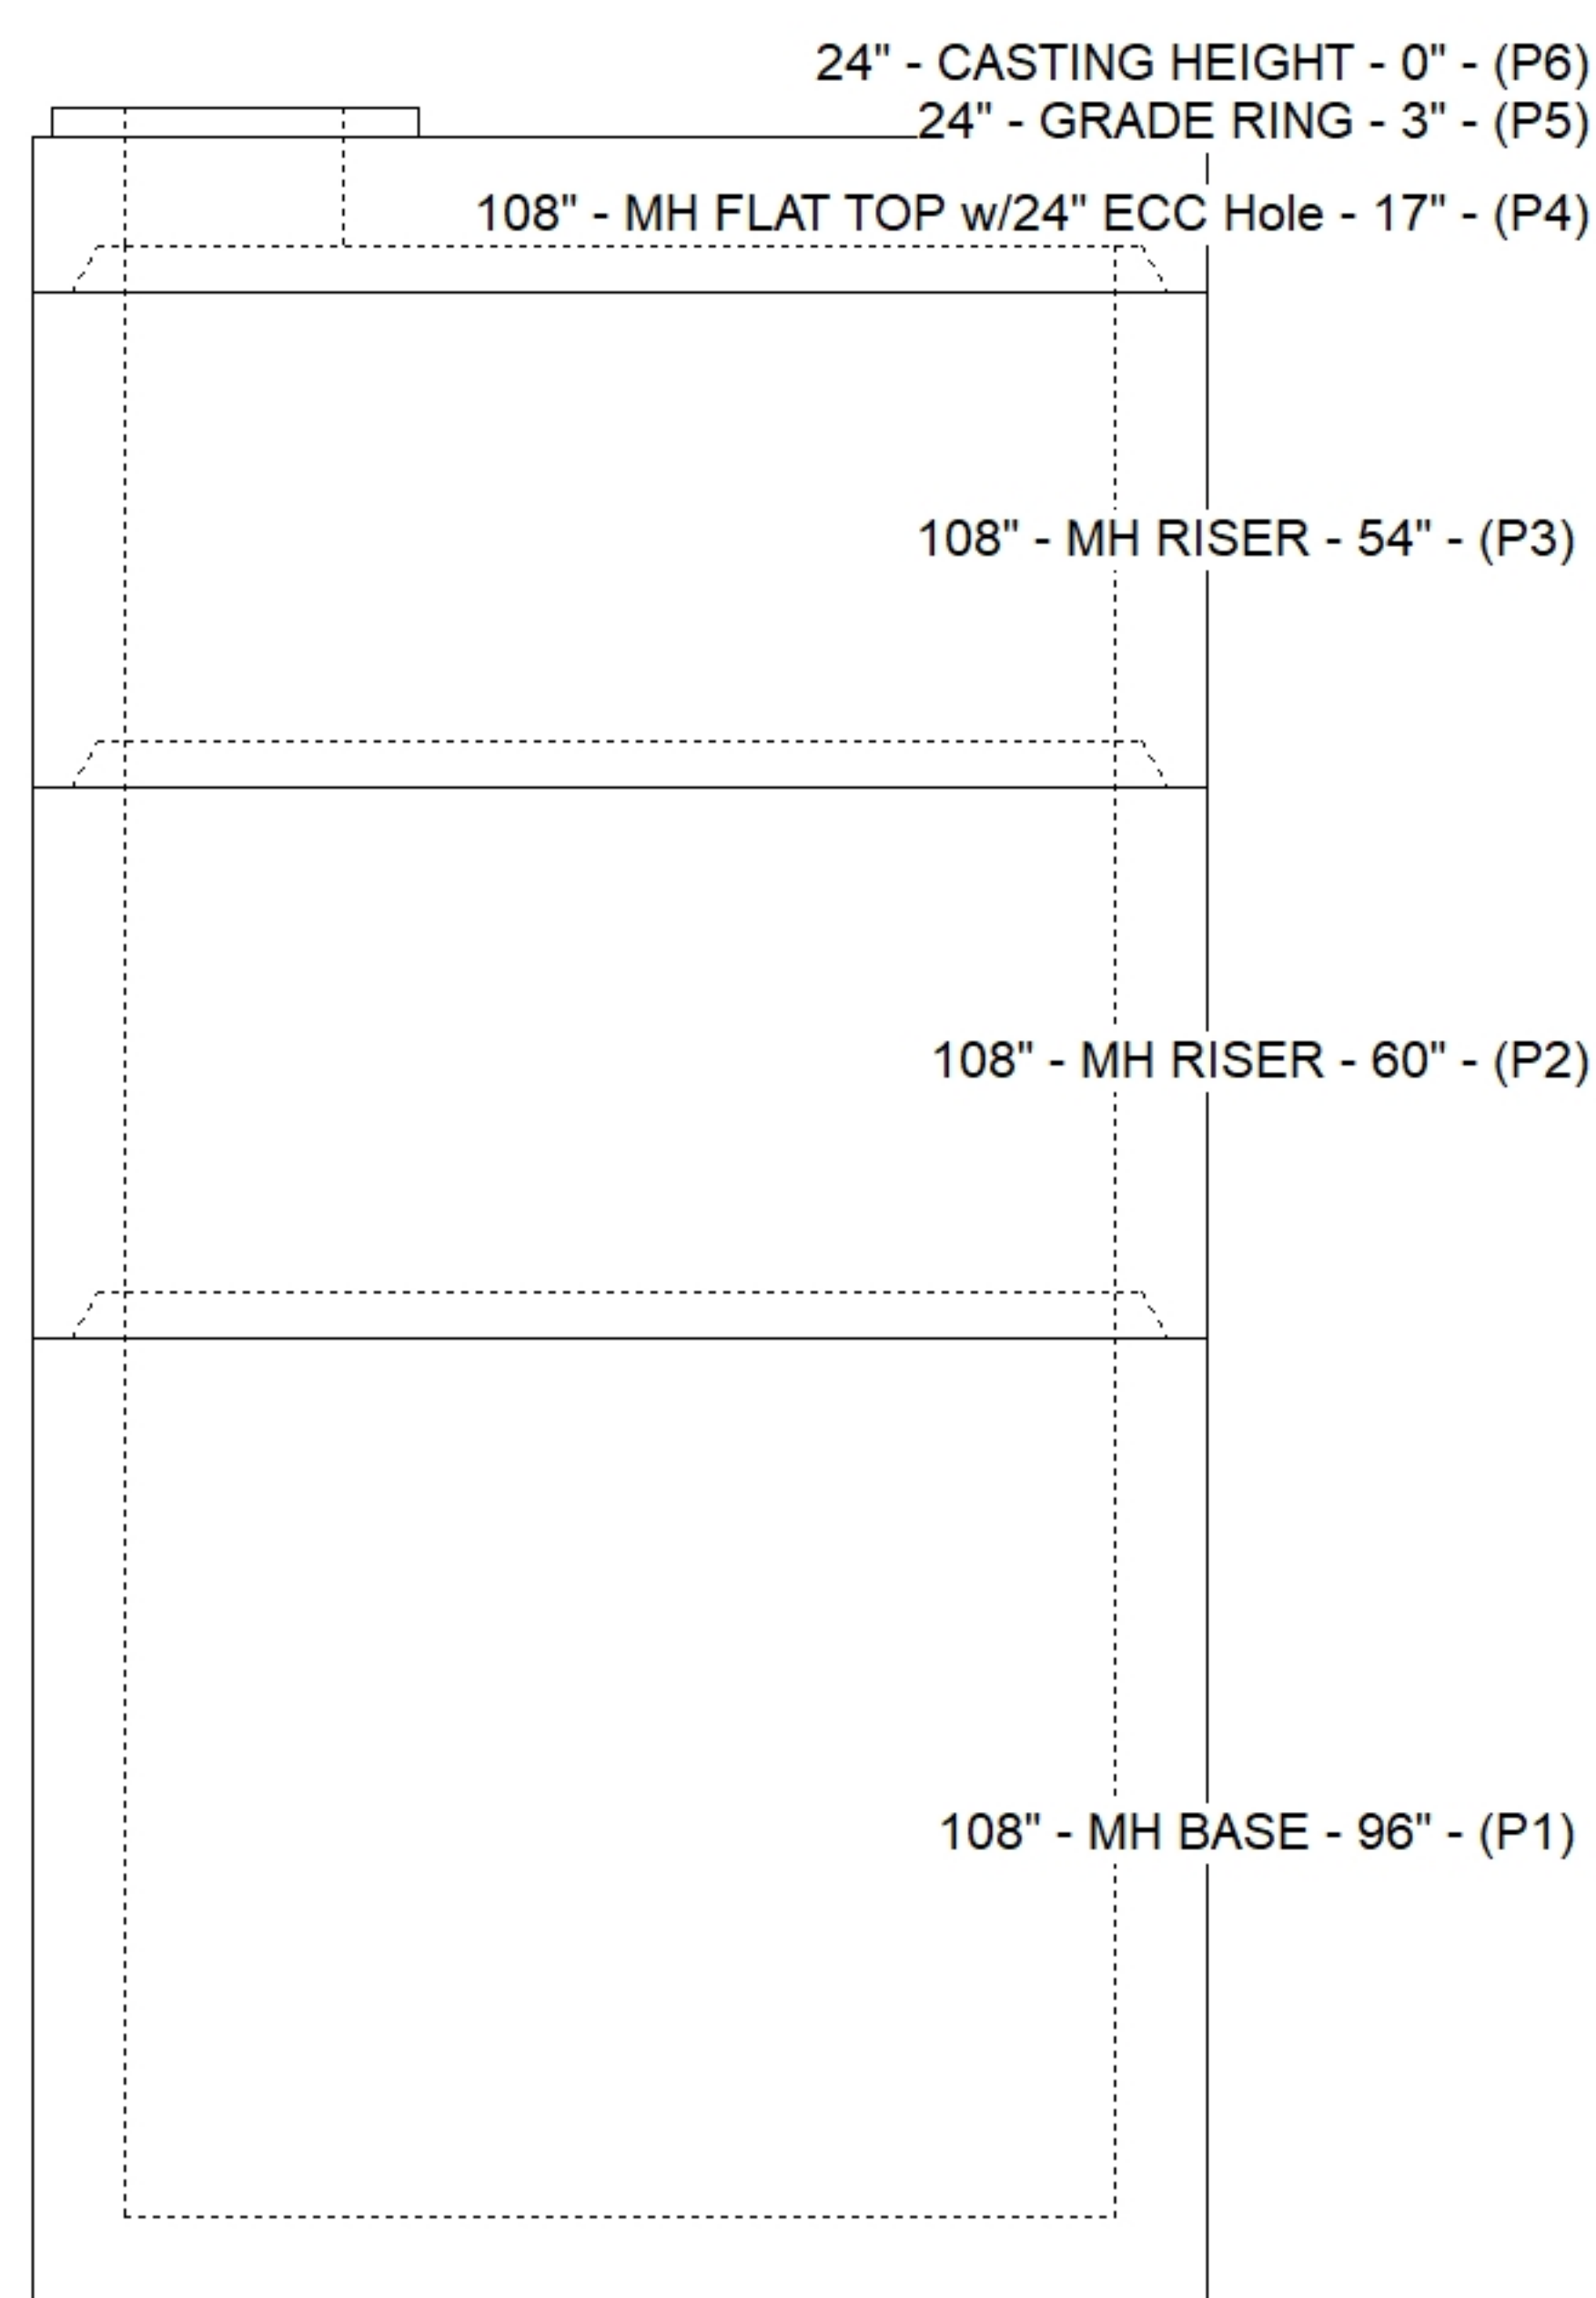

SUBMITTAL
APPROVED BY:
