



Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:15:52 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: 1411											
P3		MH108RS54		MH RISER							
P5) 24" - CASTING HEIGHT - 4" P4) 108" - MH FLAT TOP w/24" ECC Hole - 17" P3) 108" - MH RISER - 54" P2) 108" - MH RISER - 84" P1) 108" - MH BASE - 96" 3) 108" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 90 4) Hole - 6 19) MH Step ML-10-TDS-NCR - 10"						0 lb 10472 lb 16703 lb 26130 lb 30589 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 83894 lb		Structure Notes: 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.			
Rim: 510.67' Rim to Invert: 20.75' Slack: 1" Sump: 7" Step Position: 120											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3	507.67'	0°	0"	4" HDPE	4.8"	Hole 6	6"	6.003"	34.6"	0"	
Invert 4	507.67'	90°	100.531"	4" HDPE	4.8"	Hole 6	6"	6.003"	34.6"	0"	
Invert 5	507.67'	180°	201.062"	4" HDPE	4.8"	Hole 6	6"	6.003"	34.6"	0"	
Invert 6	507.67'	270°	301.593"	4" HDPE	4.8"	Hole 6	6"	6.003"	34.6"	0"	
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

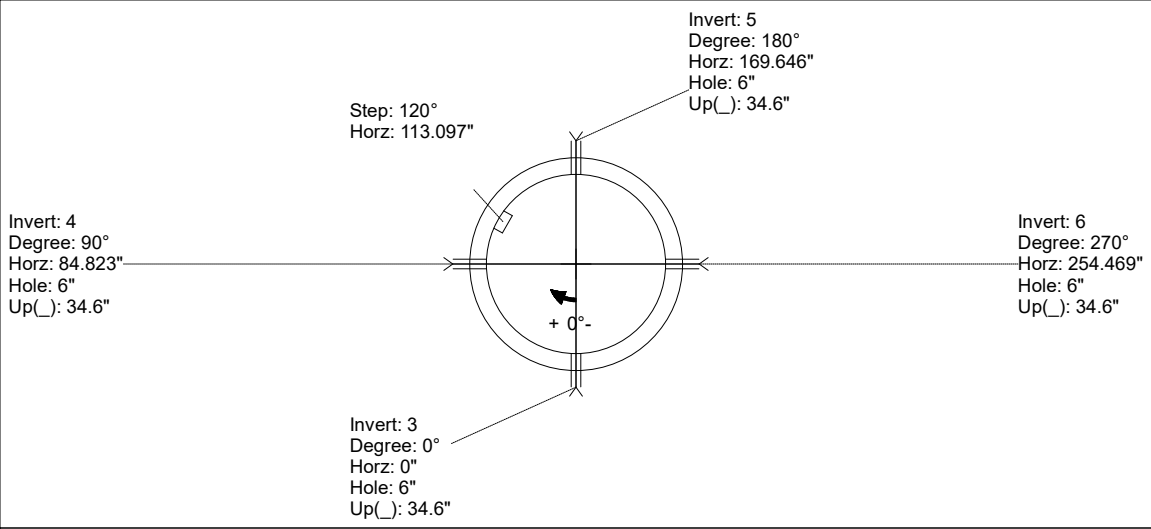

INSIDE WALL DIMENSIONS

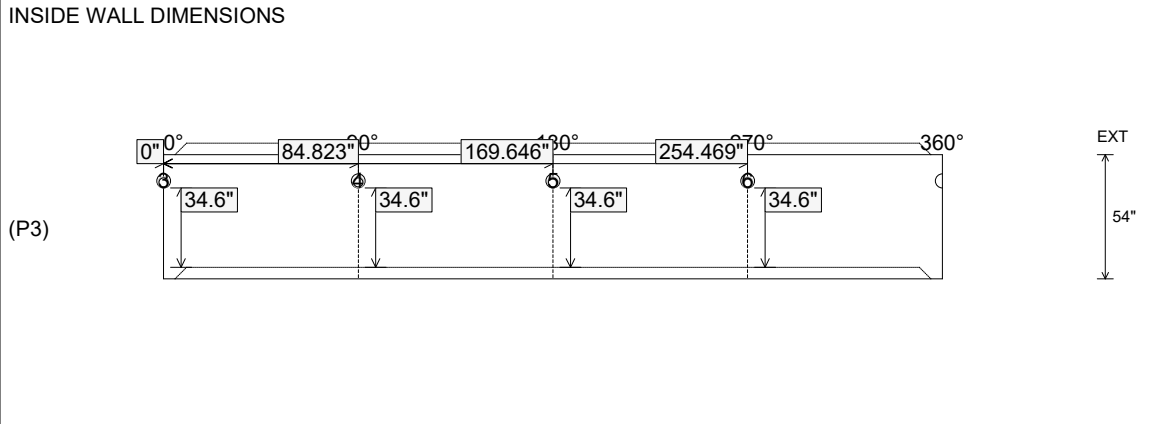

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 10" Floor Height: 0"	Height (Int): 54" Height (Ext): 54"	Weight (Net): 16703 lb Volume (Net): 4.27cu.yd
----------------------------------	------------------------------------	---	--	---
