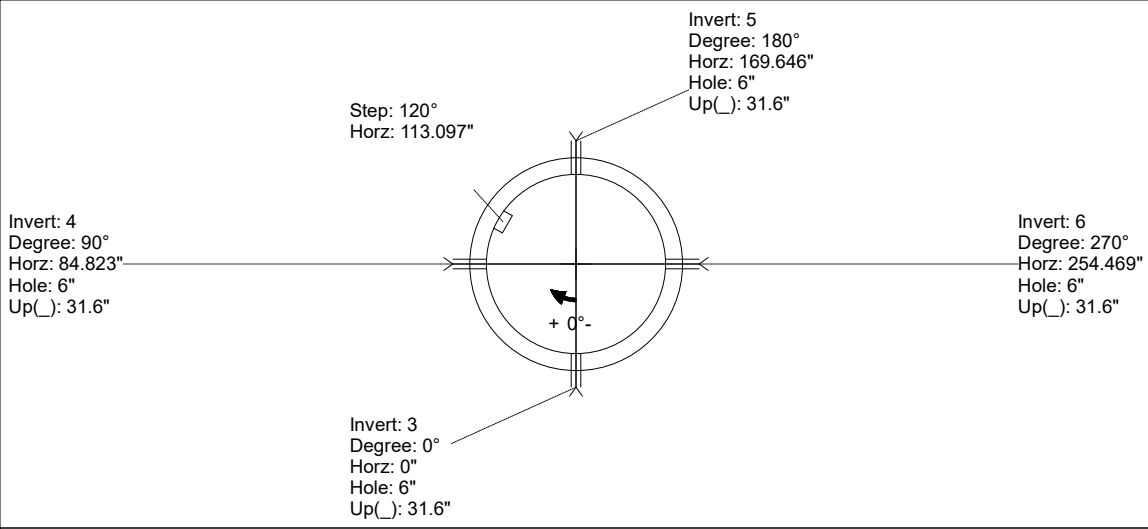
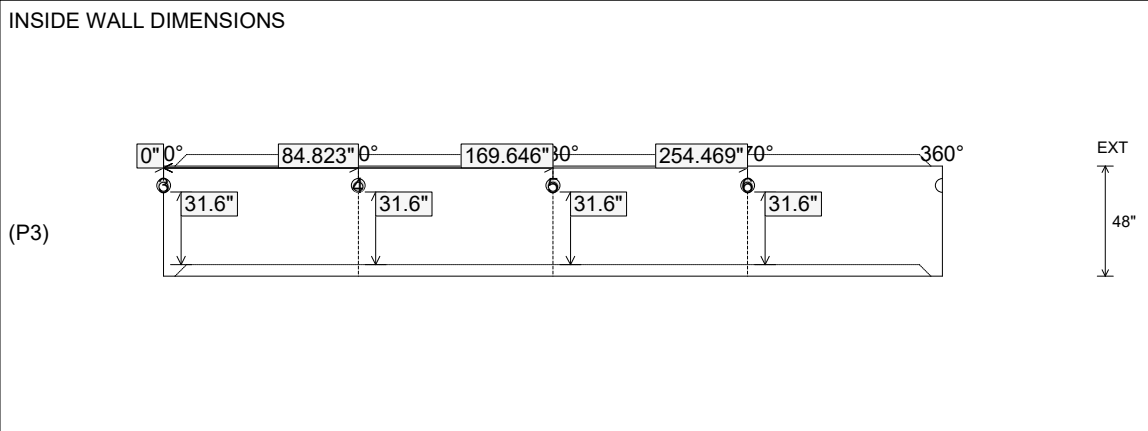


Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:15:51 PM		Tech: J. Coppage PC: M. Sullivan						
Structure ID: 1412													
P3 MH108RS48			MH RISER										
P6) 24" - CASTING HEIGHT - 4" P5) 24" - GRADE RING - 4" P4) 108" - MH FLAT TOP w/24" ECC Hole - 17" P3) 108" - MH RISER - 48" P2) 108" - MH RISER - 96" P1) 108" - MH BASE - 96" 3) 108" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 90 4) Hole - 6 19) MH Step ML-10-TDS-NCR - 10"						0 lb 270 lb 10472 lb 14836 lb 29863 lb 30589 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 86030 lb		Structure Notes: 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.					
Rim: 511.07' Rim to Invert: 21.5' Slack: 0" Sump: 7" Step Position: 120													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3	508.07'	0°	0"	4" HDPE	4.8"	Hole 6	6"	6.003"	31.6"	0"			
Invert 4	508.07'	90°	100.531"	4" HDPE	4.8"	Hole 6	6"	6.003"	31.6"	0"			
Invert 5	508.07'	180°	201.062"	4" HDPE	4.8"	Hole 6	6"	6.003"	31.6"	0"			
Invert 6	508.07'	270°	301.593"	4" HDPE	4.8"	Hole 6	6"	6.003"	31.6"	0"			
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 10" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 14836 lb Volume (Net): 3.79cu.yd				
