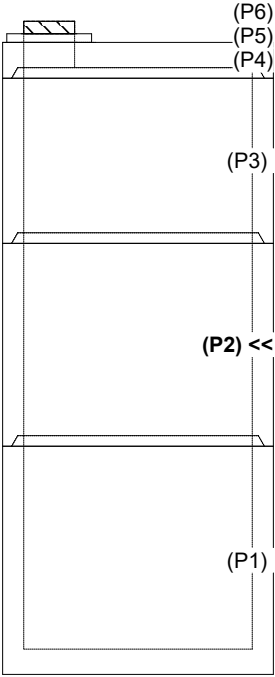


Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:15:48 PM		Tech: J. Coppage PC: M. Sullivan						
Structure ID: 1414													
P2		MH108RS96		MH RISER									
P6) 24" x 36" - CASTING HEIGHT - 6" P5) 24" x 36" - GRADE RING - 4" P4) 108" - MH FLAT TOP w/24in X 36in ECC Hole - 17" P3) 108" - MH RISER - 78" P2) 108" - MH RISER - 96" P1) 108" - MH BASE - 96" 3) 108" - Conseal CS-102 1.00" 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 90 4) Hole - 6 22) MH Step ML-10-TDS-NCR - 10"						0 lb 408 lb 12900 lb 24168 lb 29863 lb 30589 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 97928 lb		Structure Notes: . 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.					
Rim: 511.95' Rim to Invert: 24.24' Slack: 0.88" Sump: 7" Step Position: 120													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 10" Floor Height: 0"		Height (Int): 96" Height (Ext): 96"		Weight (Net): 29863 lb Volume (Net): 7.63cu.yd				
