

Contractor: Mechanical Consultants Inc

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 4.35'

Floor Height: 6"

Slack: 1.2"


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (HOE MC-375-SS F/C SELF-SEALING SANITARY).

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 6867 lb

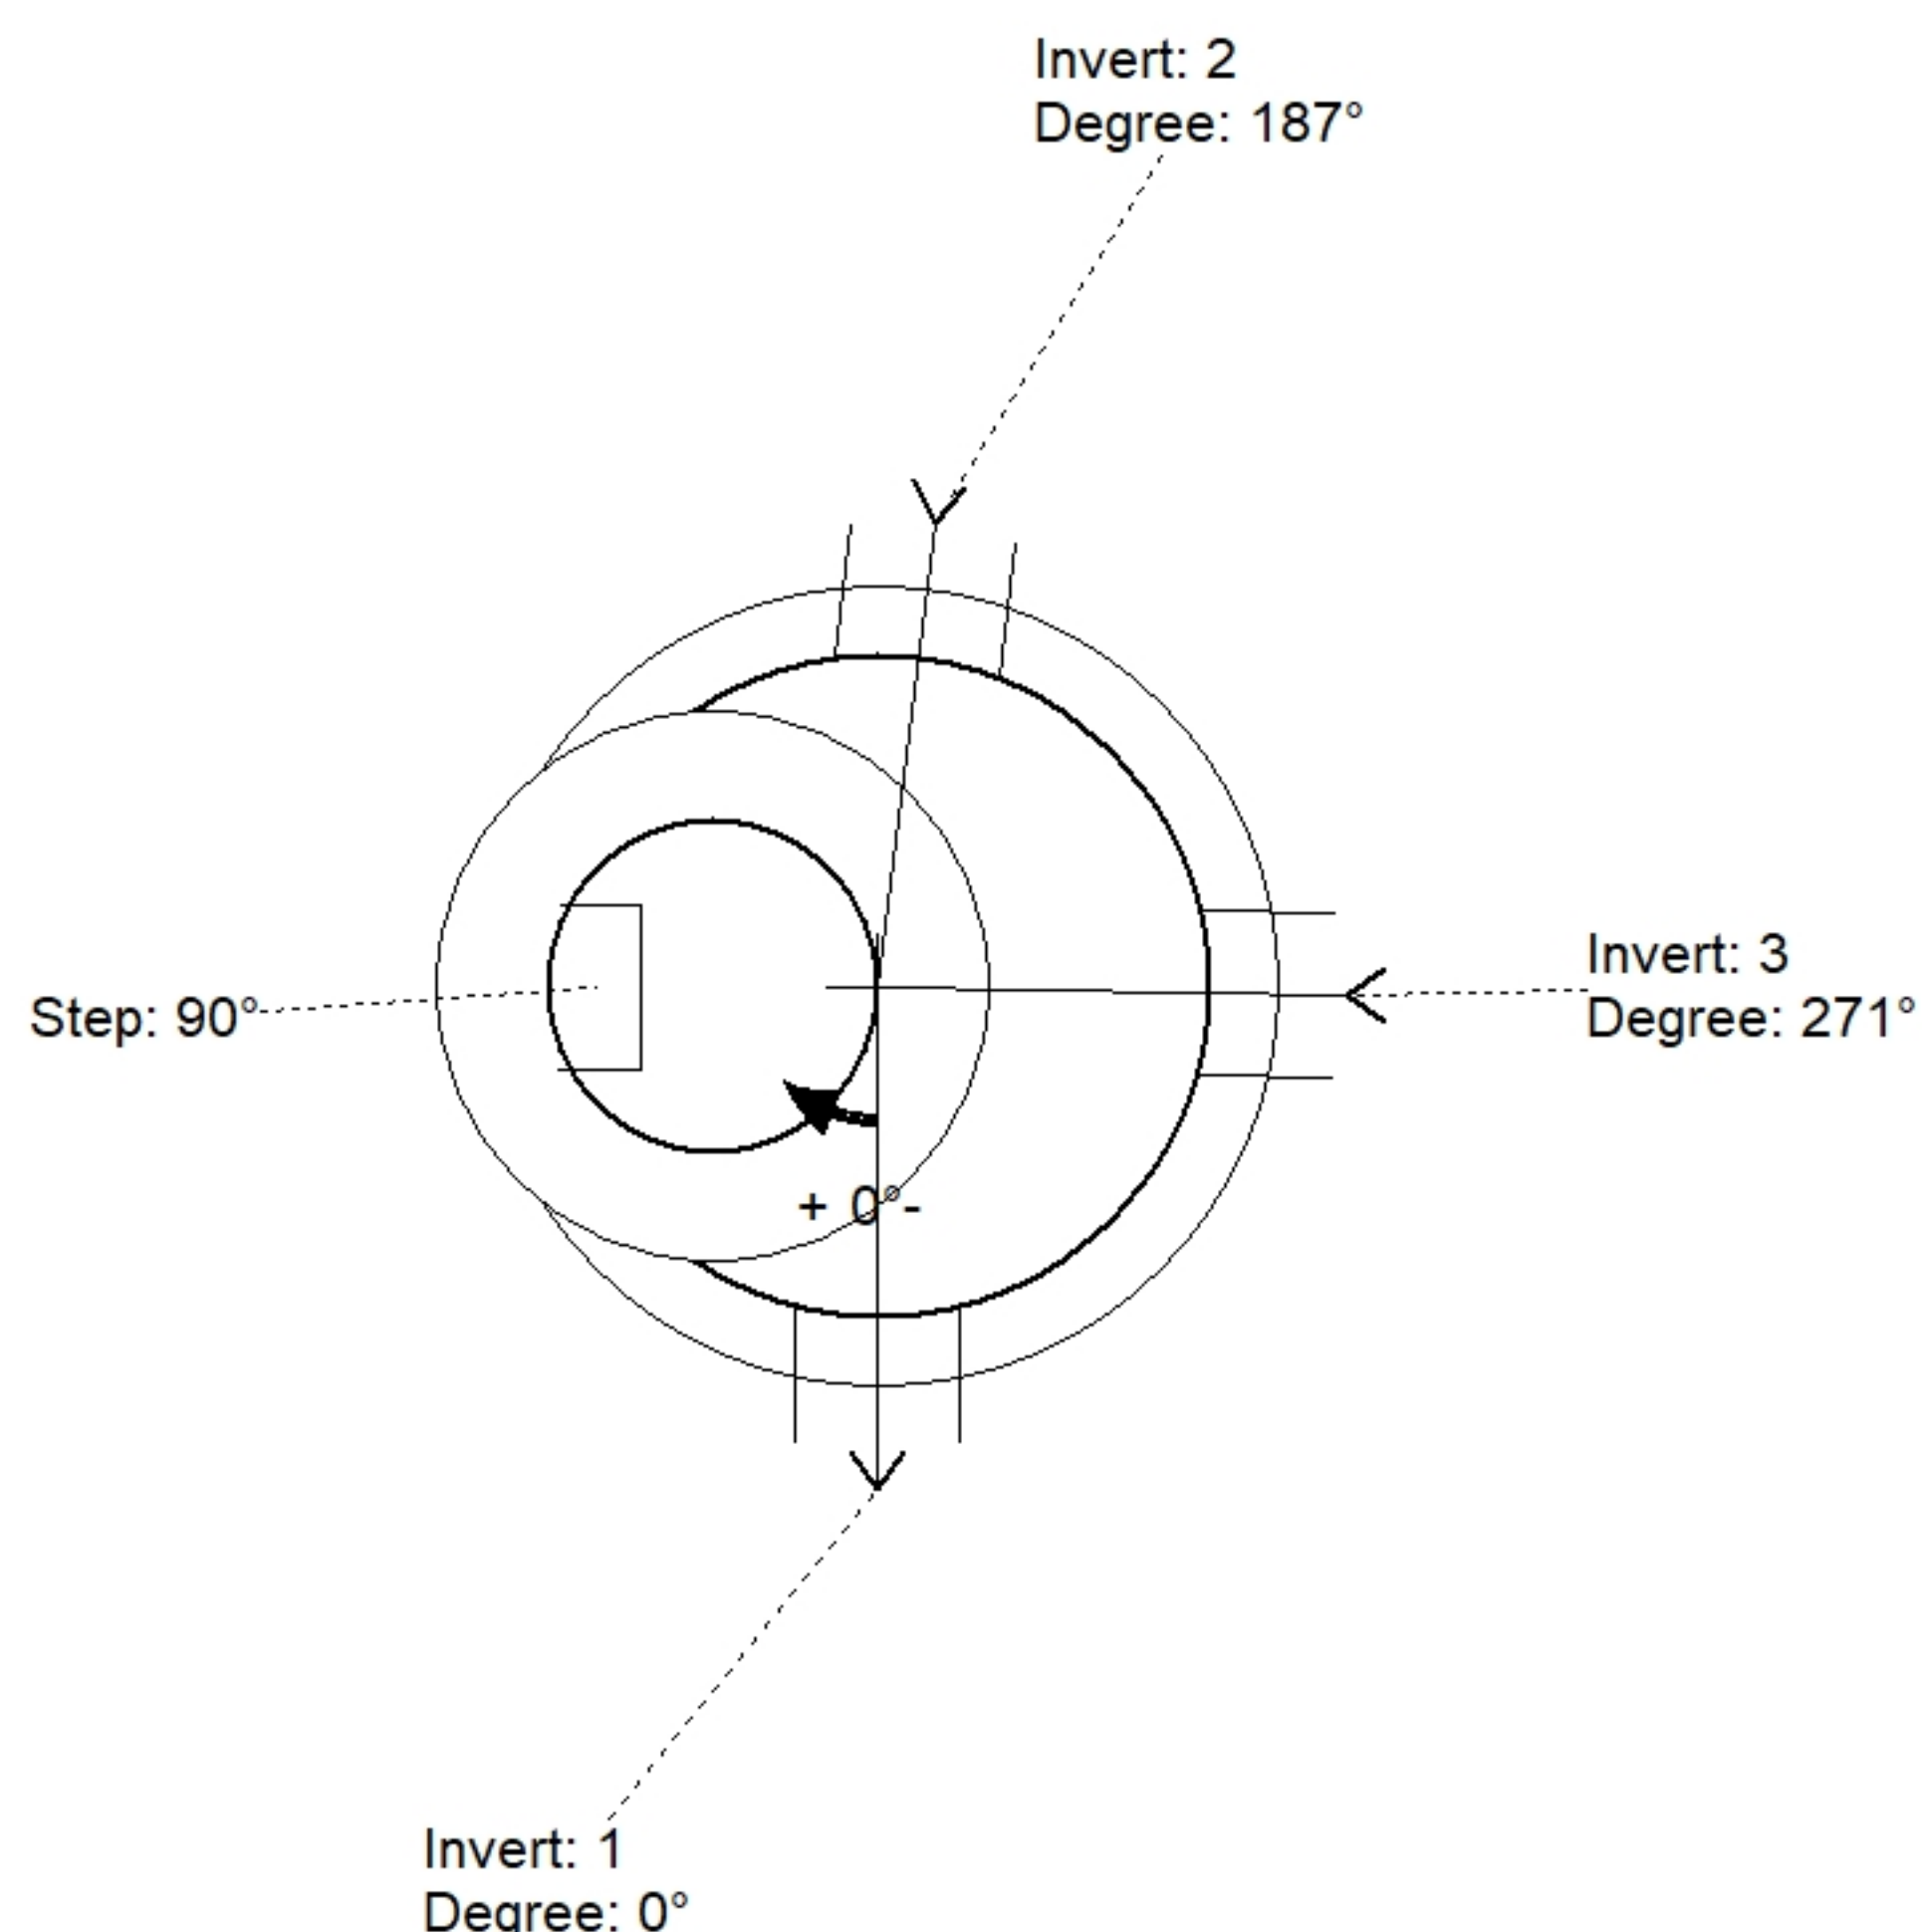

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	410.25'							
Reducer								
Invert 1	405.9'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	406.36'	187°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	5.52"	P1
Invert 3	406'	271°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

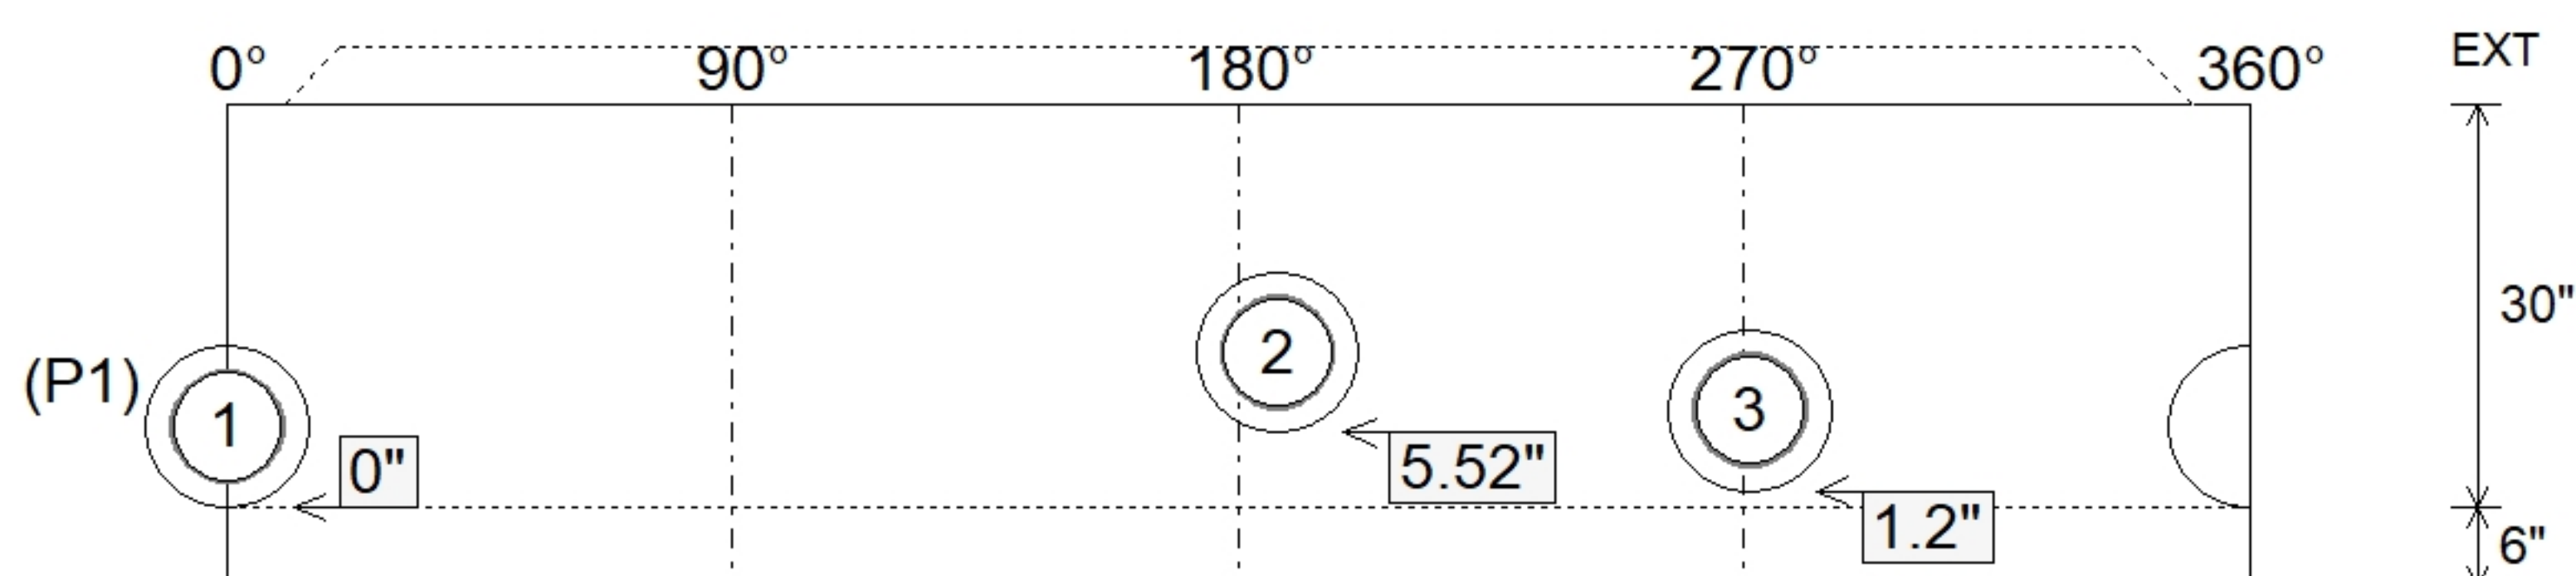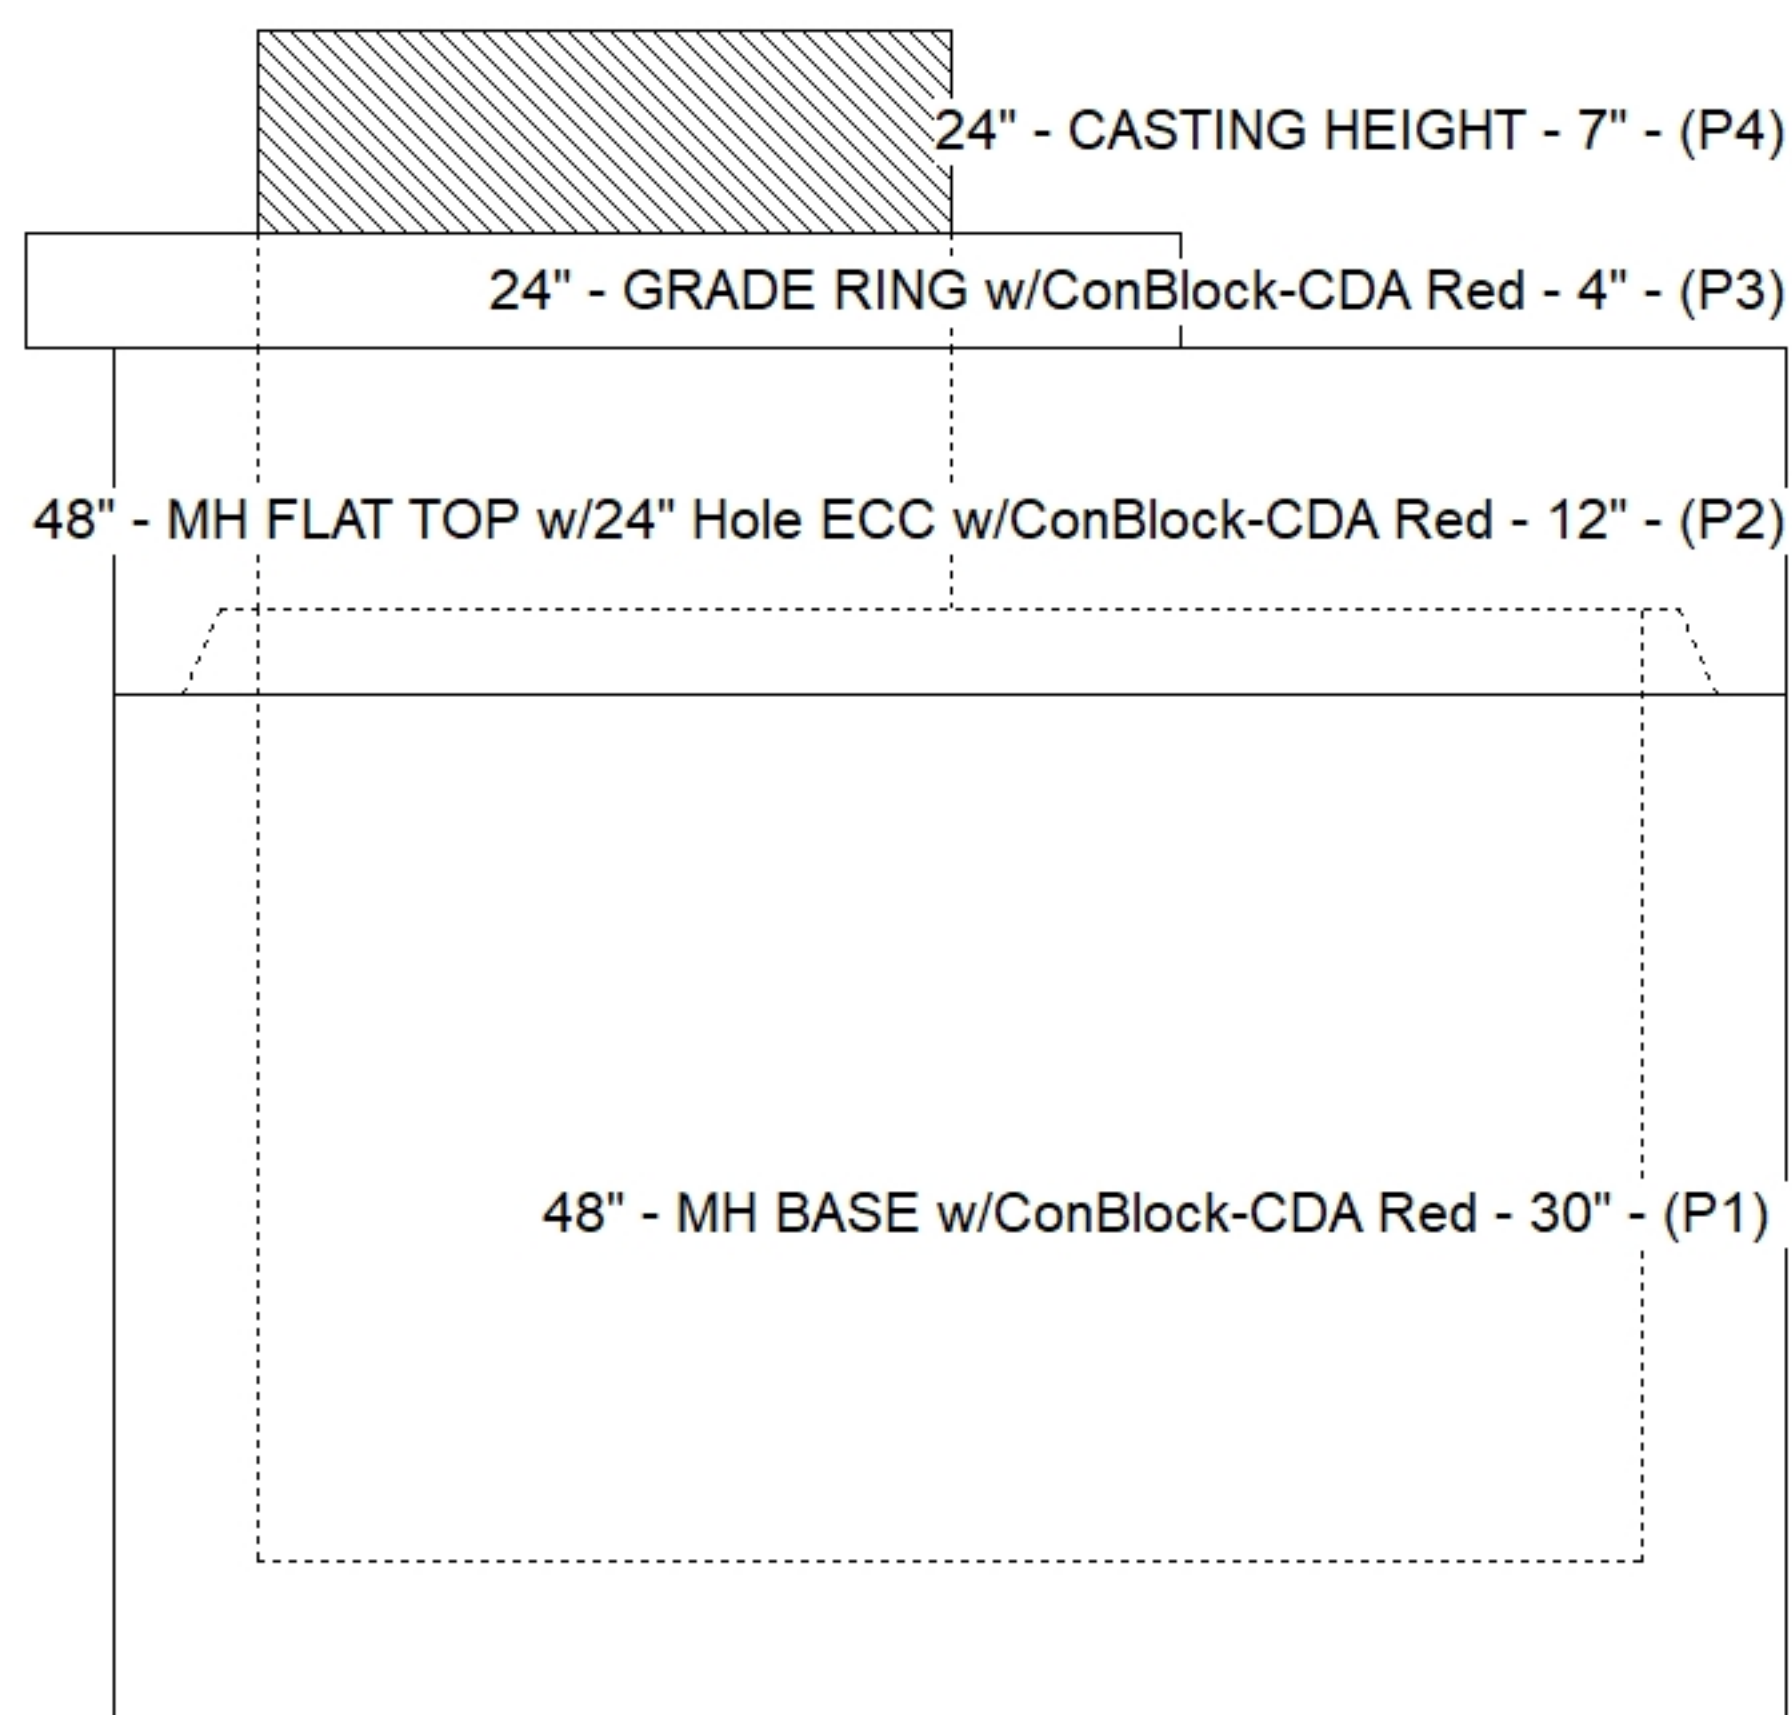

Submittal Drawing
7/27/2026 10:04:32 AM

SUBMITTAL
APPROVED BY:
