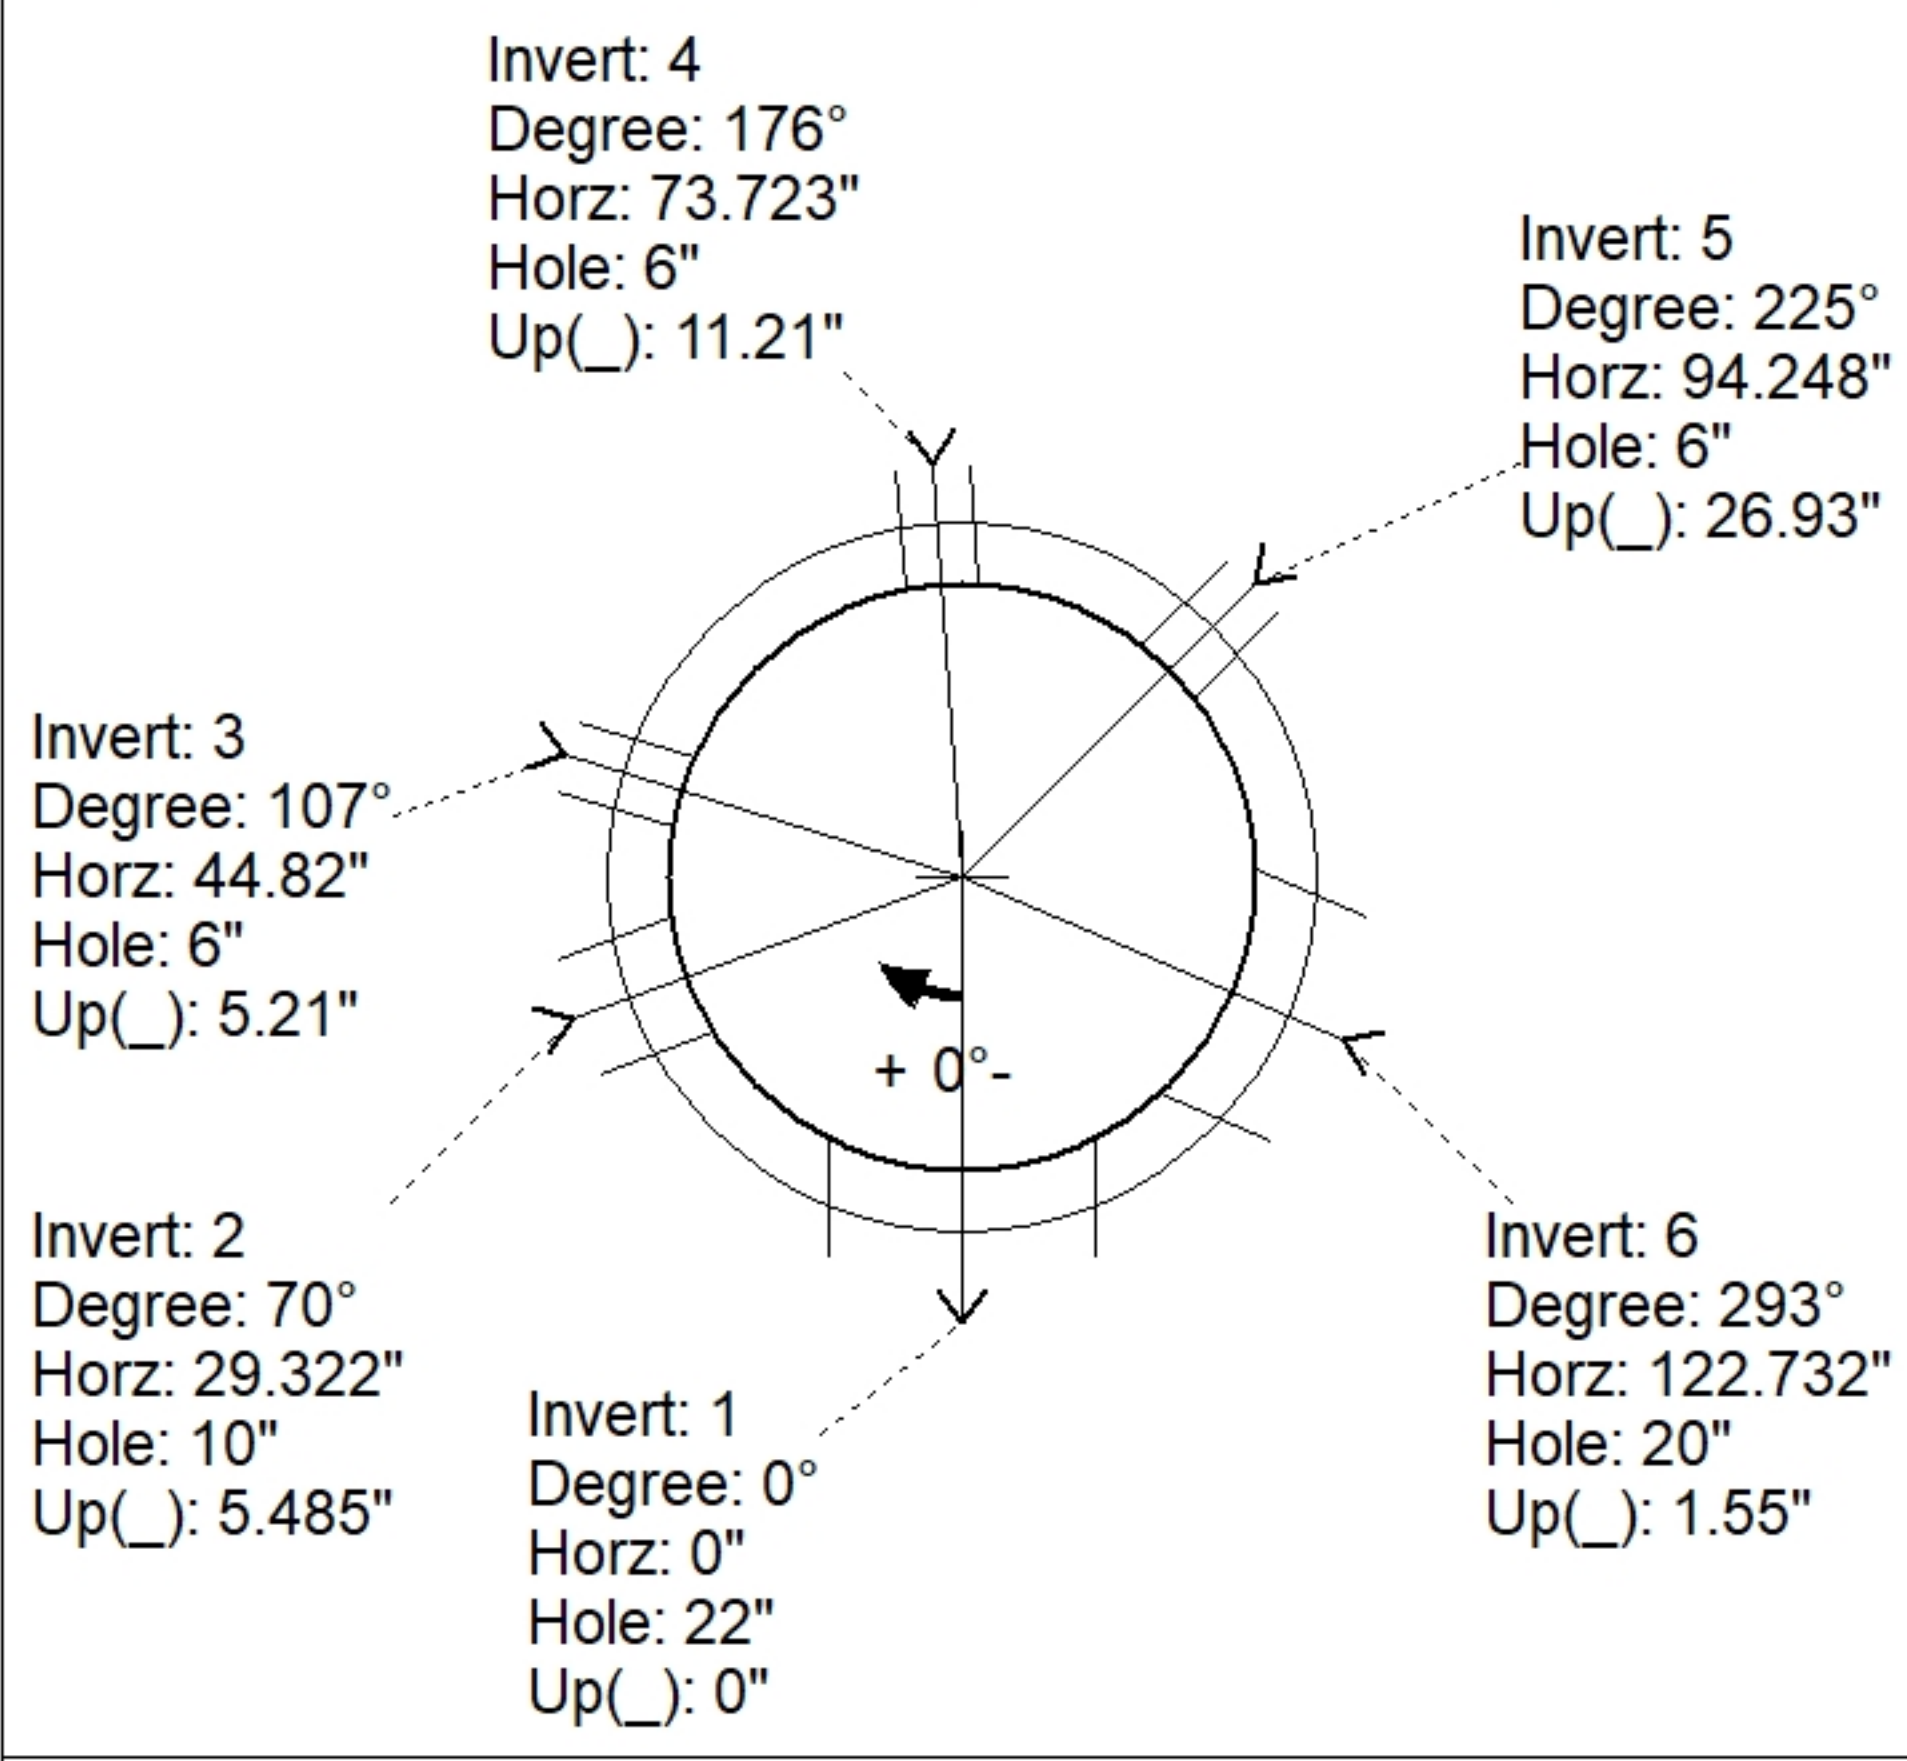
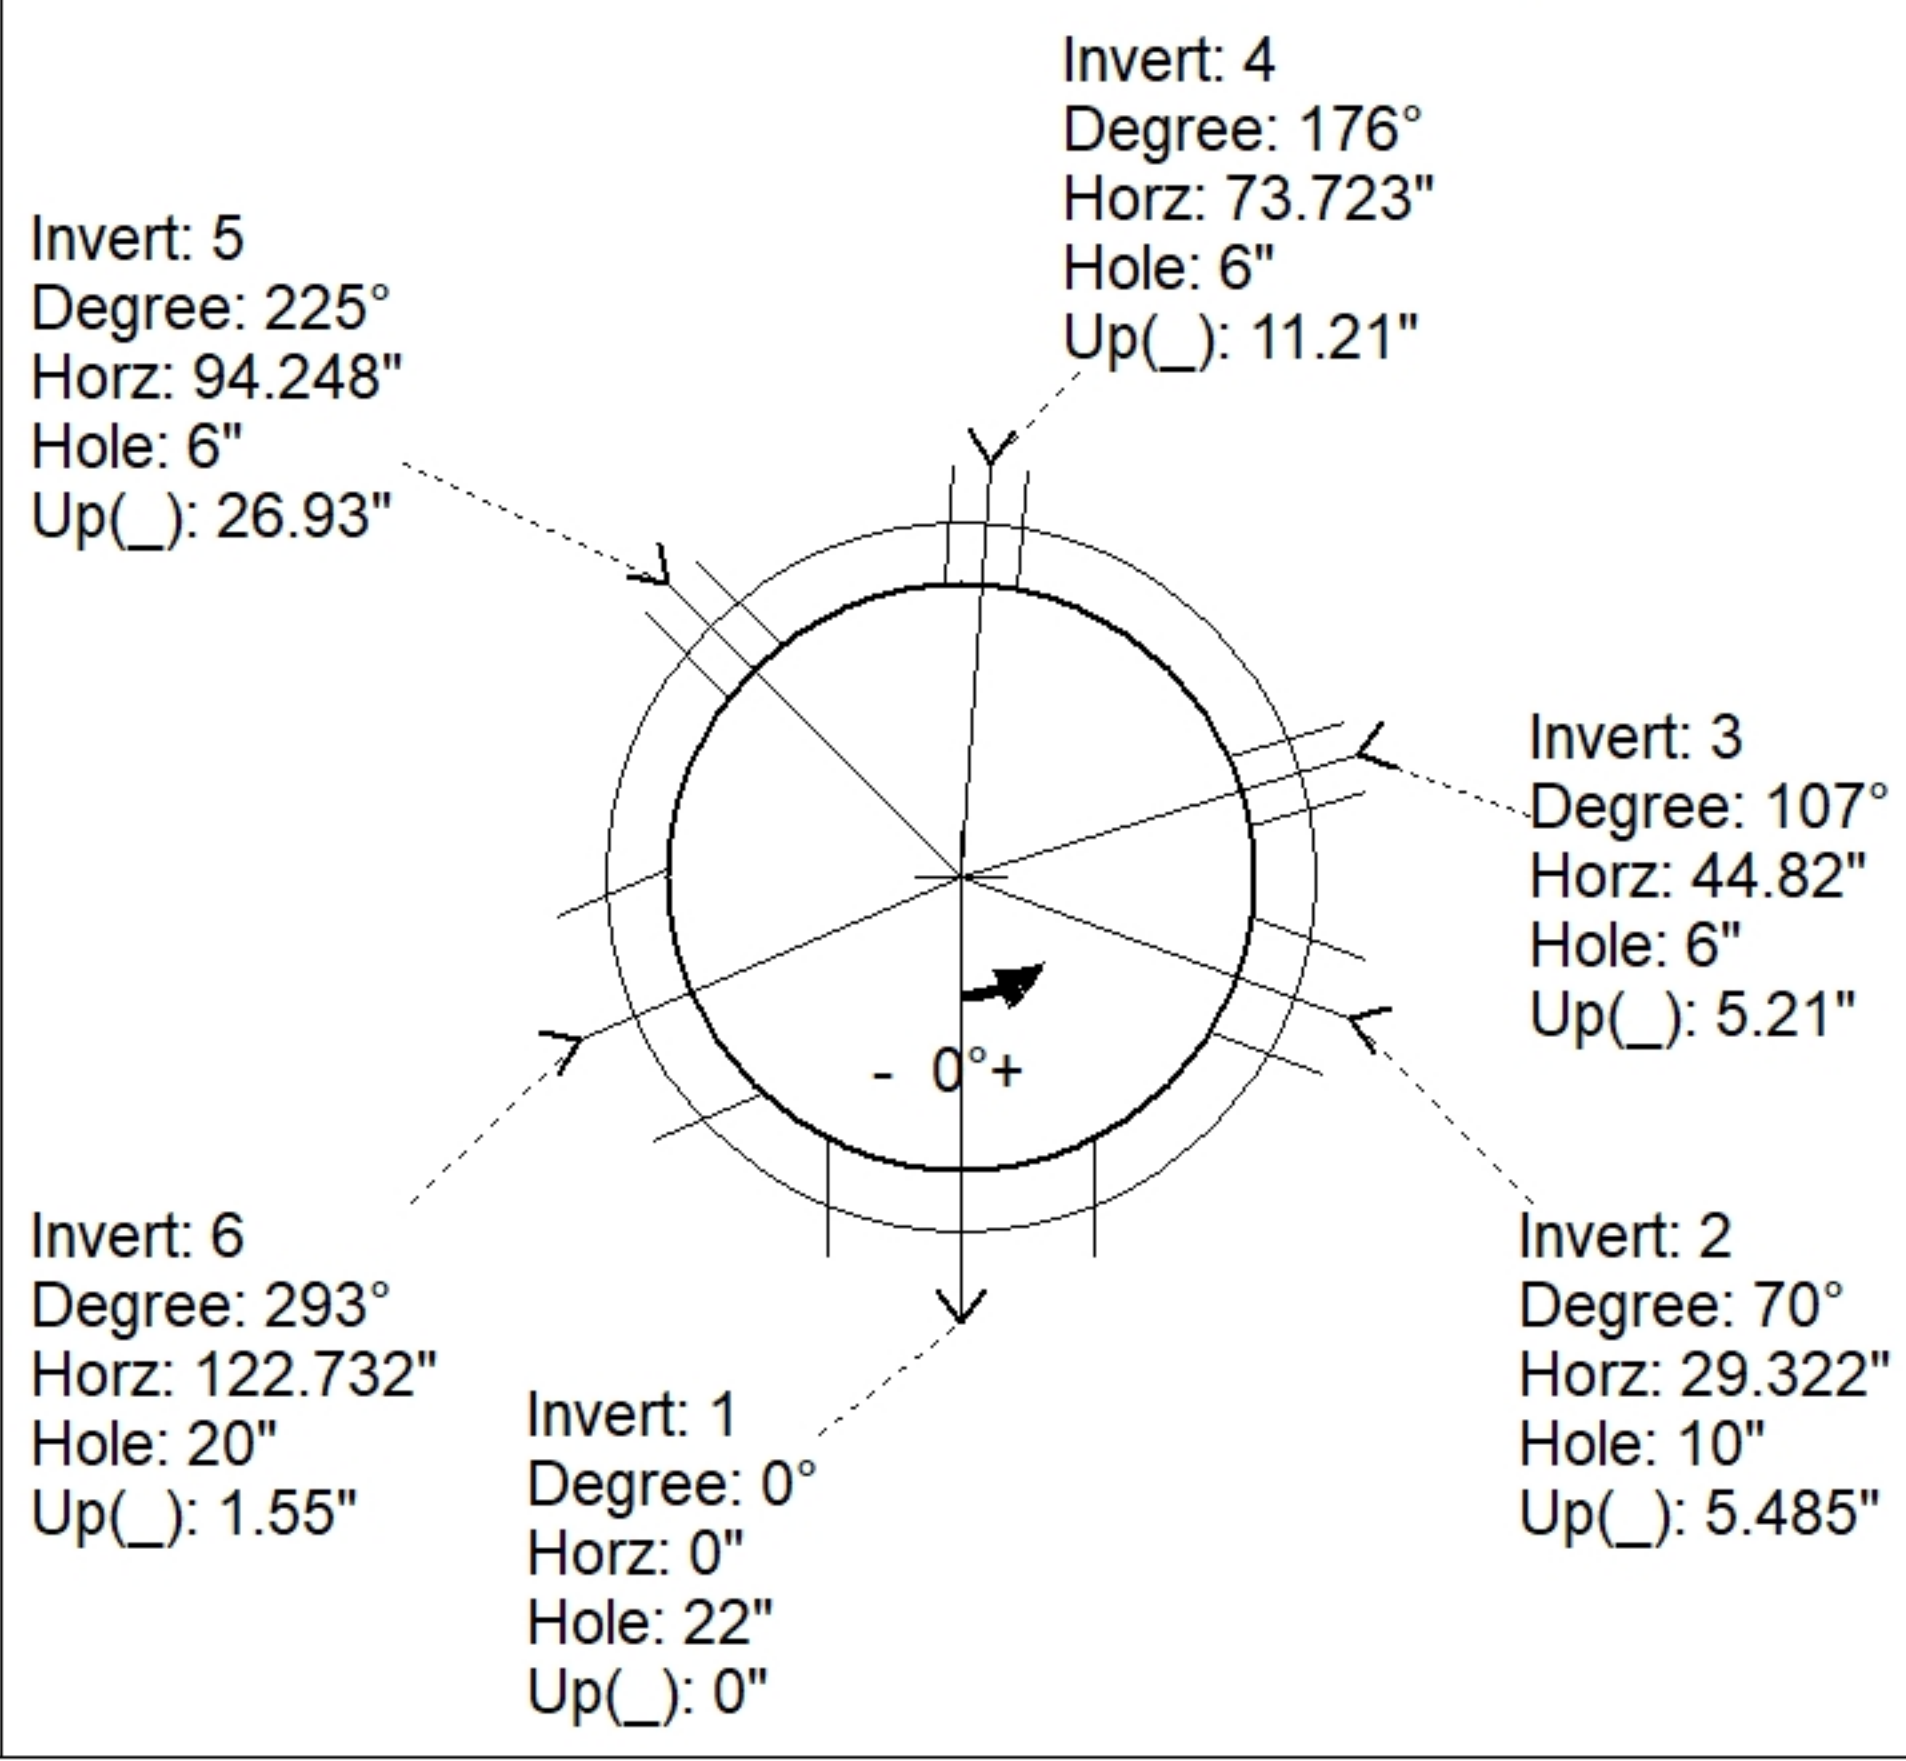
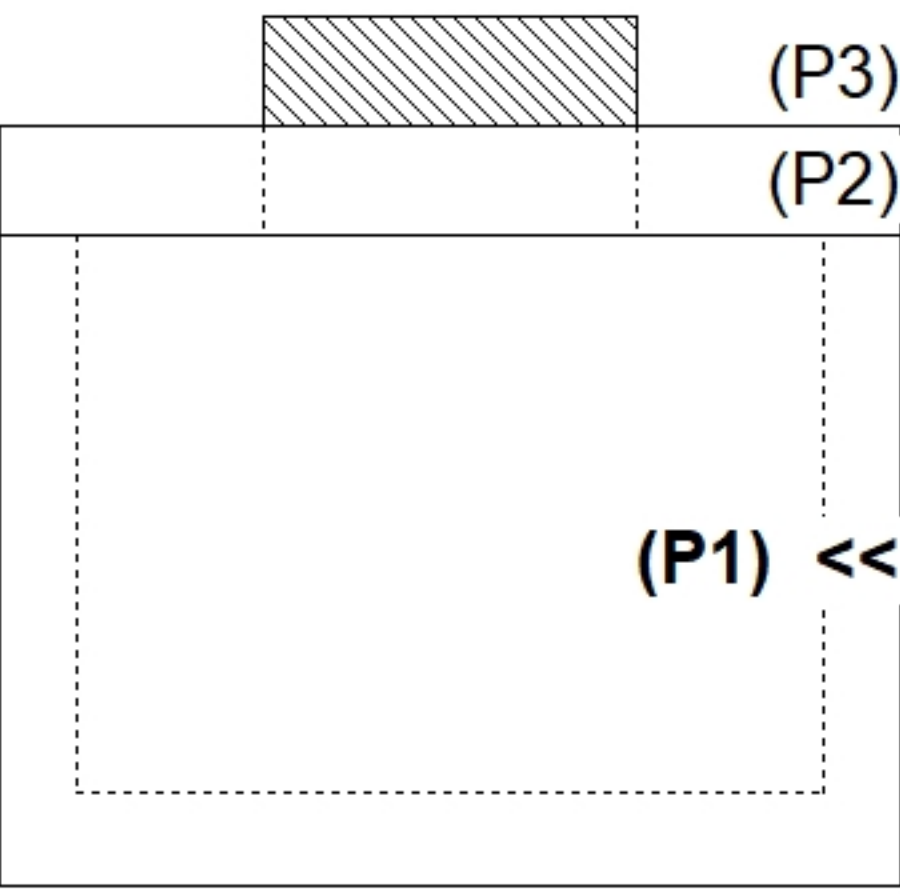
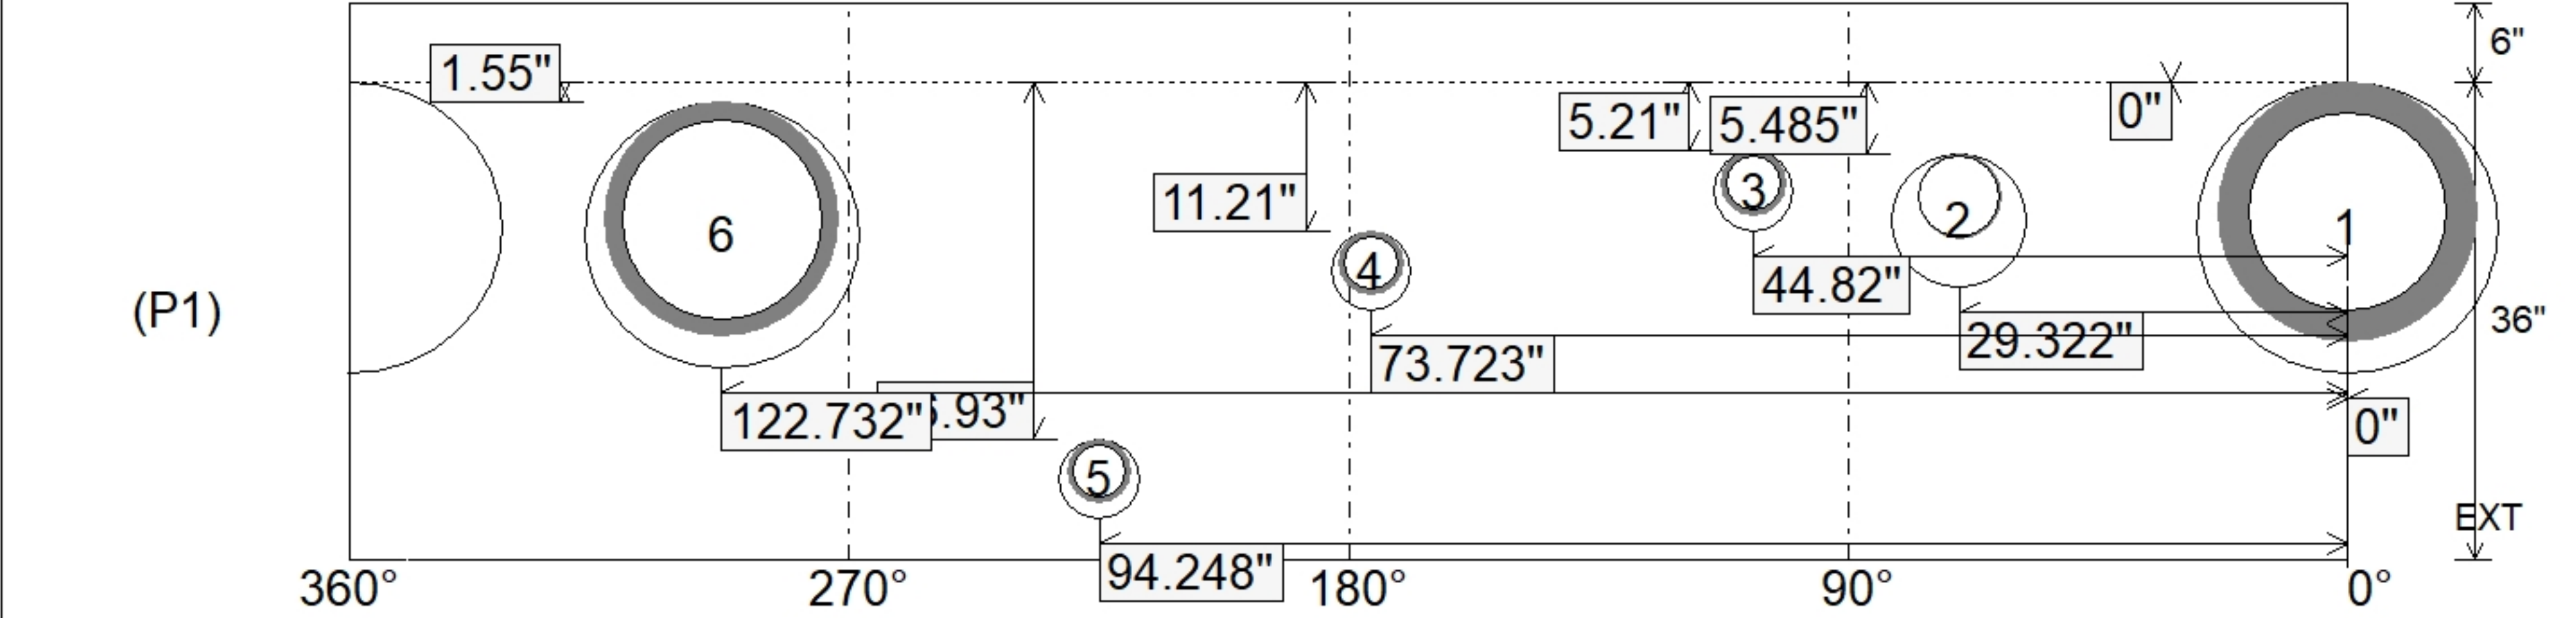


Job Name: 26-2018B Hancock Co Middle School Utility Job Location: South Lewisport, KY Contractor: Winwater Hartford KY Co.				Plant: Beaver Dam 10/12/2026 8:19:39 AM		Tech: S. Felletter PC: A. Chambers									
Structure ID: DI-7A ST-MH															
P1			MH048BA36		MH BASE F/n										
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" Center Hole F/F - 7" P1) 48" - MH BASE F/n - 36" 1) CASTING - HOE MCB-315-B Fr./Bar Grate 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 10 3) Hole - 6 1) Hole - 20					0 lb 1700 lb 3476 lb 255 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5431 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MCB-315-B F/ BAR GRATE). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.								
Rim: 412.25' Rim to Invert: 4.03' Slack: 0.61" Sump: 2.25" Step Position: 0°															
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset					
Invert 1	408.22'	0°	0"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	0"	0"					
Invert 2	408.5'	70°	35.43"	6" PVC SDR35	6.25"	Hole 10	10"	10.074"	5.485"	0"					
Invert 3	408.5'	107°	54.158"	4" HDPE	4.8"	Hole 6	6"	6.016"	5.21"	0"					
Invert 4	409'	176°	89.082"	4" HDPE	4.8"	Hole 6	6"	6.016"	11.21"	0"					
Invert 5	410.31'	225°	113.883"	4" HDPE	4.8"	Hole 6	6"	6.016"	26.93"	0"					
Invert 6	408.27'	293°	148.301"	15" HDPE	17.6"	Hole 20	20"	20.629"	1.55"	0"					
Invert 7															
Invert 8															
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS  <table><tr><td>Coating (Int): Coating (Ext):</td><td>Seam Up: Flat Seam Dn: n/a</td><td>Wall Thickness: 5" Floor Height: 6"</td><td>Height (Int): 36" Height (Ext): 42"</td><td>Weight (Net): 3476 lb Volume (Net): 0.89cu.yd</td></tr></table>											Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3476 lb Volume (Net): 0.89cu.yd
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3476 lb Volume (Net): 0.89cu.yd											
