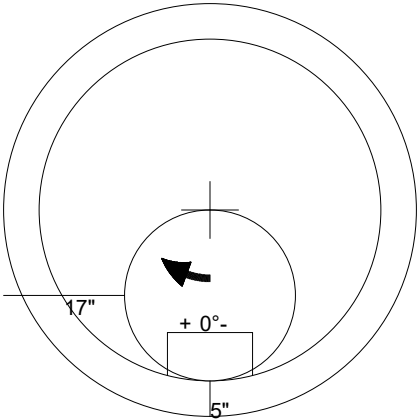



Job Name: 26-2026 - NEW MAINTENANCE AND STORAGE BUILDING		Plant: 100	Tech: Jared - F	
Job Location: Greenville, KY 42345		10/5/2026 3:39:04 PM	PC: A. Chambers	
Contractor: Winwater Hartford KY Co.				
Structure ID: MH-3 SS-MH				
P3 MH048CN36		ECC CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE T/h - 30" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) PSX - 12-06 NYLO 7) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 3000 lb 1677 lb 3330 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 8 lb 8 lb 0 lb ----- 9936 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C SANITARY) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
