

Plant: 100

6/12/2026 7:49:40 AM

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht F/n

3400 lb
5270 lb
0 lb
6090 lb
206 lb
0 lb
0 lb

Structure Total: 14965 lb

** KYTC STATE PROJECT **

1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PI AT 28 DAYS.
3. HOE-KY-206 F/C CAST INTO TOP SLAB.

REINFORCING PER ASTM A615 (GRADE 60).




- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 375.03' Rim to Invert: 6.9' Slack: 0.8" Sump: 0" Step Position:


[illegible]

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

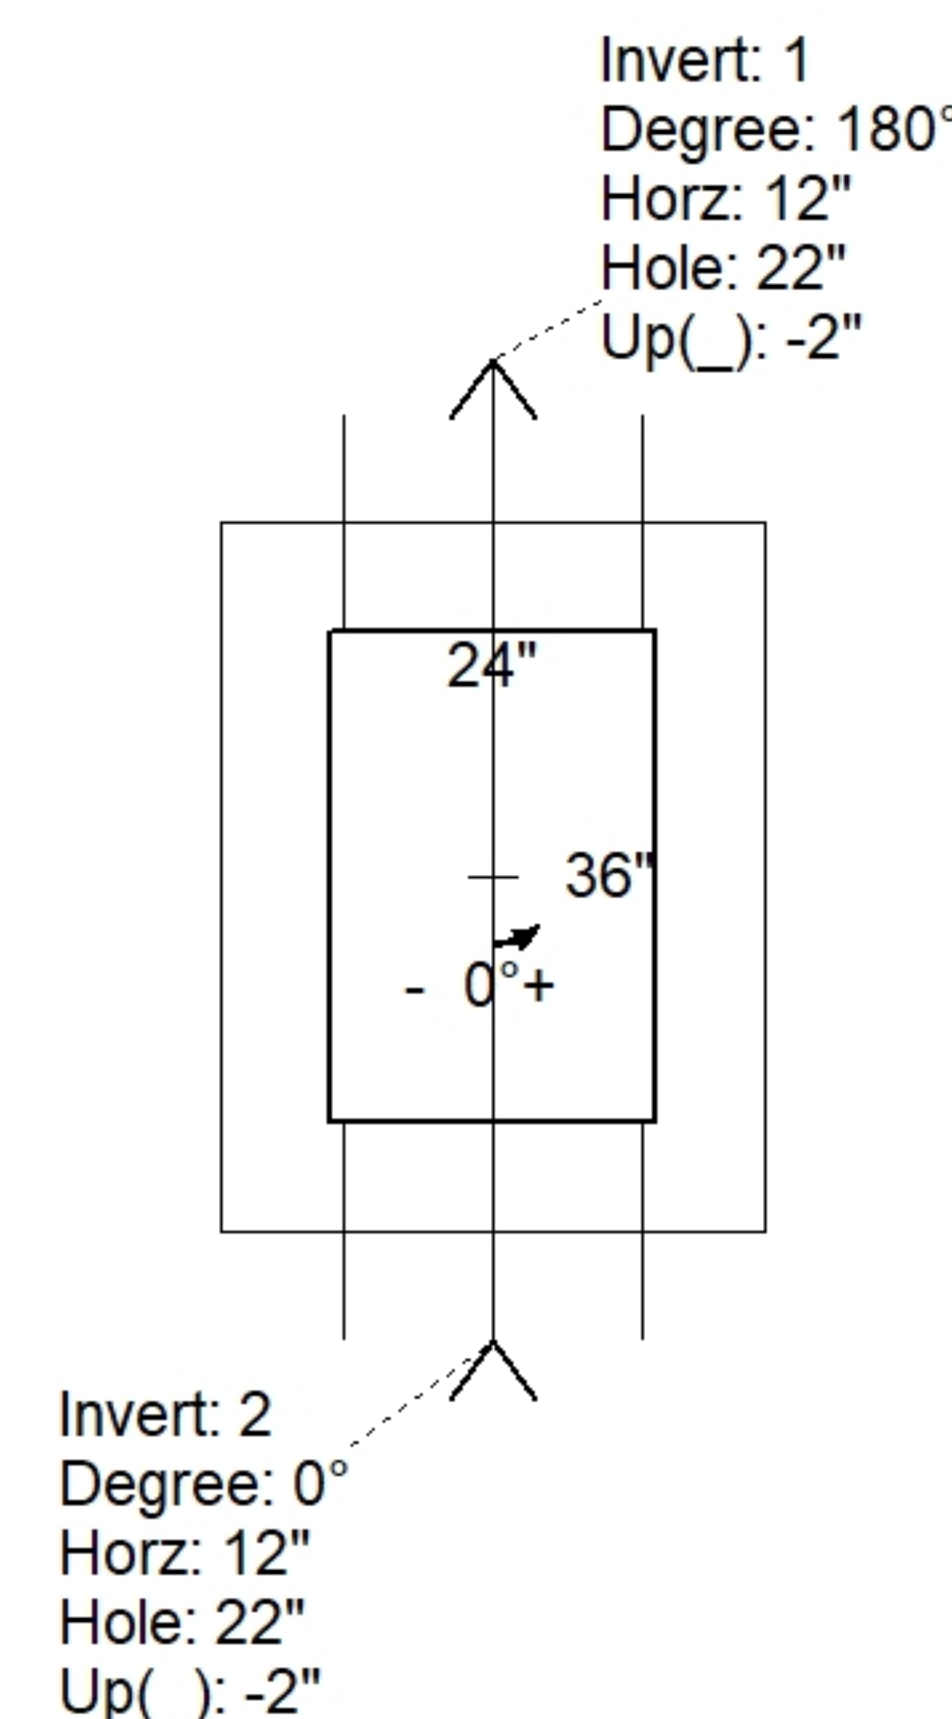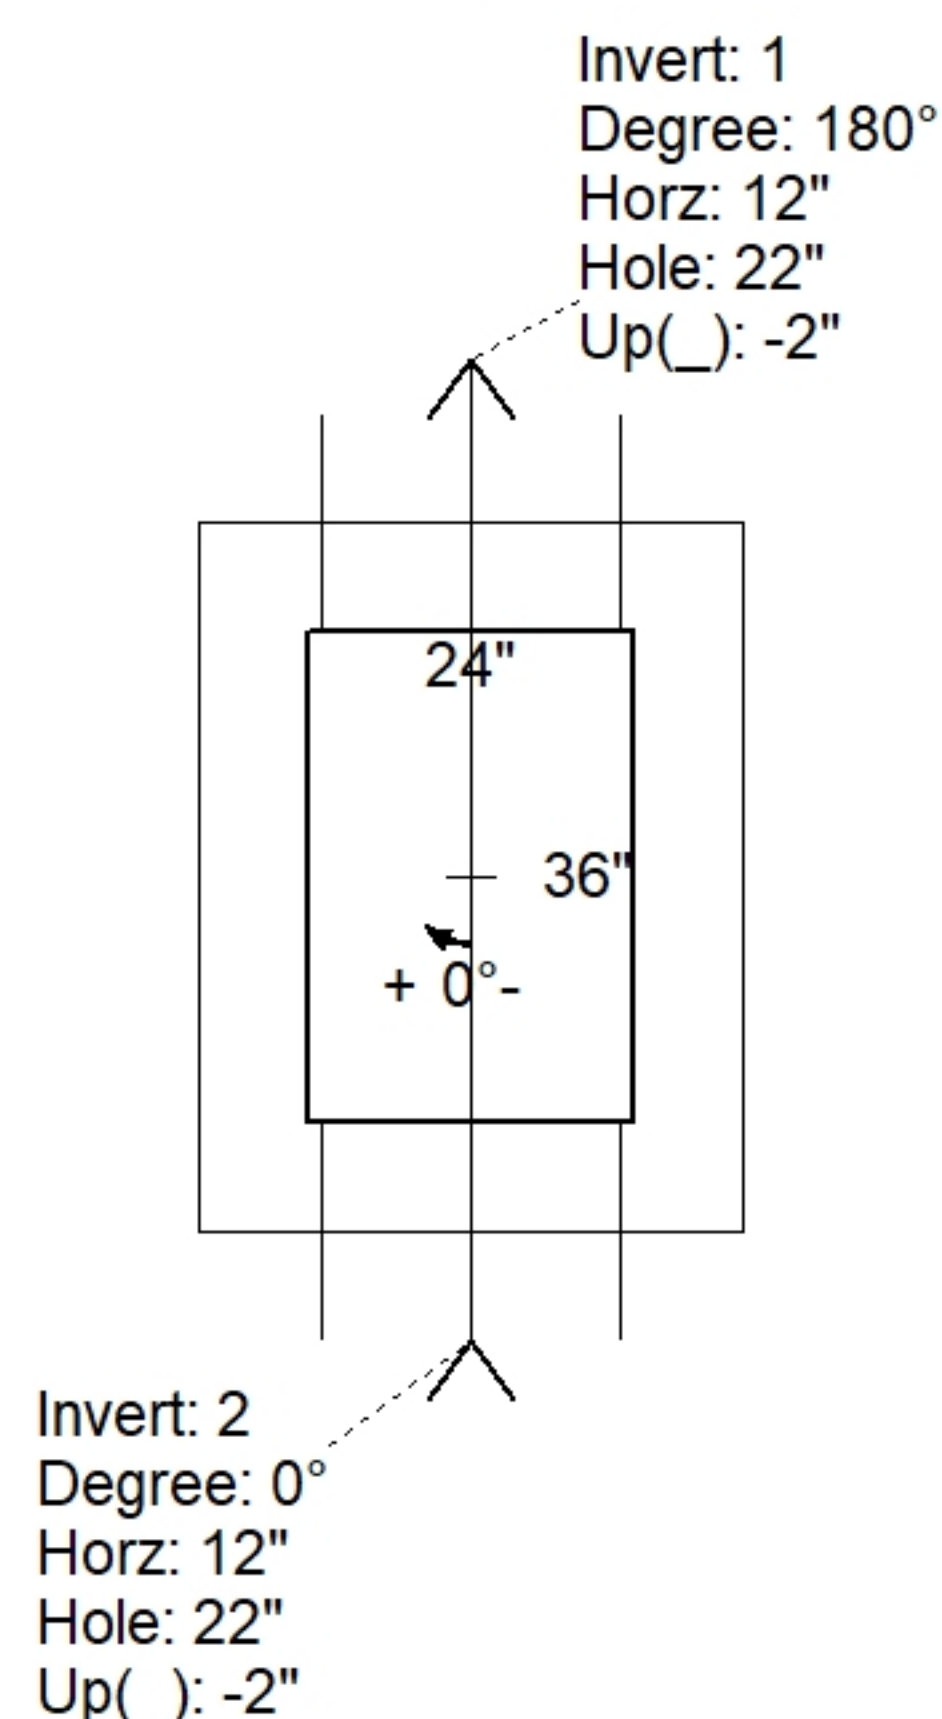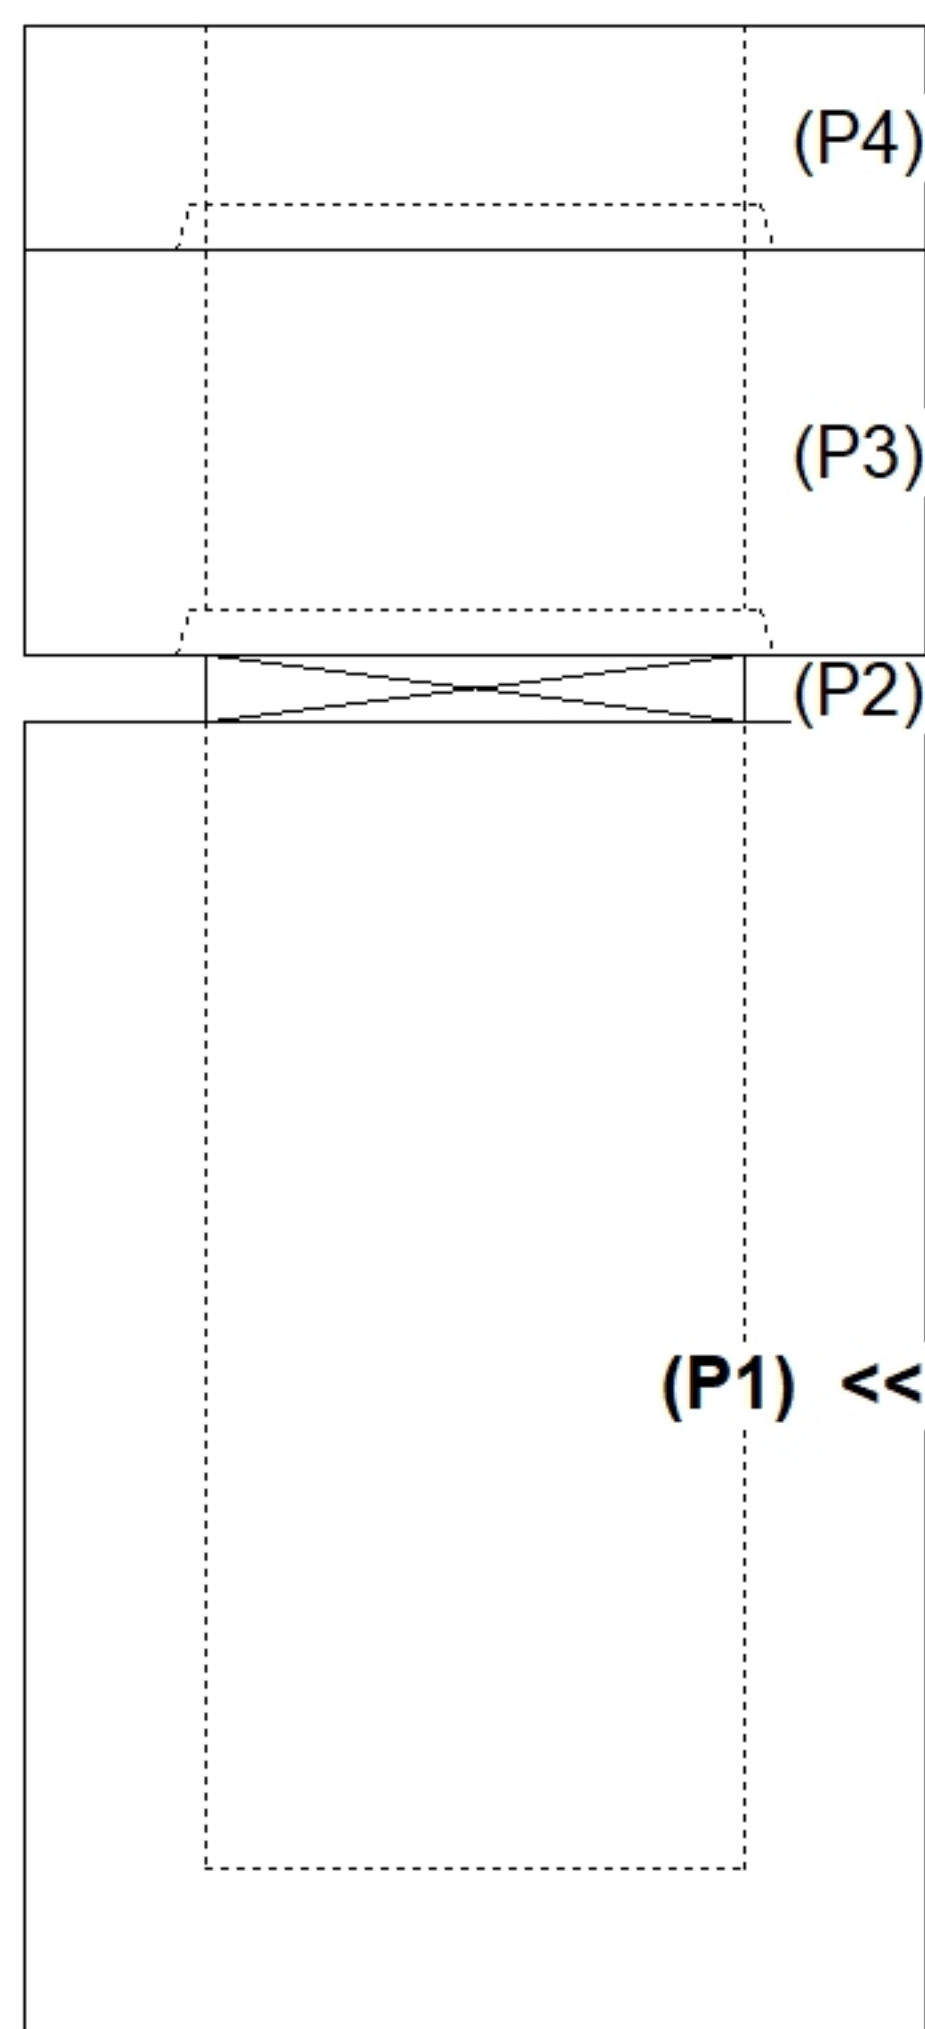

INSIDE WALL DIMENSIONS

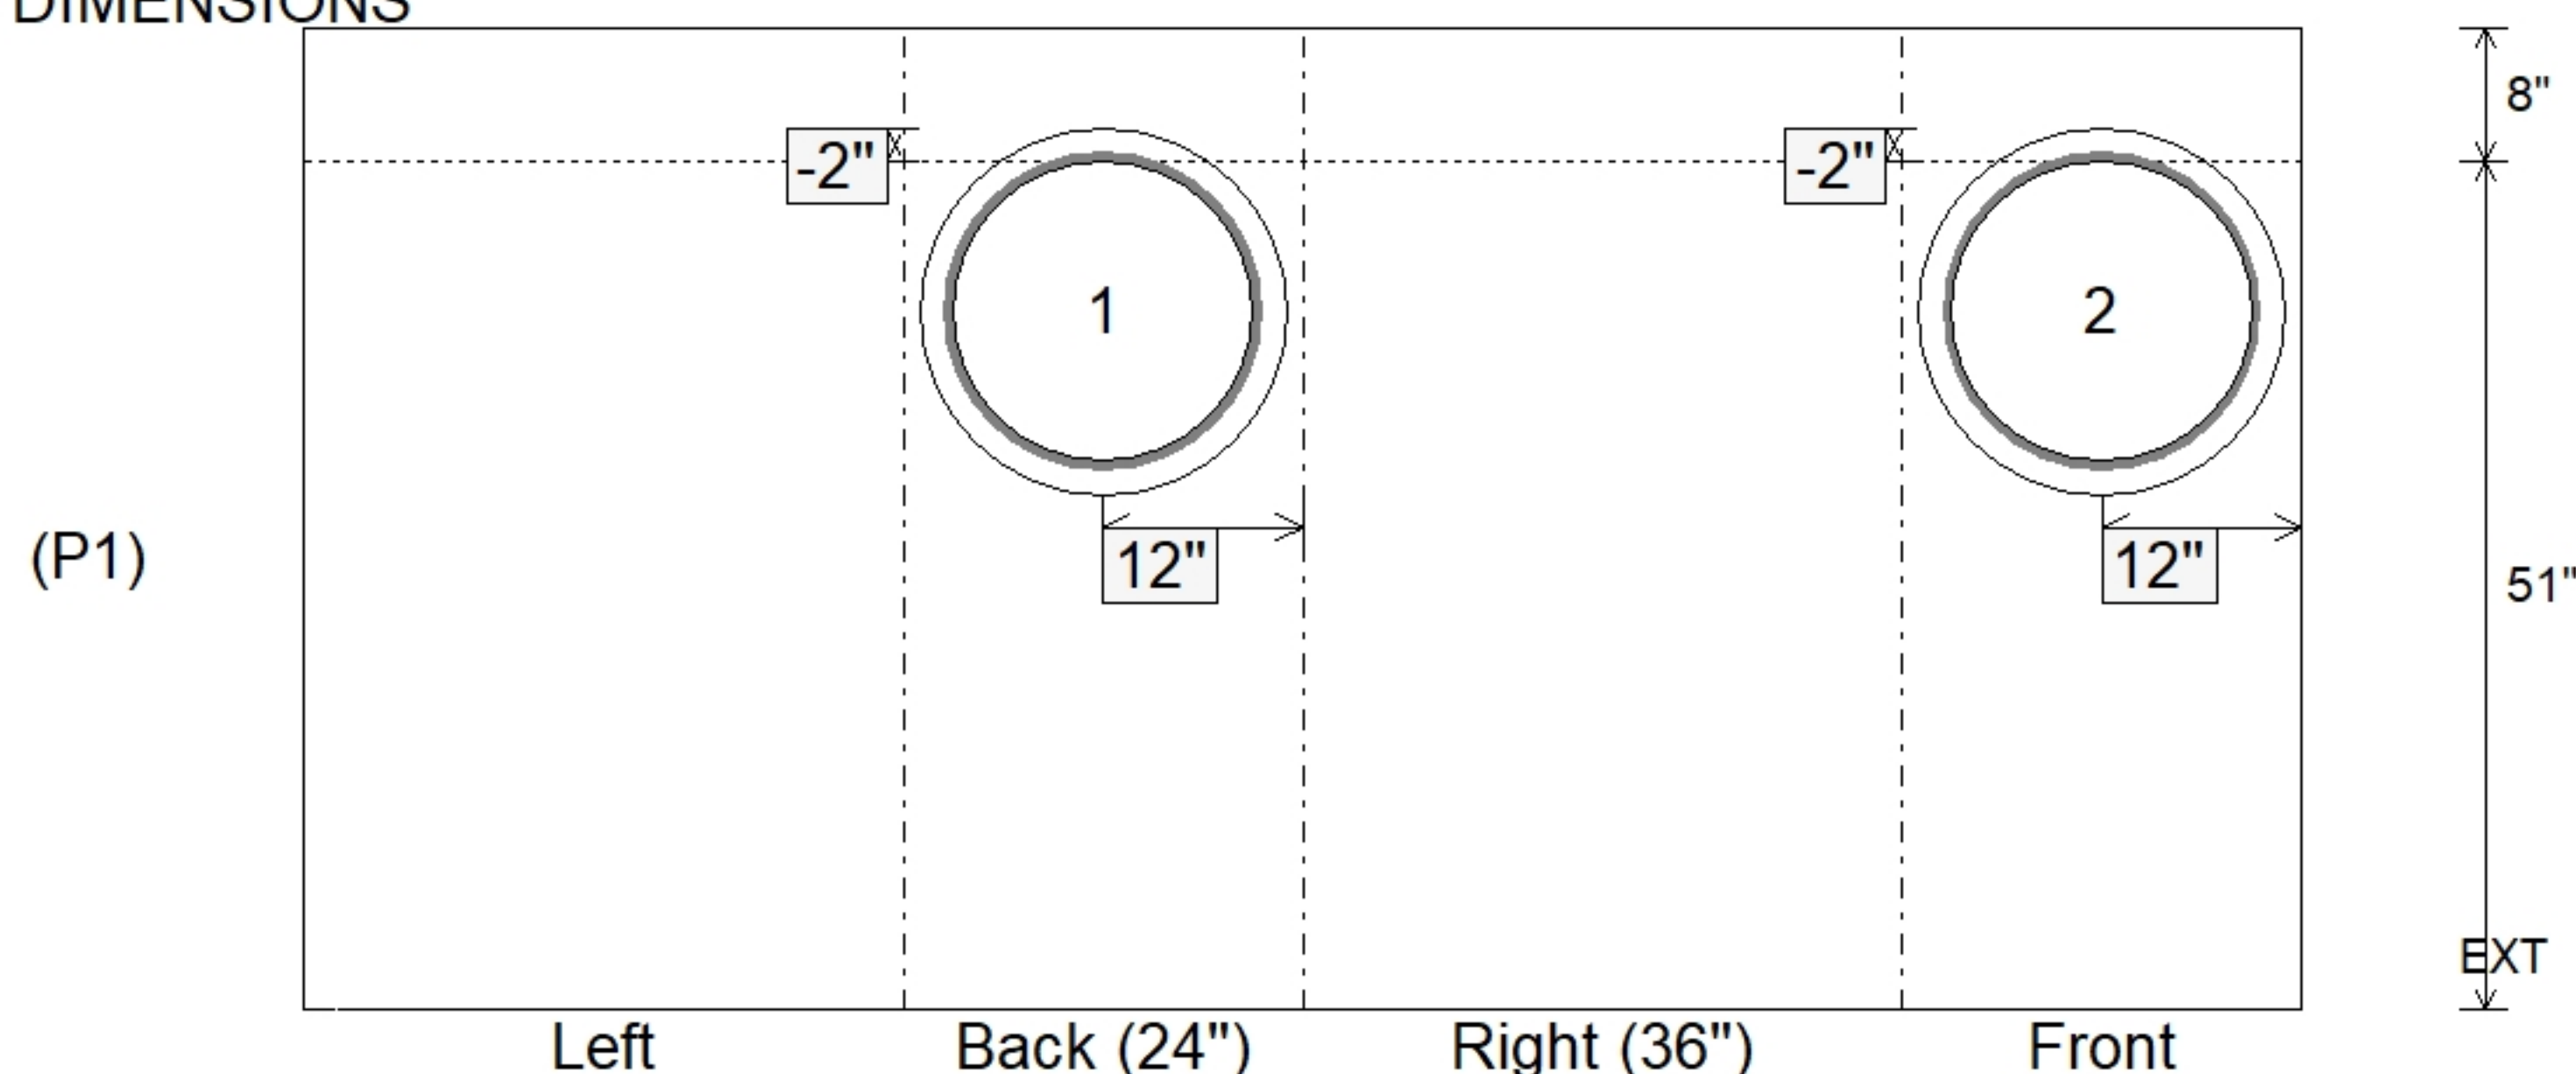

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 51"
Height (Ext): 59"

Weight (Net): 6090 lb
Volume (Net): 1.56cu.yd
