



Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:48 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: C1 DBI2											
P2		BX3648-08R-VH		BOX RISER 8inW, Variable Ht F/G							
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW, Variable Ht F/G - 40" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht T/n - 60" 1) CASTING - HOE KY-398 SET (DBI 2) 2) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 48 1) Hole - 40 1) Hole - 10					0 lb 5309 lb 8535 lb 398 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 14242 lb		Structure Notes: 1. KYTC DBI TYPE 2 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-398 SET (DBI 2)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 368.18' Rim to Invert: 8.53' Slack: 0.36" Sump: 6" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3	364.9'	210°	30.625"	6" HDPE	6.9"	Hole 10	10"	11.547"	5"	-12"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

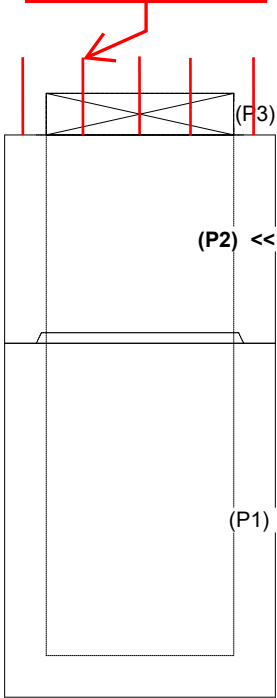

RIGHT-SIDE UP VIEW (int. dimensions)

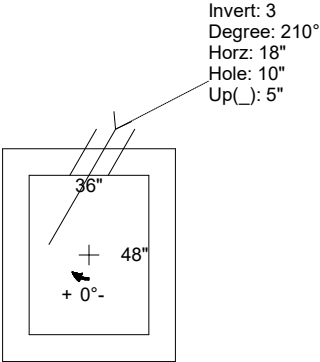

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 40" Height (Ext): 40"	Weight (Net): 5309 lb Volume (Net): 1.36cu.yd
----------------------------------	----------------------------------	--	--	--
