

Contractor: M. Bowling, Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 48"

Rim to Invert: 8.53'

Floor Height: 8"


Slack: 0.36"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 36" x 48" - P.I.P. - BY OTHERS - 8"
P2) 36" x 48" - BOX RISER 8inW, Variable Ht - 40"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 60"
1) CASTING - HOE KY-398 SET (DBI 2)
2) 36" x 48" - Conseal CS-102 1.00"
1) Hole - 48
1) Hole - 40
1) Hole - 10

0 lb
5309 lb
8535 lb
398 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 14242 lb

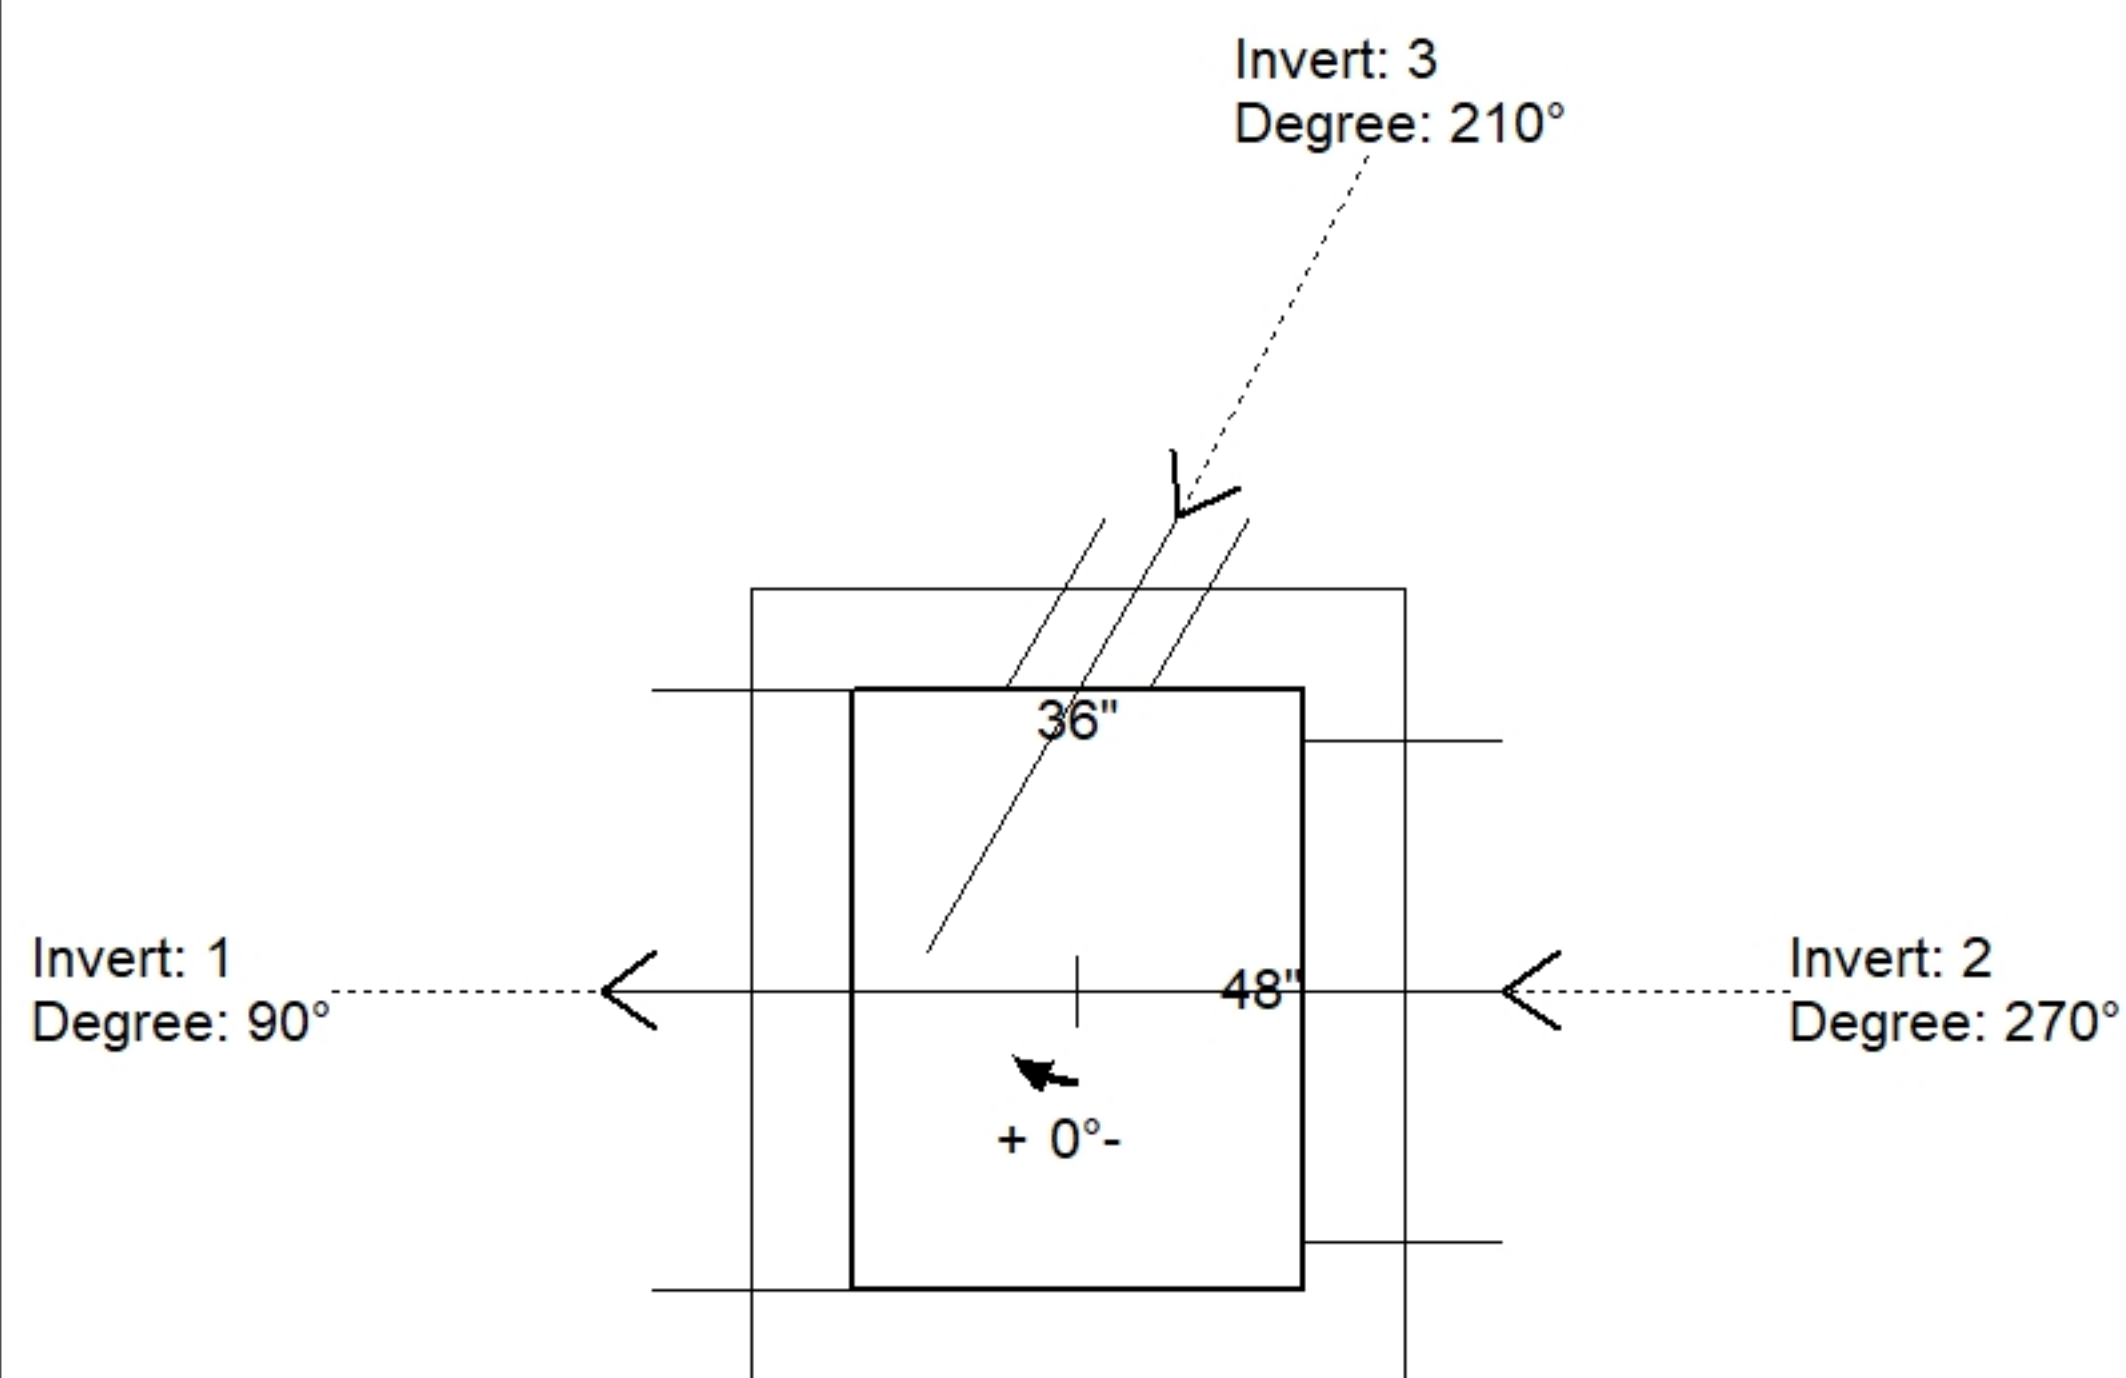

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	368.18'							
Reducer								
Invert 1	359.65'	90°	36" RCP B WALL	44"	48"	Hole 48	0"	P1
Invert 2	359.85'	270°	30" RCP B WALL	37"	40"	Hole 40	3.4"	P1
Invert 3	364.9'	210°	6" HDPE	6.9"	10"	Hole 10	5"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

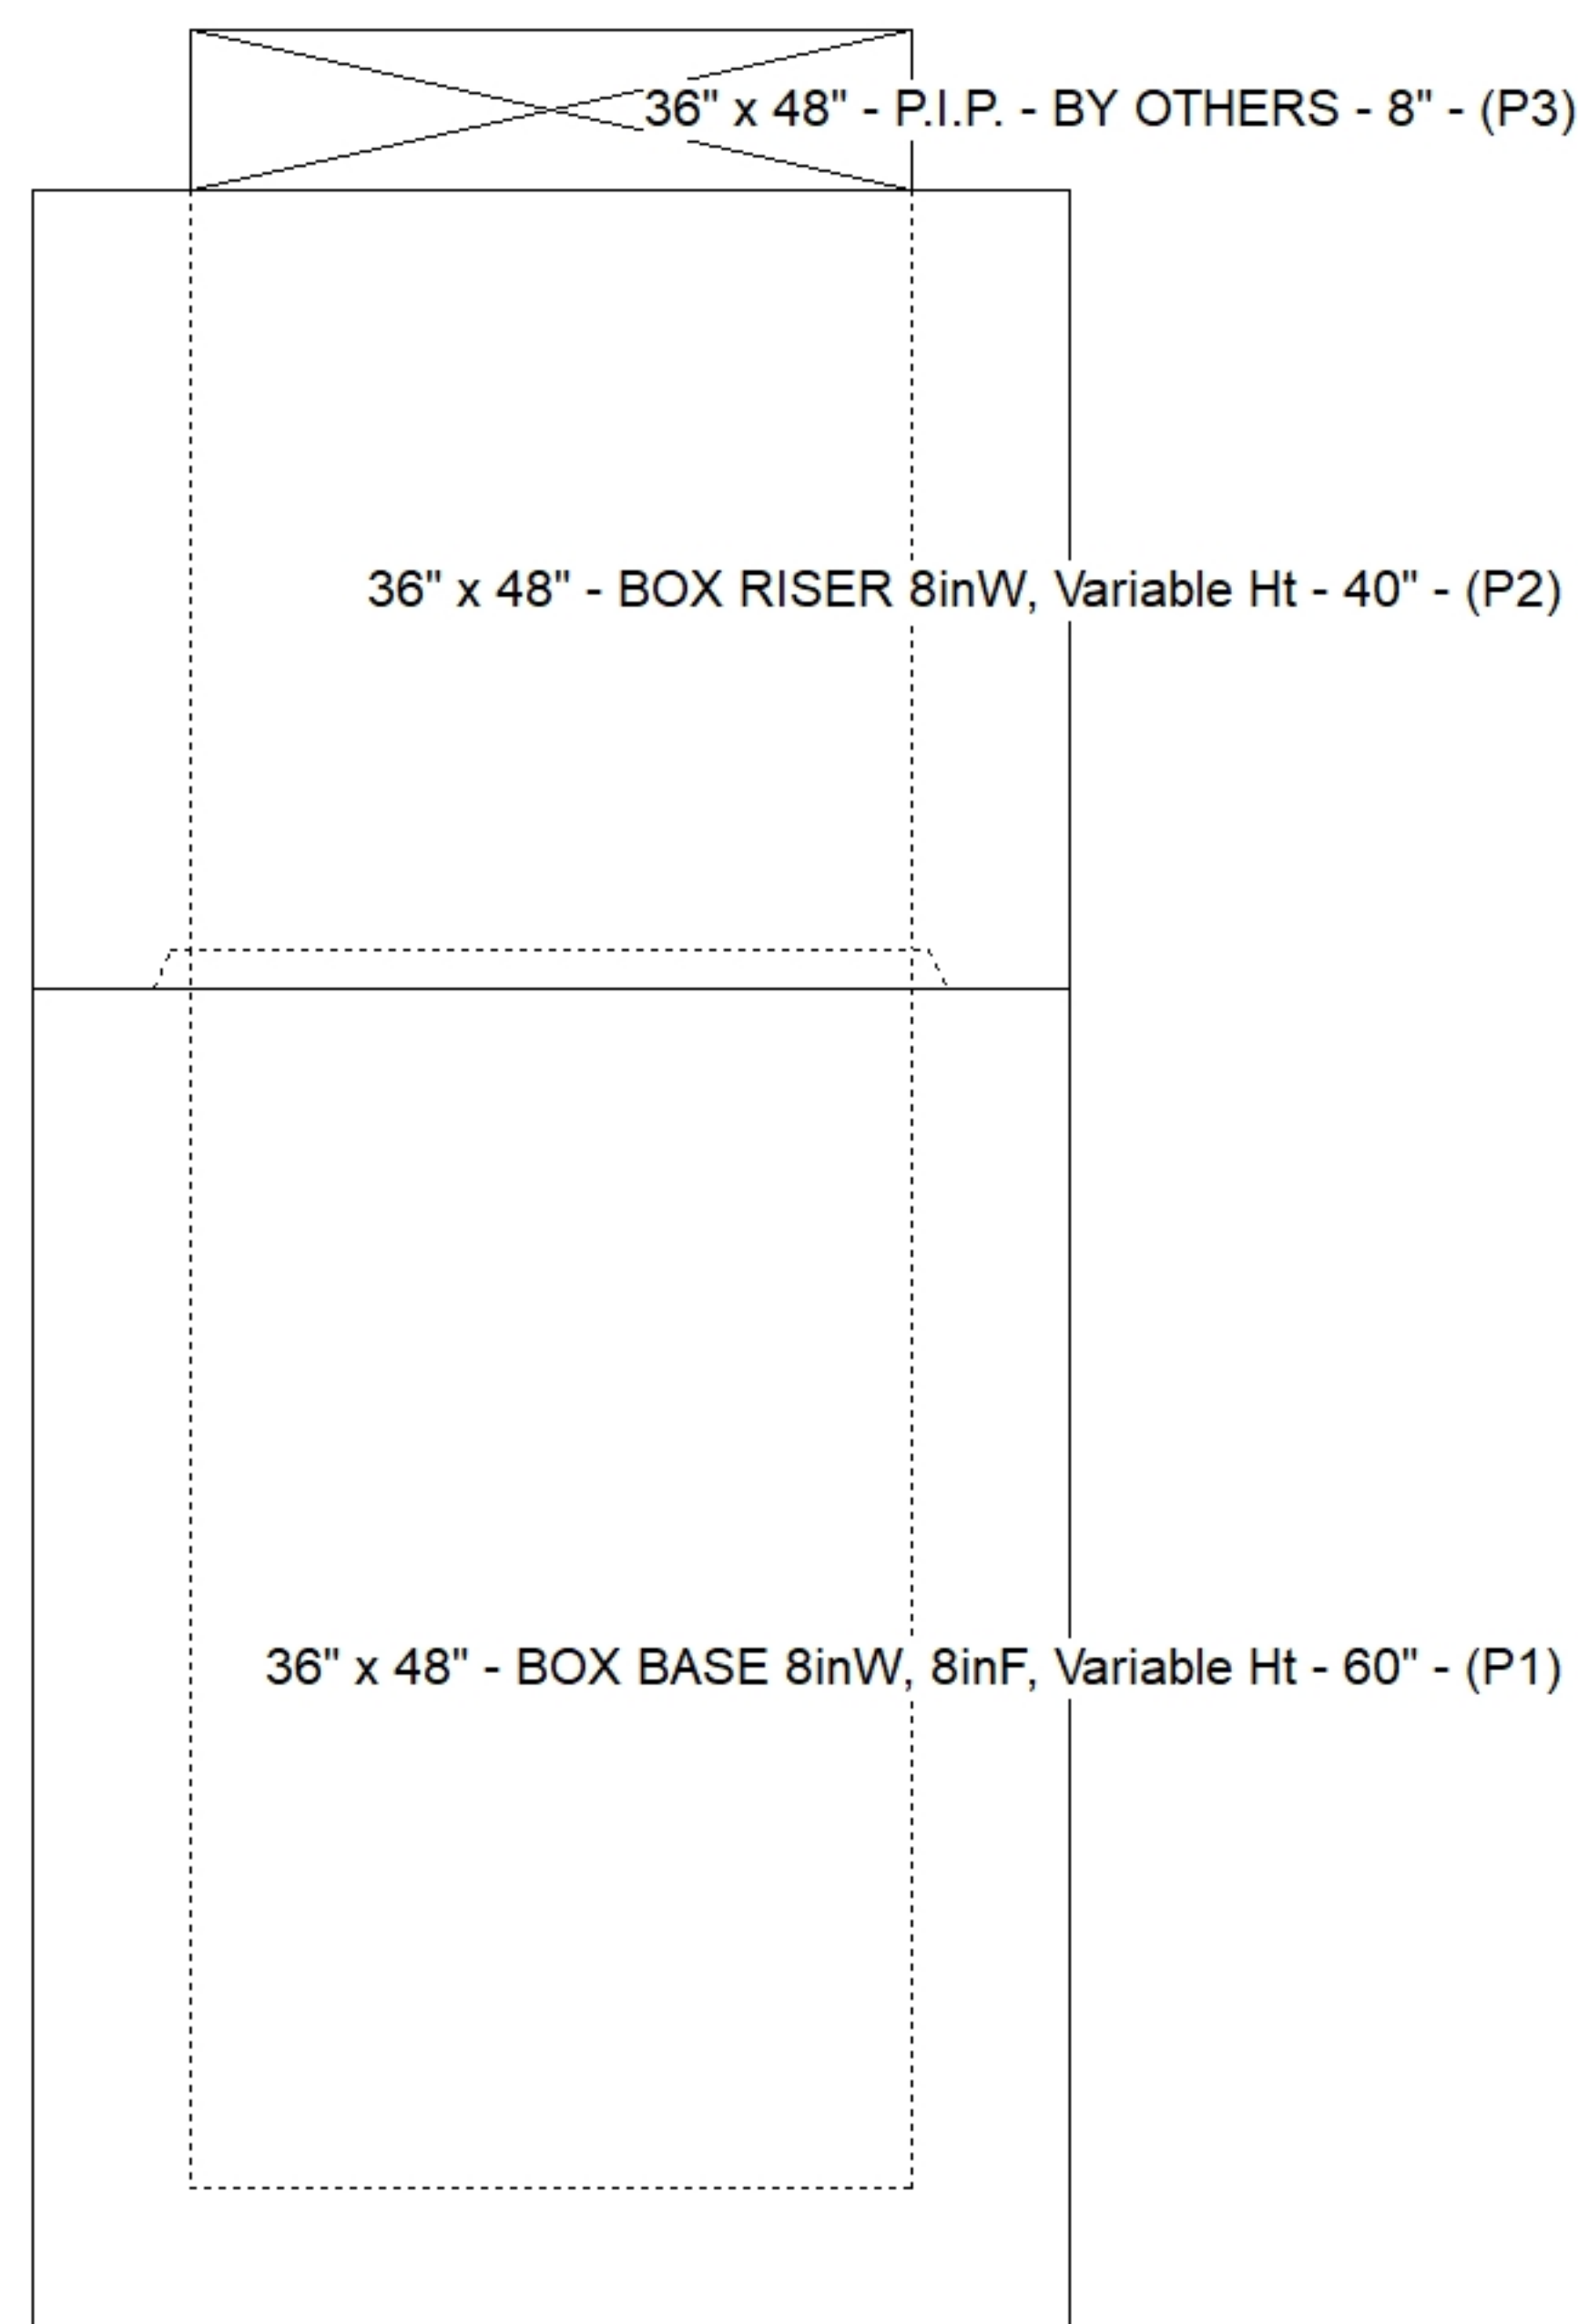

Default - Interior Dimensions

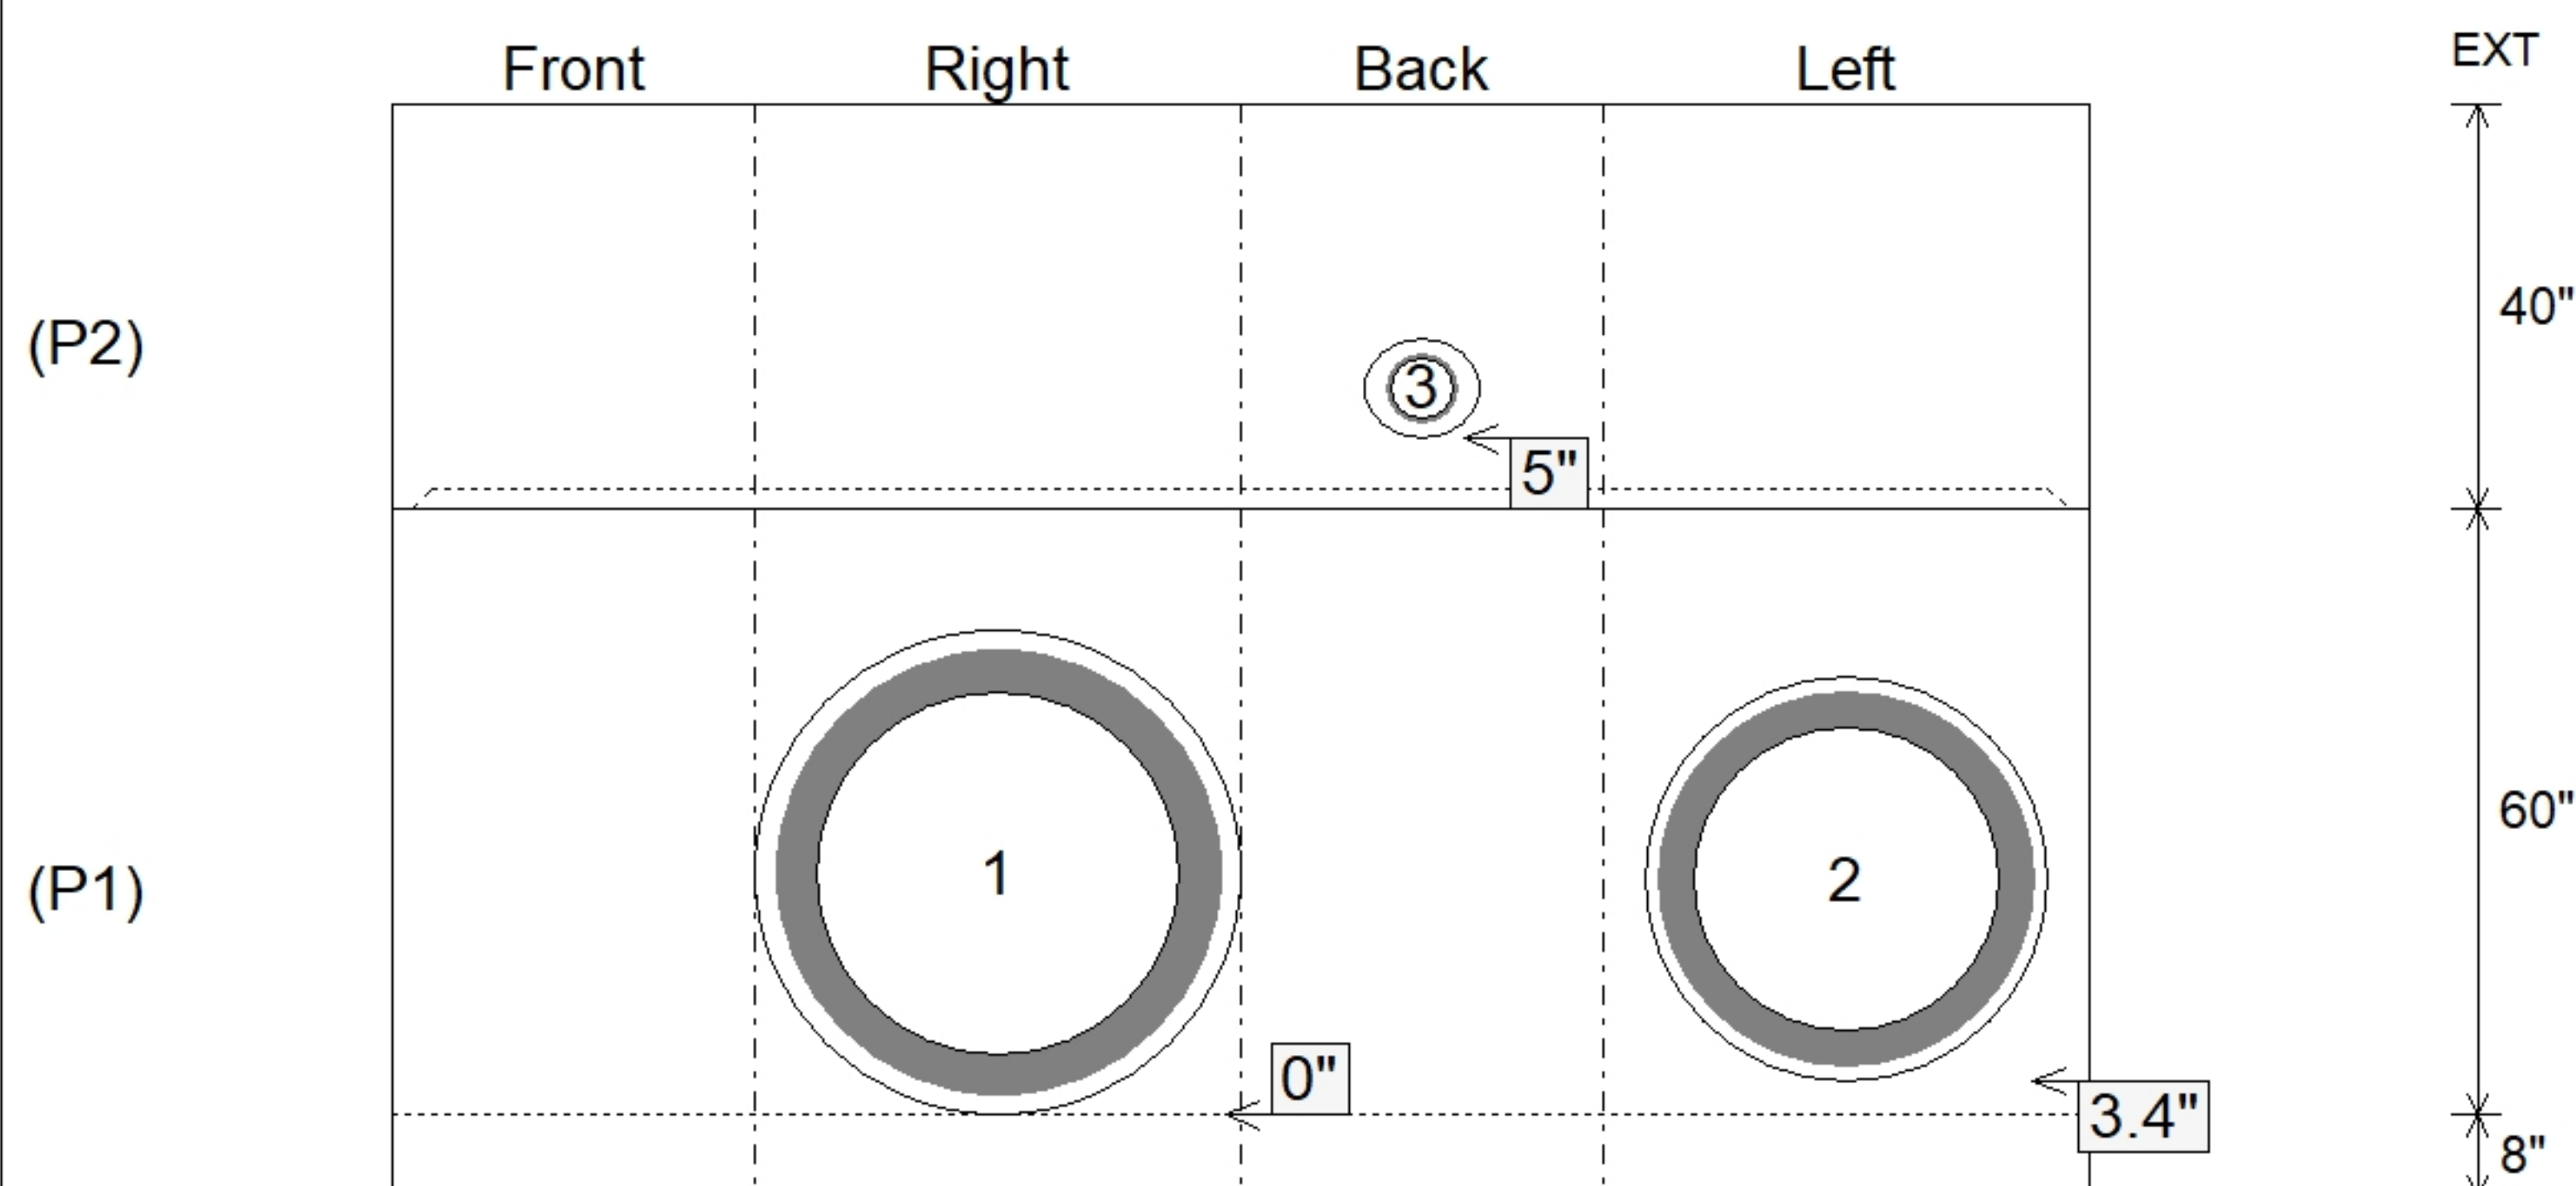

Submittal Drawing
8/3/2026 2:43:22 PM

SUBMITTAL
APPROVED BY:
