



Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:49 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: C2 DBI7										
P2 BX3654-08R-VH		BOX RISER 8inW, Variable Ht F/G								
P3) 36" x 36" - P.I.P. - BY OTHERS - 8" P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 42" P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70" 1) CASTING - HOE KY-328 SET (DBI 7) 2) 36" x 54" - Conseal CS-102 1.00" 1) Hole - 54 1) Hole - 48 1) Hole - 10					0 lb 5916 lb 10038 lb 328 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 16282 lb		Structure Notes: 1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 368.27' Rim to Invert: 9.56' Slack: 0.72" Sump: 6" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3	365'	210°	28.875"	6" HDPE	6.9"	Hole 10	10"	11.547"	6.5"	-15"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


#5 DOWELS @ 12" O.C. STUBBED 20" OUT THE TOP OF THE WALLS

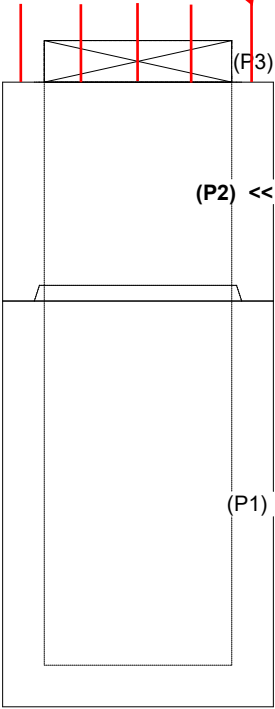

RIGHT-SIDE UP VIEW (int. dimensions)

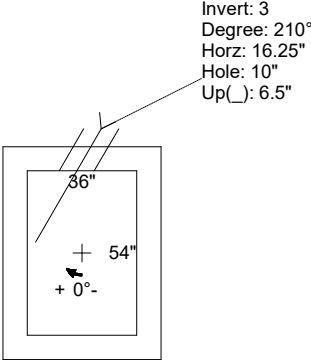

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 42" Height (Ext): 42"	Weight (Net): 5916 lb Volume (Net): 1.51cu.yd
----------------------------------	----------------------------------	--	--	--
