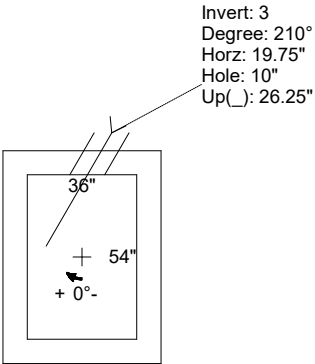



Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:49 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: C3 DBI7											
P2 BX3654-08R-VH		BOX RISER 8inW, Variable Ht F/G									
P3) 36" x 36" - P.I.P. - BY OTHERS - 8" P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 50" P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70" 1) CASTING - HOE KY-328 SET (DBI 7) 2) 36" x 54" - Conseal CS-102 1.00" 2) Hole - 54 1) Hole - 10					0 lb 7055 lb 10099 lb 328 lb 0 lb 0 lb 0 lb ----- Structure Total: 17482 lb		Structure Notes: . 1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 367.96' Rim to Invert: 10.2' Slack: 0.4" Sump: 6" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3	365.7'	210°	32.375"	6" HDPE	6.9"	Hole 10	10"	11.547"	26.25"	-12"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
#5 DOWELS @ 12" O.C. STUBBED 20" OUT THE TOP OF THE WALLS RIGHT-SIDE UP VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 50" Height (Ext): 50"		Weight (Net): 7055 lb Volume (Net): 1.8cu.yd		
