



Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:13 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: C4 DBI7										
P1 BX6072-08W08F-BAVF BOX BASE 8inW, 8inF, Variable Ht T/n										
P3) 36" x 36" - P.I.P. - BY OTHERS - 8" P2) 60" x 72" - BOX RISER 8inW, Variable Ht F/G - 55" P1) 60" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 82" 1) CASTING - HOE KY-328 SET (DBI 7) 2) 60" x 72" - Conseal CS-102 1.00" 1) Hole - 62 1) Hole - 40 1) Hole - 54 1) Hole - 10					0 lb 10876 lb 15713 lb 328 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 26917 lb		Structure Notes: 1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 368.36' Rim to Invert: 11.55' Slack: 0.6" Sump: 7" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	356.81'	60°	39.375"	48" RCP B WALL	58"	Hole 62	62"	71.591"	0"	15"
Invert 2	358.7'	315°	29.375"	30" RCP B WALL	37"	Hole 40	40"	56.569"	24.625"	25"
Invert 3	357.01'	270°	44"	42" RCP B WALL	51"	Hole 54	54"	54"	3.375"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

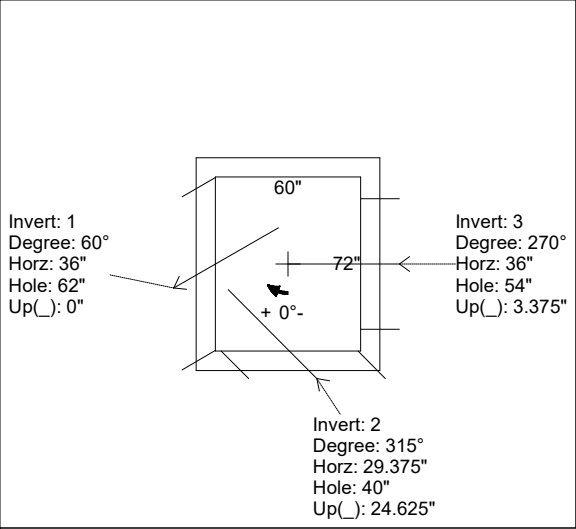


RIGHT-SIDE UP VIEW (int. dimensions)

WEIGHTS
FIRST POUR - 4,489 LBS
SECOND POUR - 11,224 LBS
TOTAL - 15,713 LBS

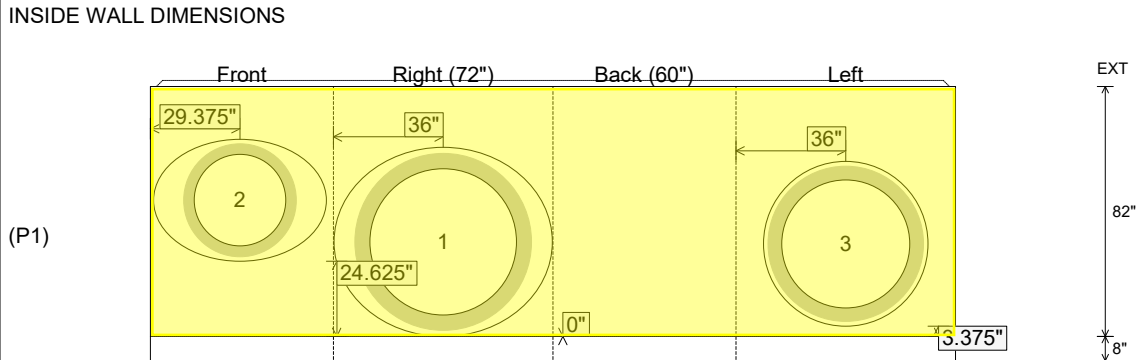

INSIDE WALL DIMENSIONS

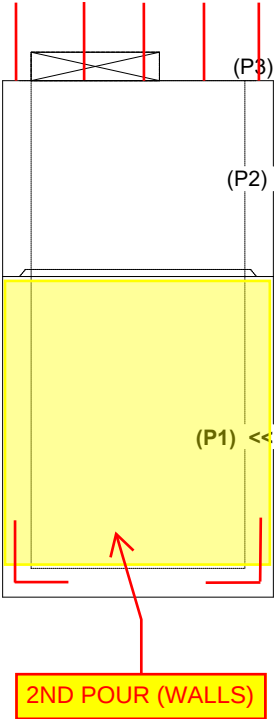

2ND POUR (WALLS)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 82" Height (Ext): 90"	Weight (Net): 15713 lb Volume (Net): 4.01cu.yd
----------------------------------	---------------------------------	--	--	---
