

Contractor: M. Bowling, Inc.

TECH: Jared - F

Plant: 100



Size: 60" x 72"

Rim to Invert: 11.55'

Floor Height: 8"

Slack: 0.6"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
P2) 60" x 72" - BOX RISER 8inW, Variable Ht - 55"
P1) 60" x 72" - BOX BASE 8inW, 8inF, Variable Ht - 82"

1) SECONDARY POUR - Walls
1) CASTING - HOE KY-328 SET (DBI 7)
2) 60" x 72" - Conseal CS-102 1.00"

1) Hole - 62
1) Hole - 40
1) Hole - 54
1) Hole - 10



0 lb
10876 lb
15713 lb
0 lb
328 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 26917 lb

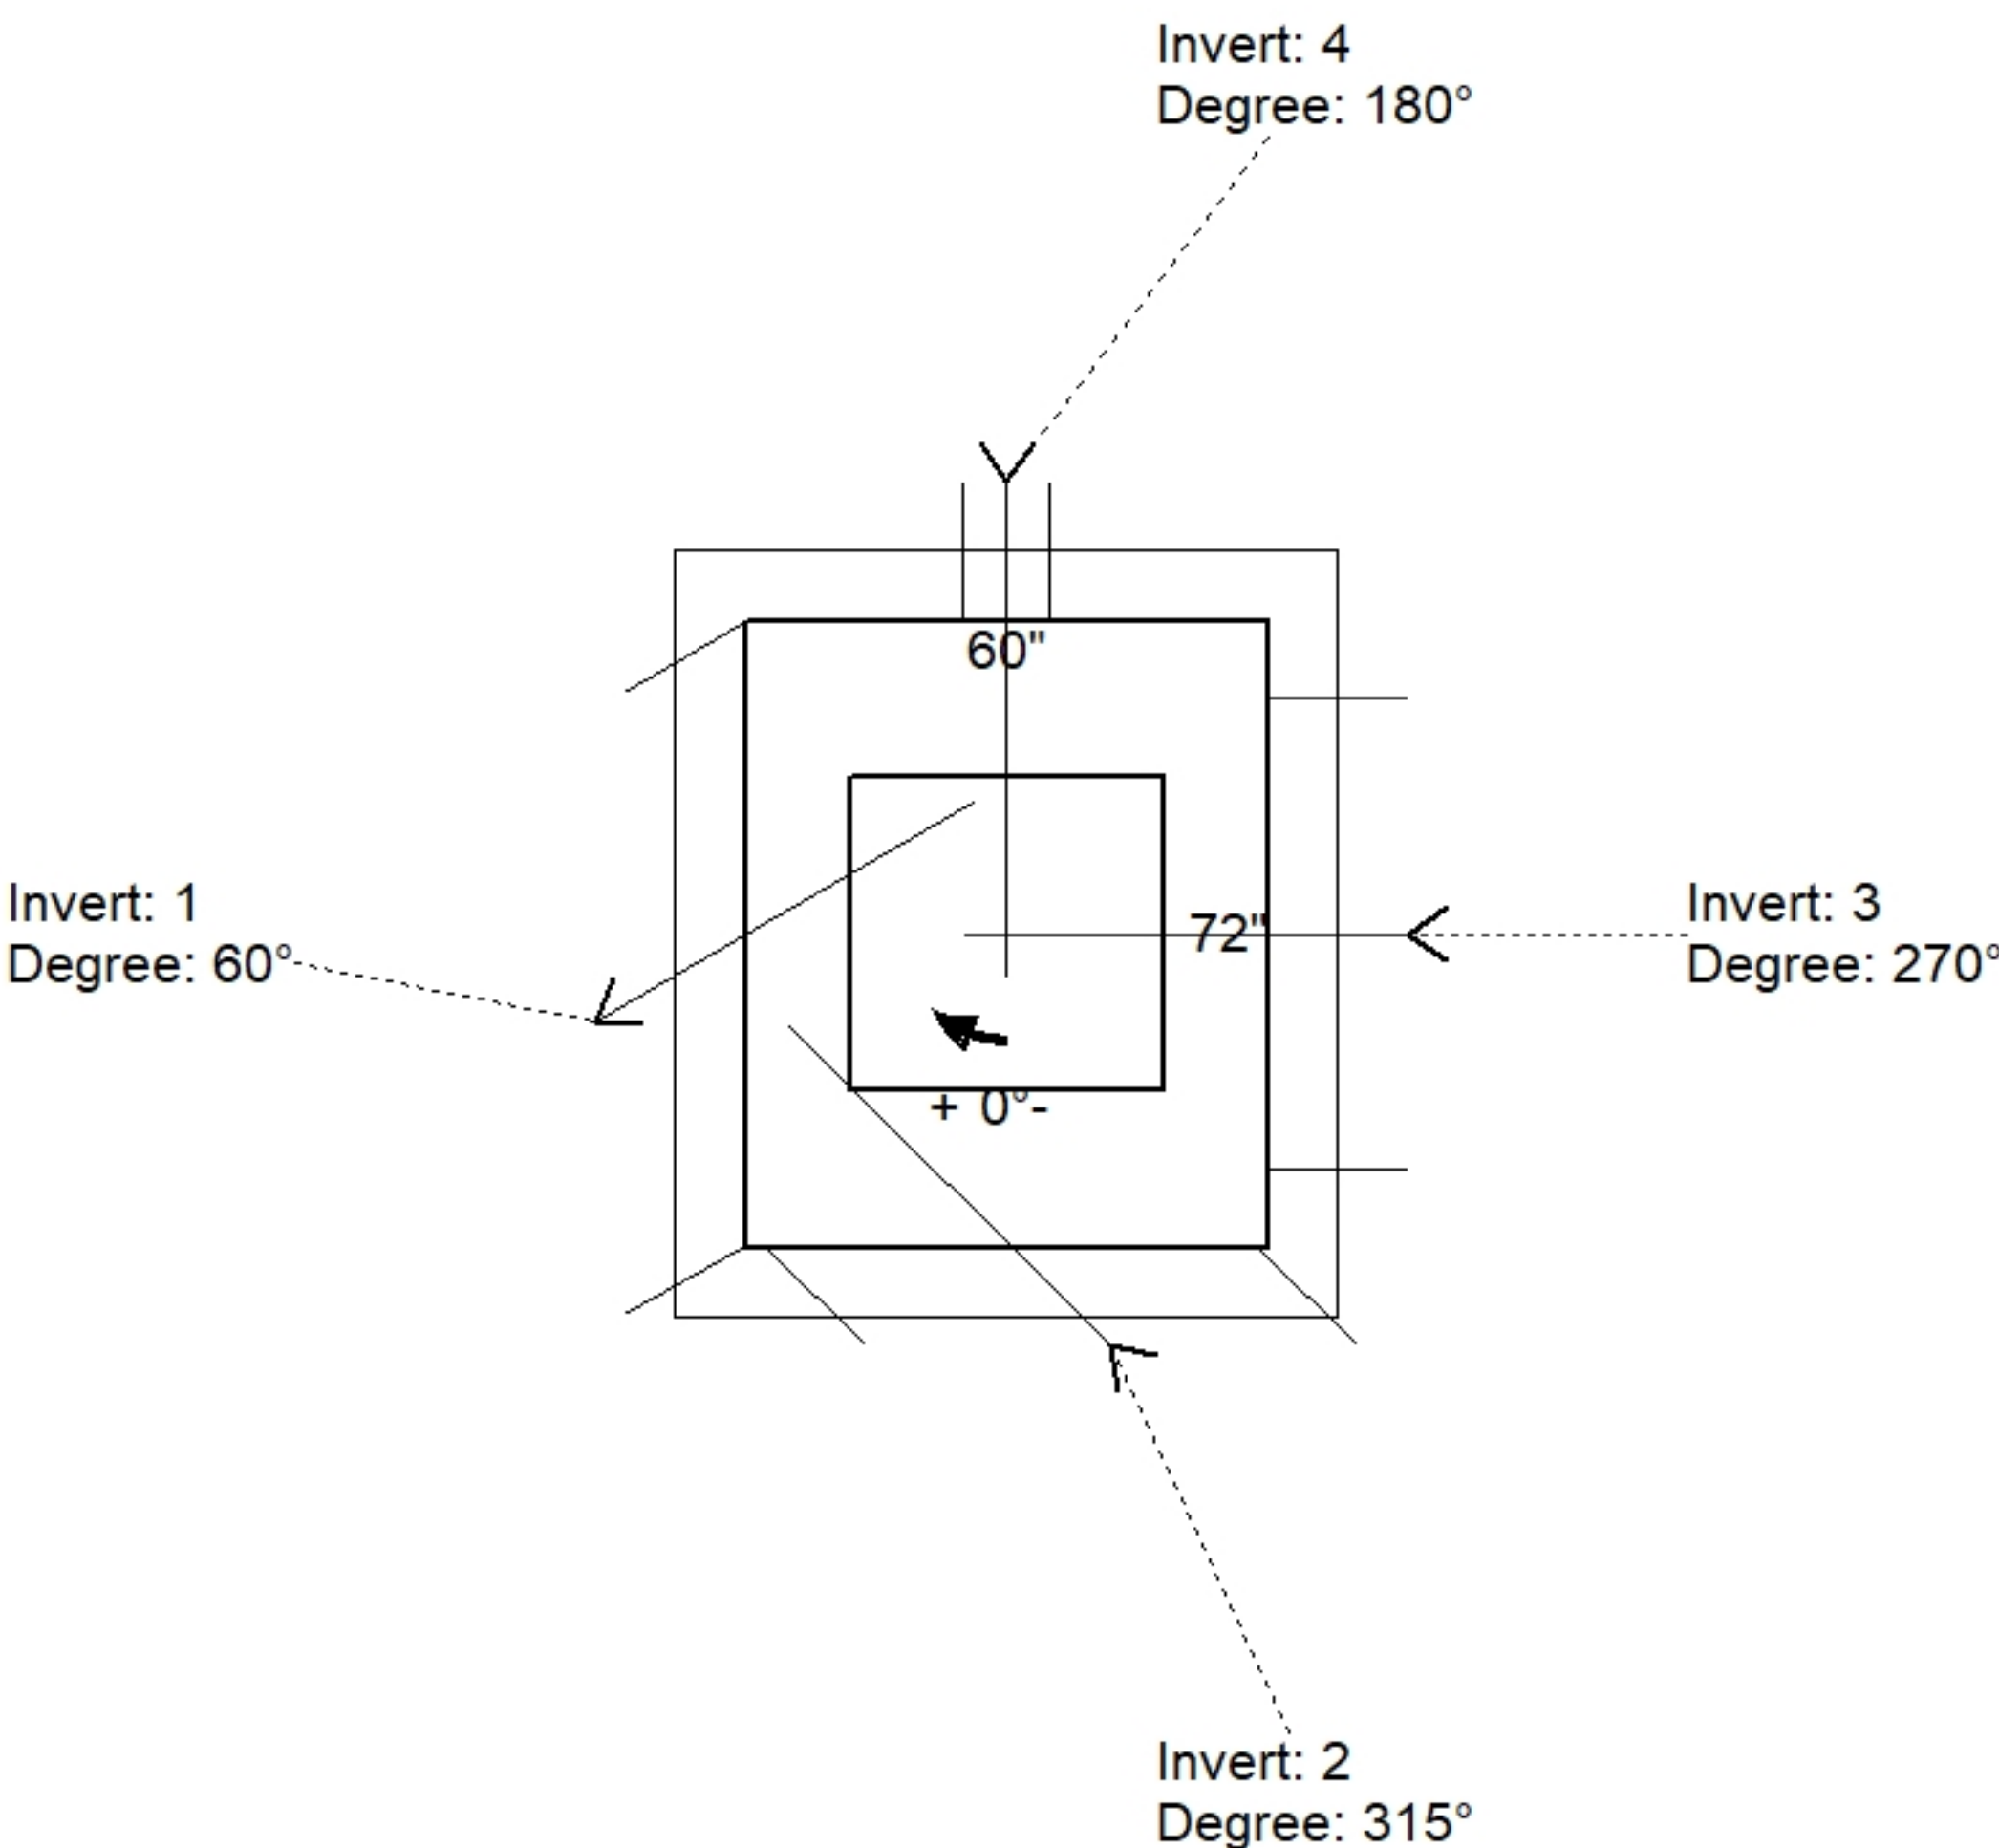

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	368.36'							
Reducer								
Invert 1	356.81'	60°	48" RCP B WALL	58"	62"	Hole 62	0"	P1
Invert 2	358.7'	315°	30" RCP B WALL	37"	40"	Hole 40	24.68"	P1
Invert 3	357.01'	270°	42" RCP B WALL	51"	54"	Hole 54	3.4"	P1
Invert 4	365.23'	180°	6" HDPE	6.9"	10"	Hole 10	22.04"	P2
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

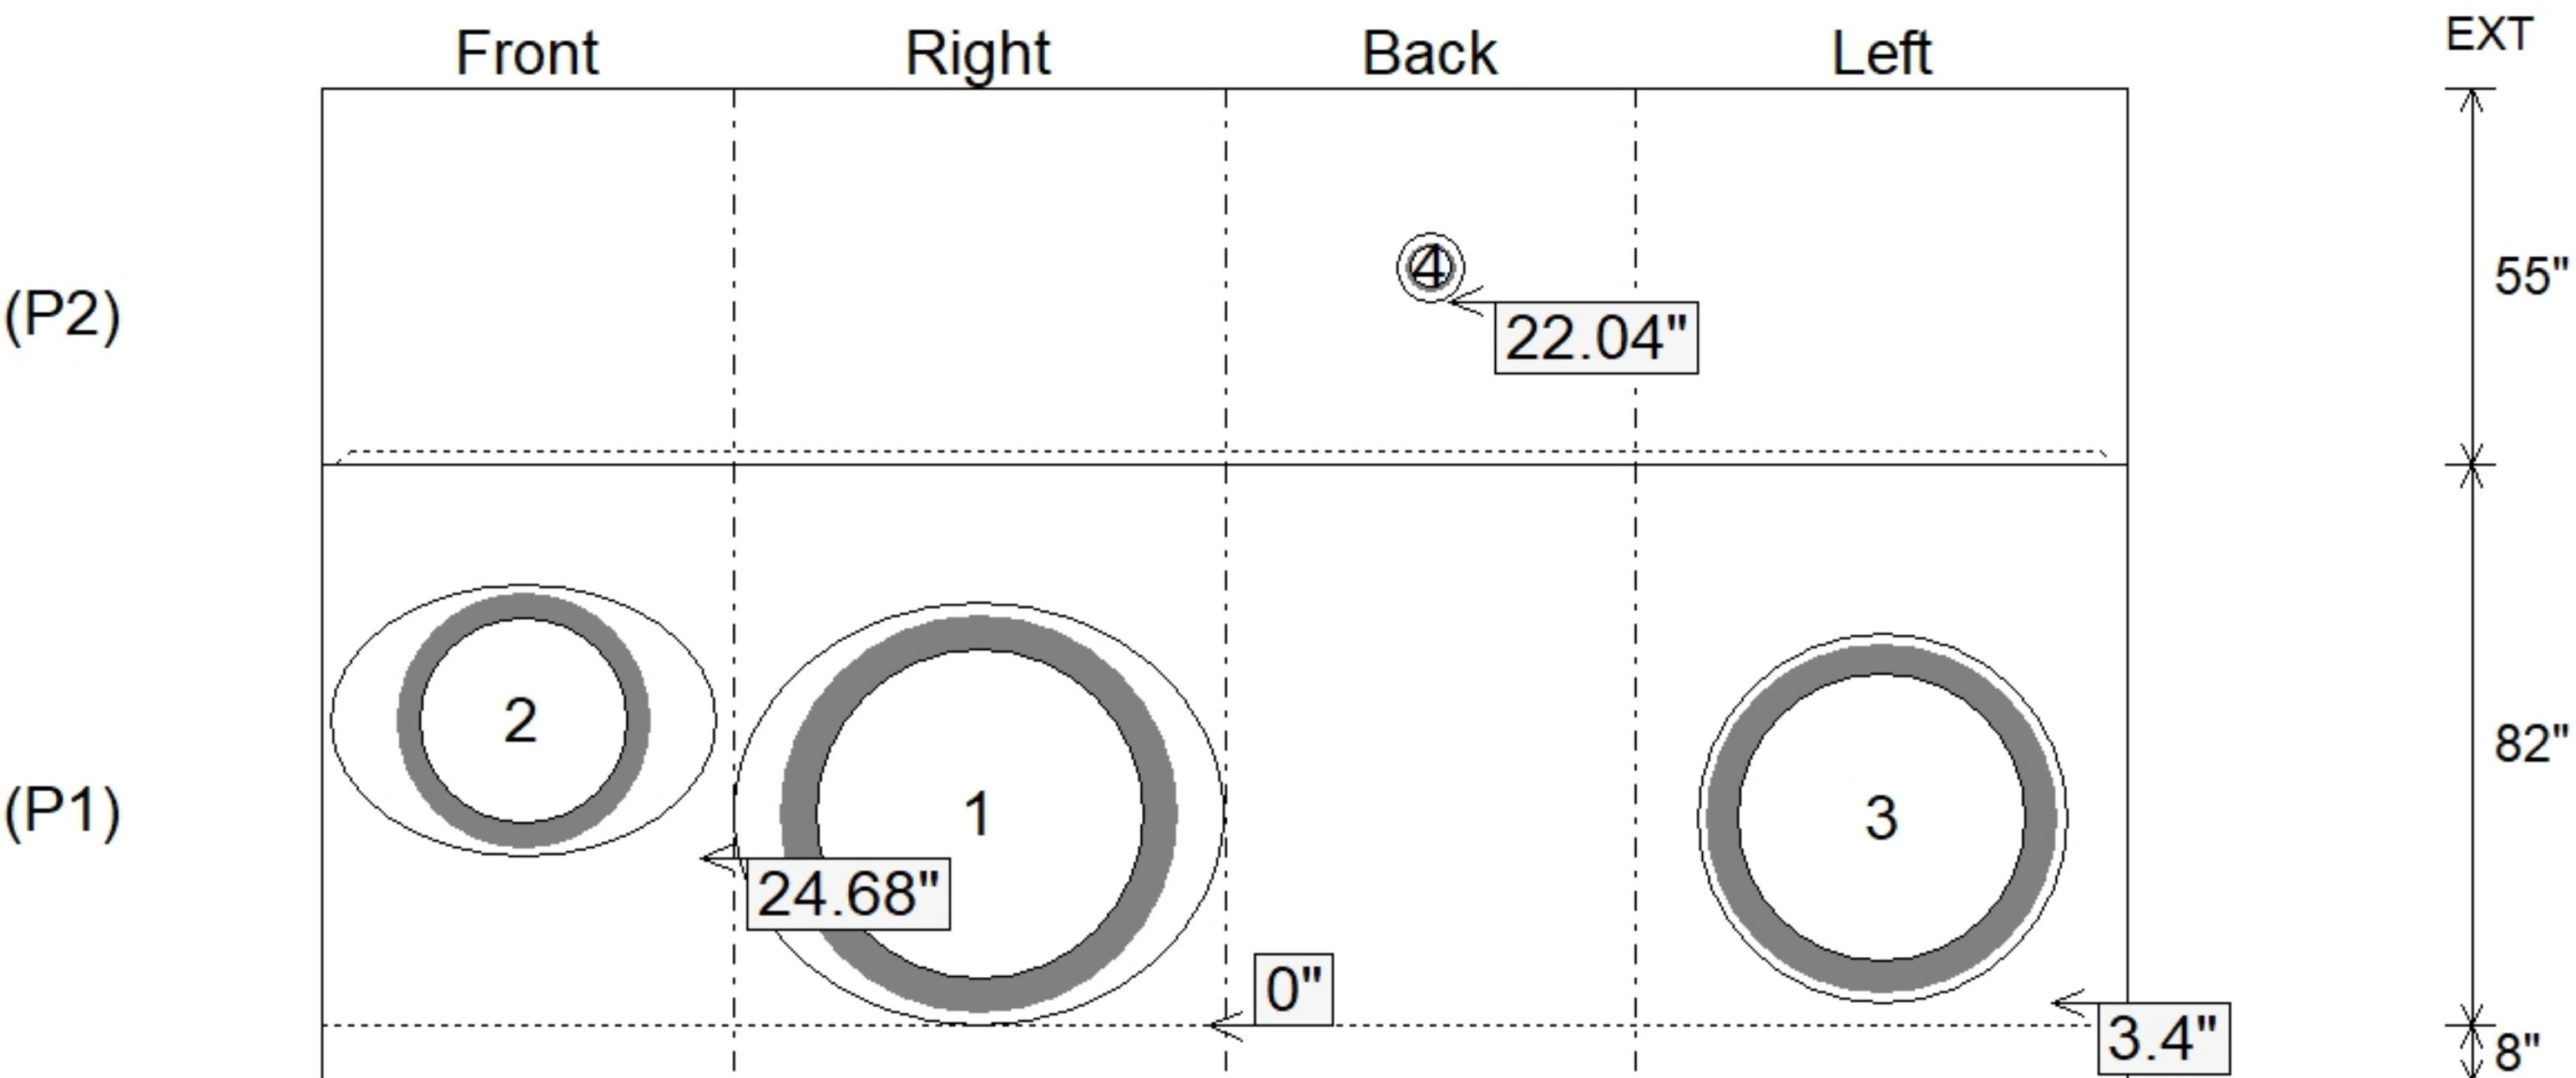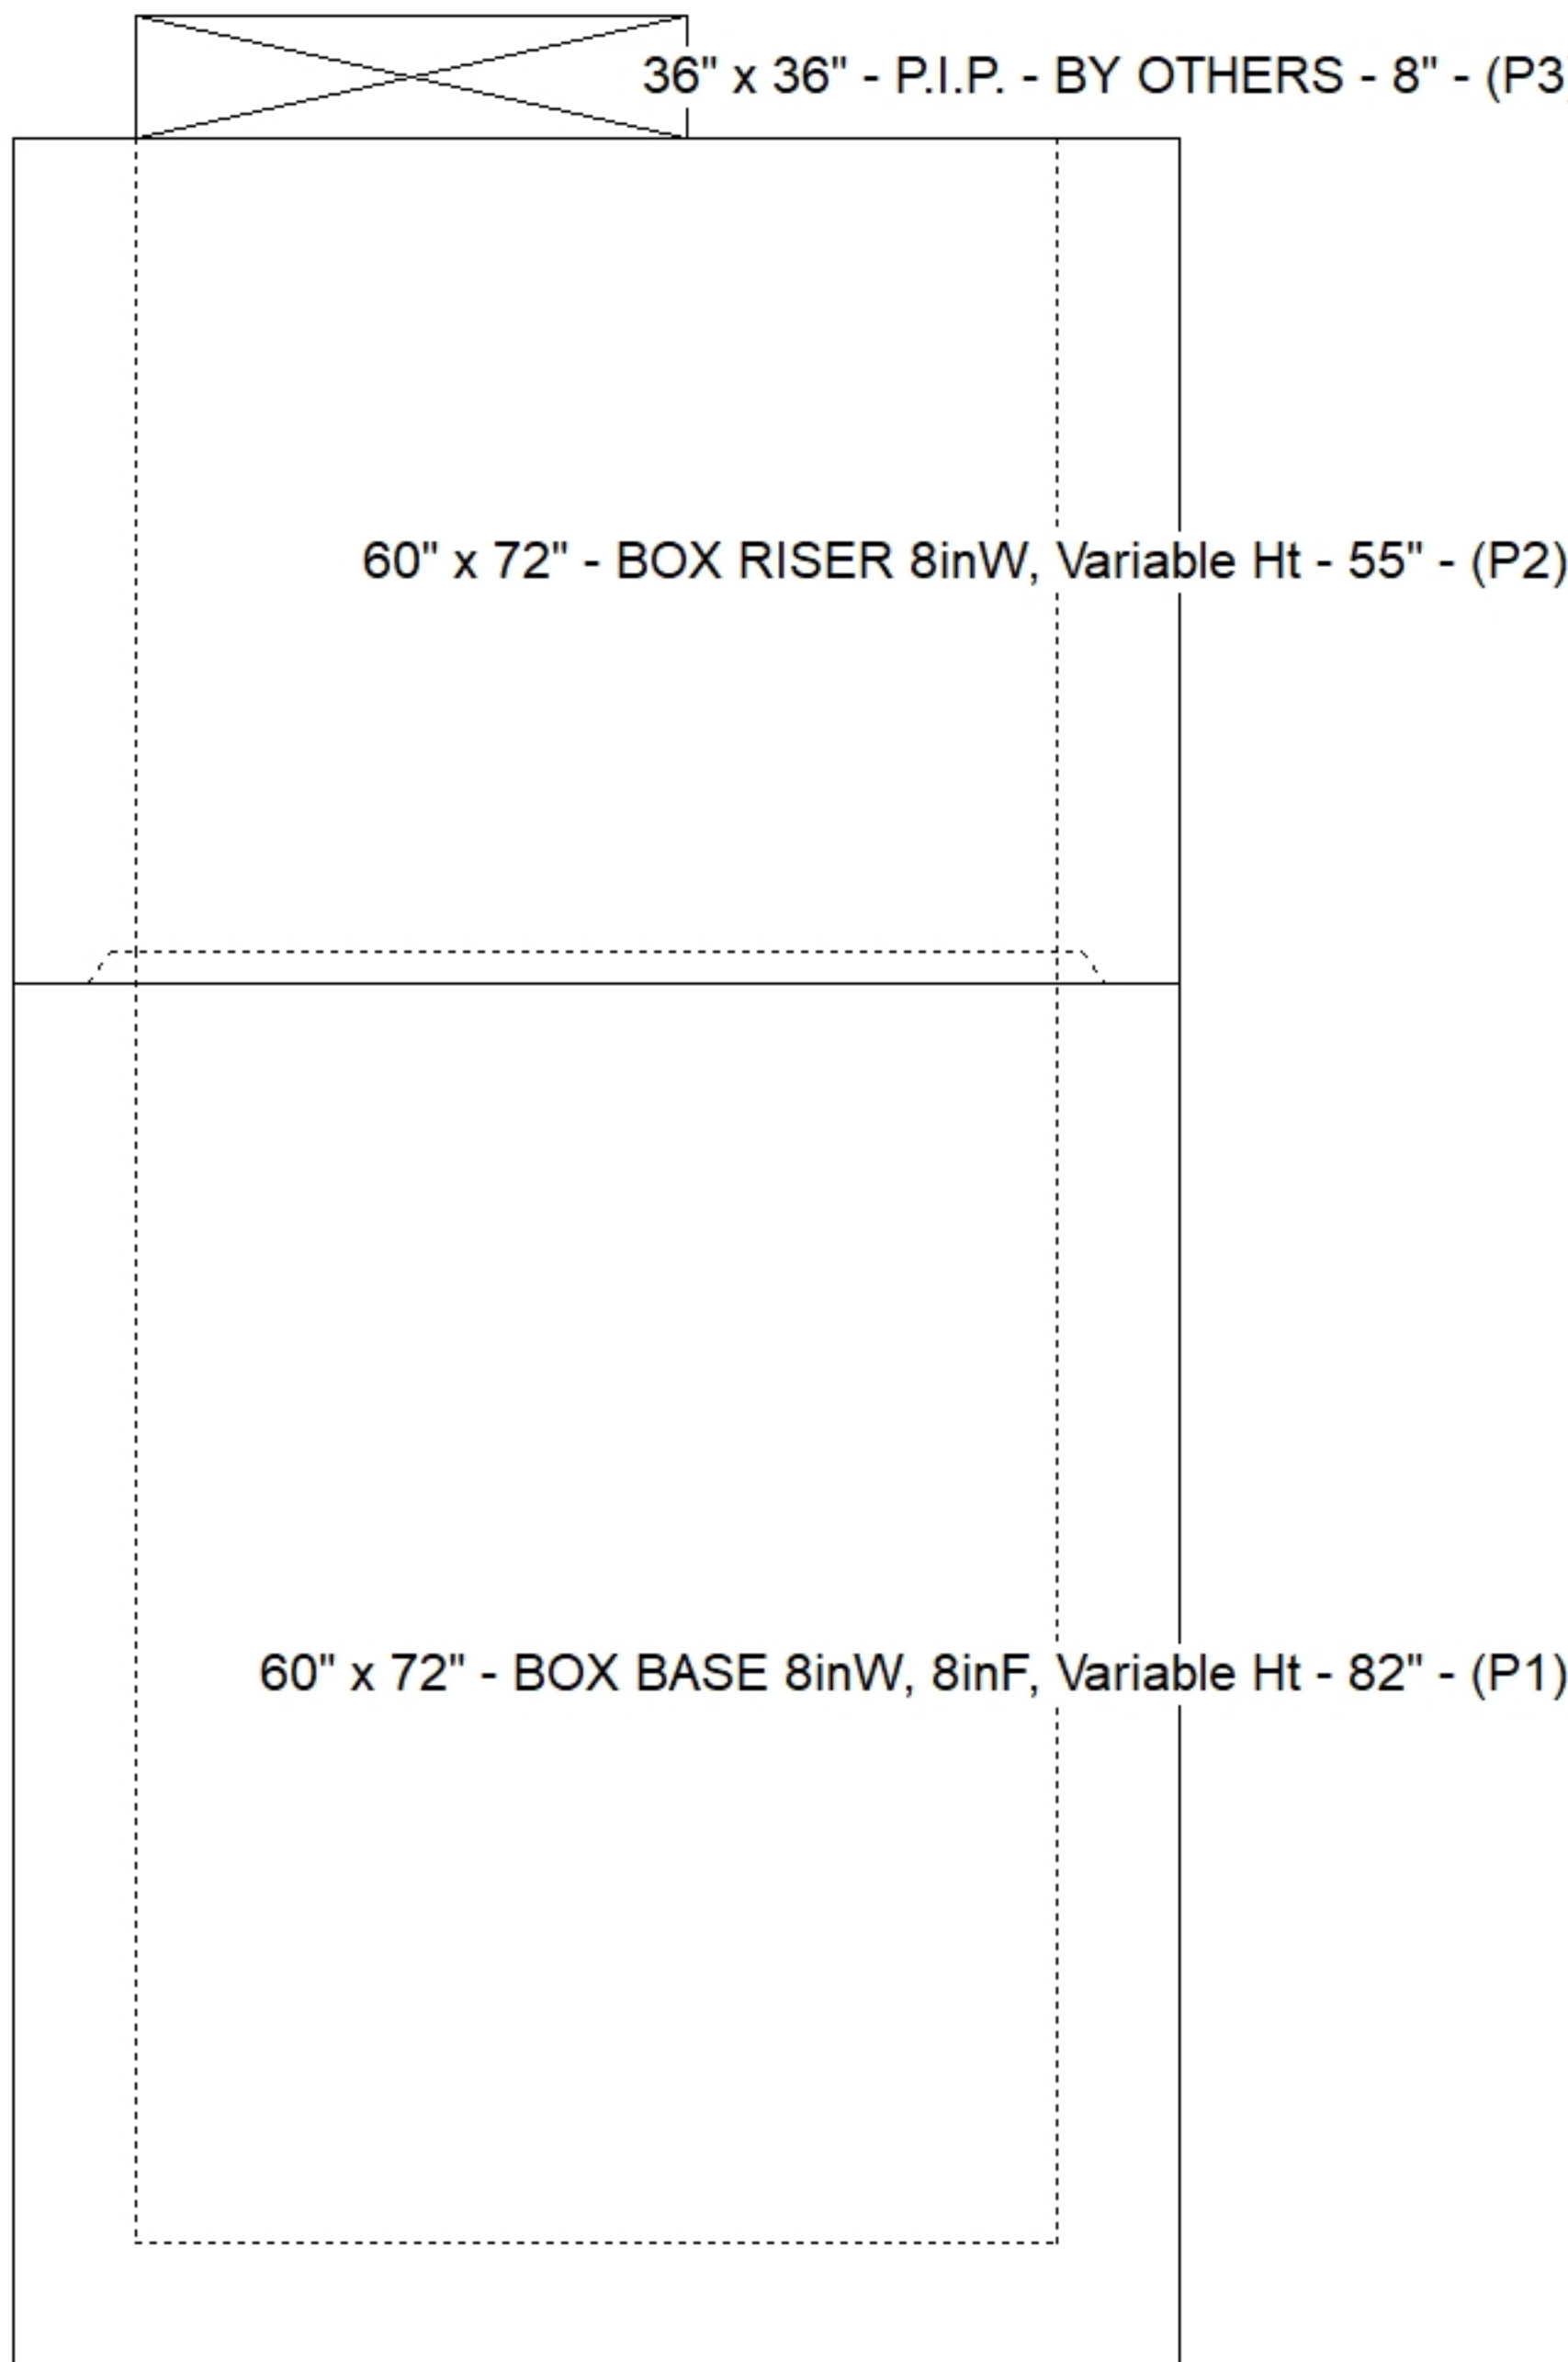

Submittal Drawing
8/3/2026 2:43:24 PM

SUBMITTAL
APPROVED BY:
