



Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 8/3/2026 12:43:26 PM		Tech: Jared - F PC: A. Chambers			
Structure ID: D1 DBI2										
P1 BX3648-08BA60 BOX BASE 8inW, 8inF F/n										
P2) 36" x 48" - P.I.P. - BY OTHERS - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60" 1) CASTING - HOE KY-398 SET (DBI 2) 1) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 10					0 lb 9393 lb 398 lb 0 lb 0 lb 0 lb ----- Structure Total: 9791 lb		Structure Notes: 1. KYTC DBI TYPE 2 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-398 SET (DBI 2)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 367.57' Rim to Invert: 5.36' Slack: 1.32' Sump: 5" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	362.21'	90°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	0"	0"
Invert 2	364.7'	180°	26"	6" HDPE	6.9"	Hole 10	10"	10"	32.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

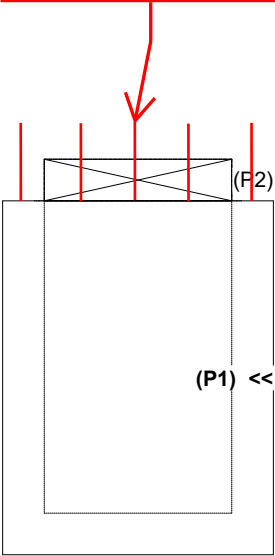


RIGHT-SIDE UP VIEW (int. dimensions)

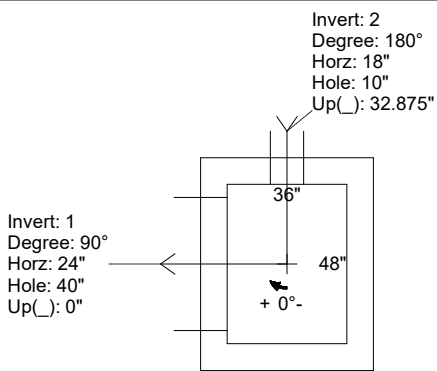

UPSIDE-DOWN VIEW (int. dimensions)

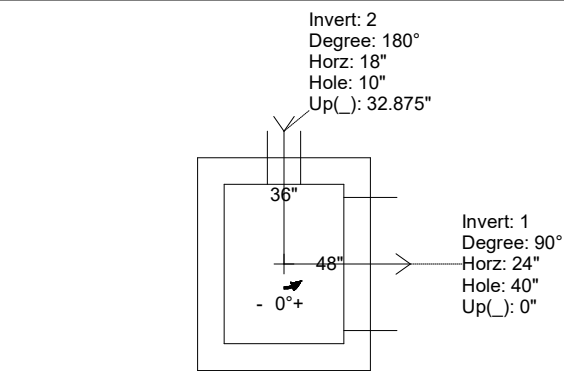

INSIDE WALL DIMENSIONS

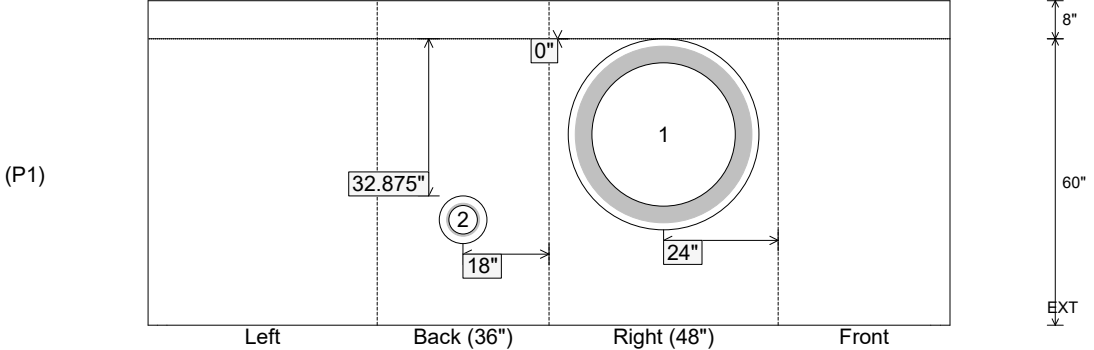

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 9393 lb Volume (Net): 2.4cu.yd
----------------------------------	-------------------------------	--	--	---
