




Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:09 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: D8 DBI2										
P1 BX3648-08BAVF BOX BASE 8inW, 8inF, Variable Ht T/n										
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW F/G - 36" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht T/n - 47" 1) CASTING - HOE KY-398 SET (DBI 2) 2) 36" x 48" - Conseal CS-102 1.00" 2) Hole - 40 1) Hole - 10					0 lb 4772 lb 6857 lb 398 lb 0 lb 0 lb 0 lb Structure Total: 12028 lb		Structure Notes: 1. KYTC DBI TYPE 2 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-398 SET (DBI 2)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 367.76' Rim to Invert: 7.17' Slack: 0.04" Sump: 5" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	360.59'	90°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	0"	0"
Invert 2	360.79'	270°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

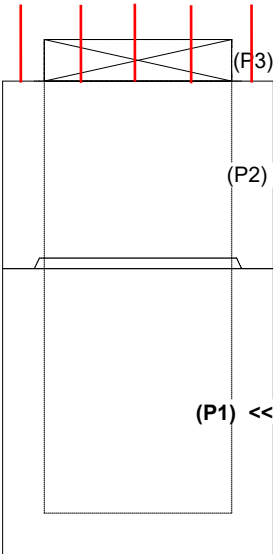

RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

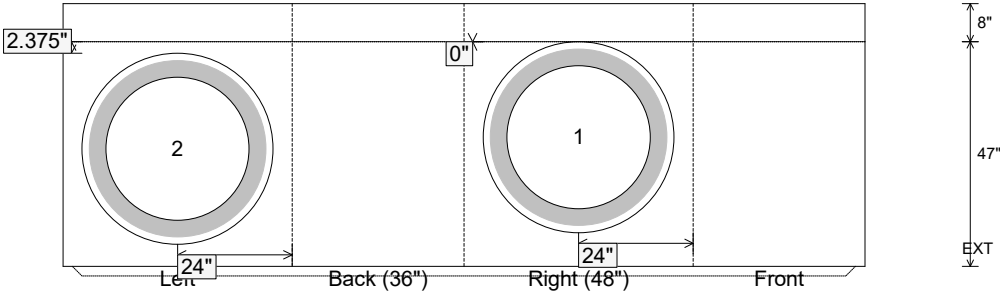

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 47" Height (Ext): 55"	Weight (Net): 6857 lb Volume (Net): 1.75cu.yd
----------------------------------	---------------------------------	--	--	--
