

Contractor: M. Bowling, Inc.

Plant: 100




Slack: 0.04"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 36" x 48" - P.I.P. - BY OTHERS - 8"
P2) 36" x 48" - BOX RISER 8inW, Variable Ht - 36"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 47"
1) CASTING - HOE KY-398 SET (DBI 2)
2) 36" x 48" - Conseal CS-102 1.00"
2) Hole - 40
1) Hole - 10



0 lb
4772 lb
6857 lb
398 lb
0 lb
0 lb
0 lb

Structure Total: 12028 lb

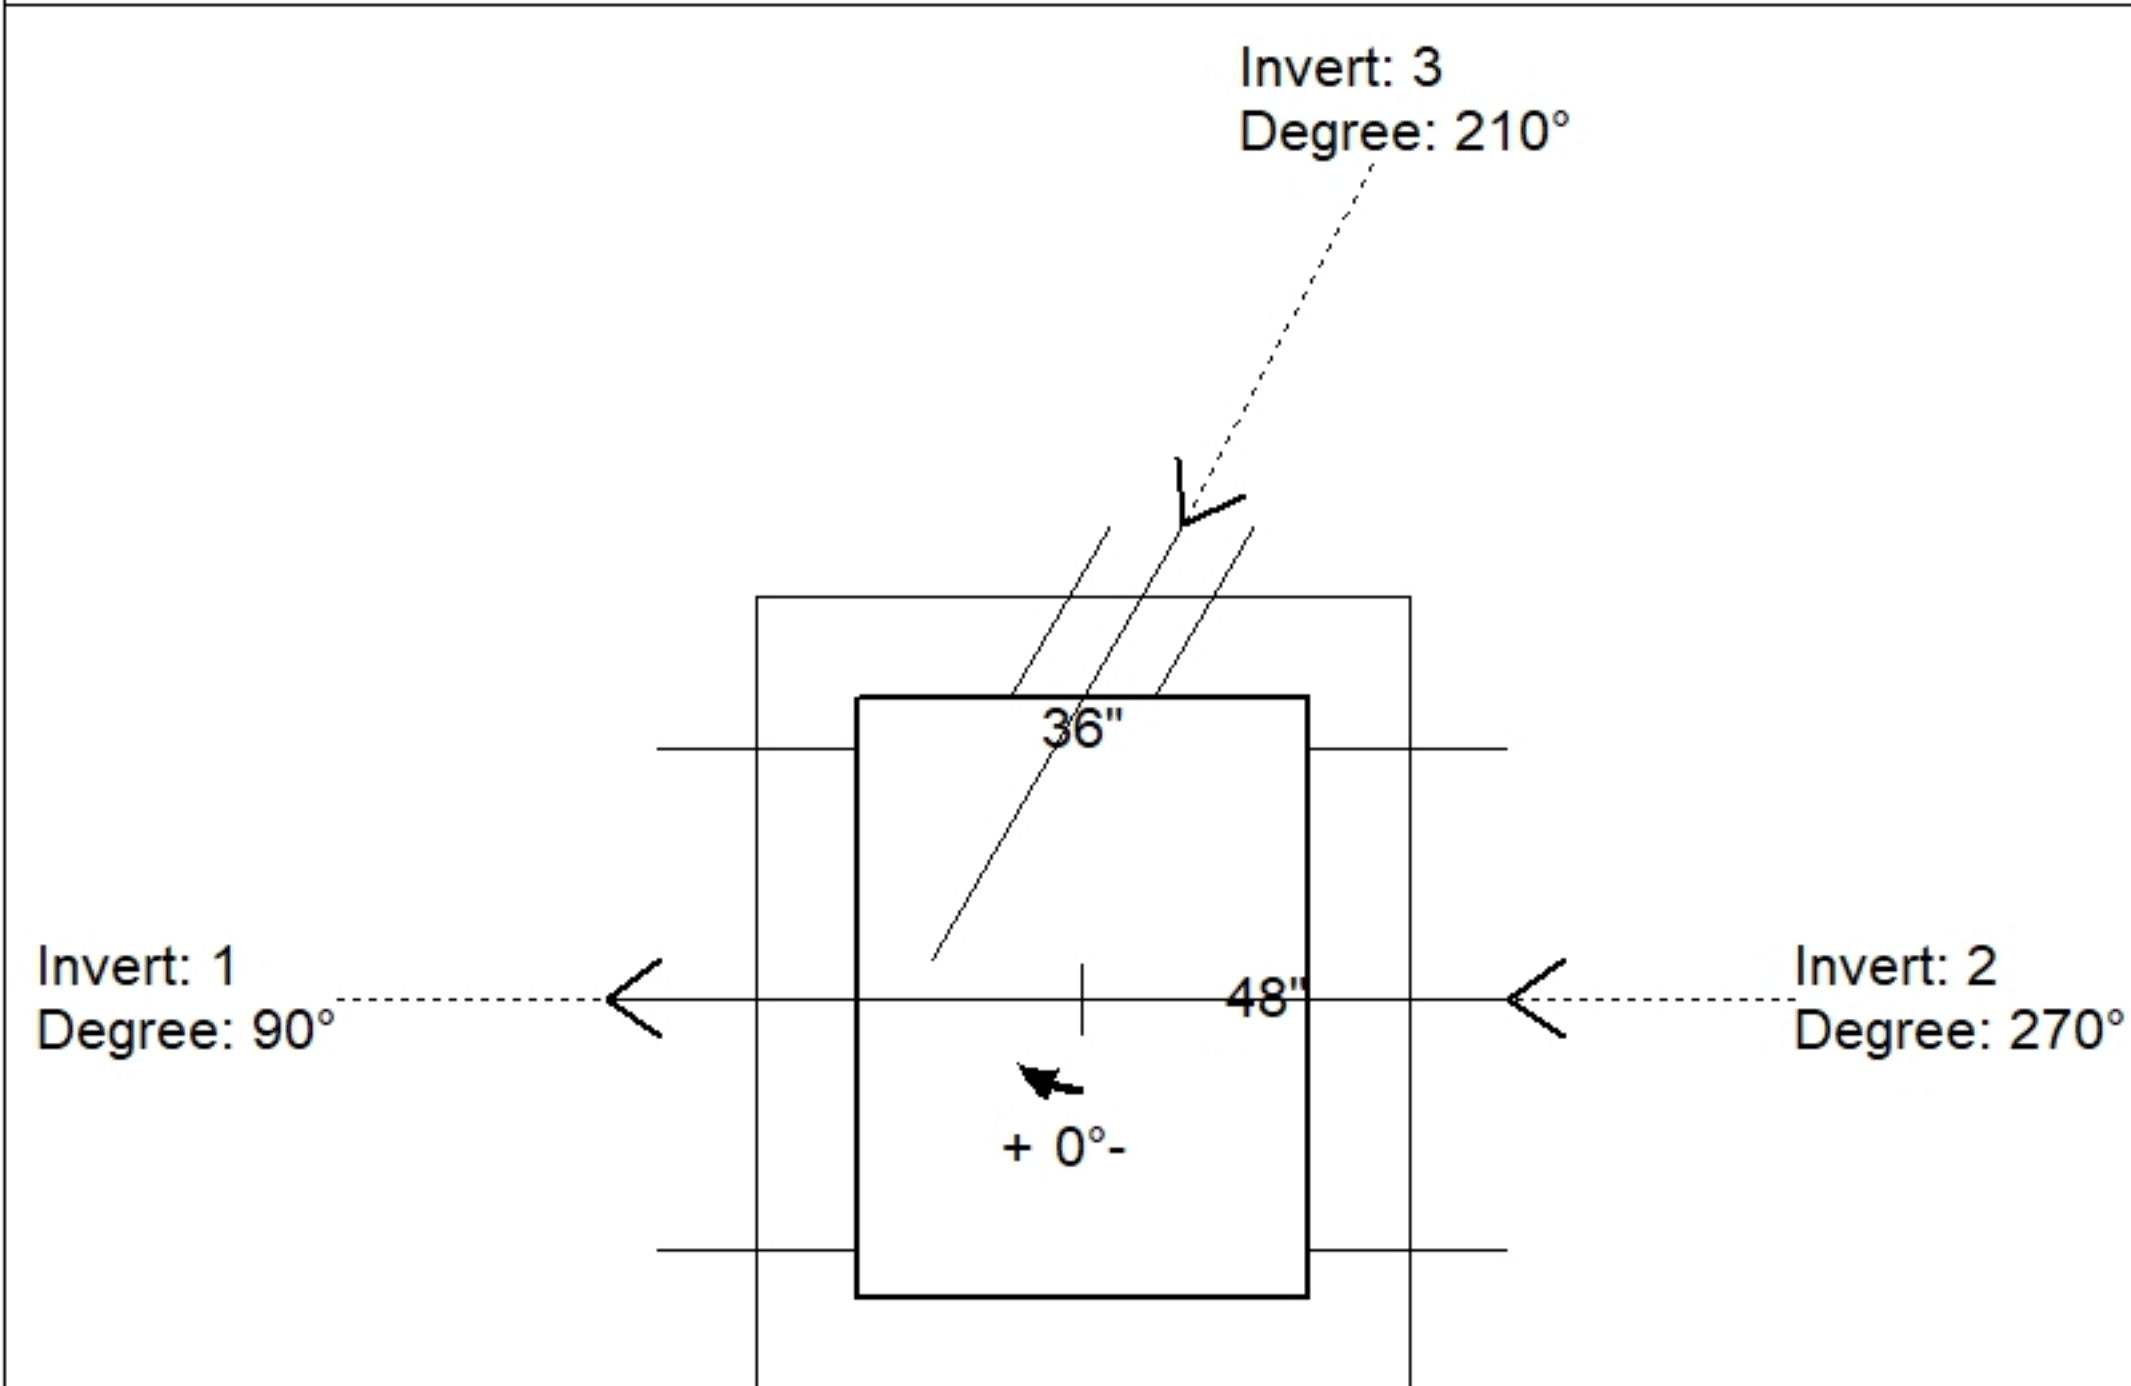

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	367.76'							
Reducer								
Invert 1	360.59'	90°	30" RCP B WALL	37"	40"	Hole 40	0"	P1
Invert 2	360.79'	270°	30" RCP B WALL	37"	40"	Hole 40	2.4"	P1
Invert 3	365.2'	210°	6" HDPE	6.9"	10"	Hole 10	9.32"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

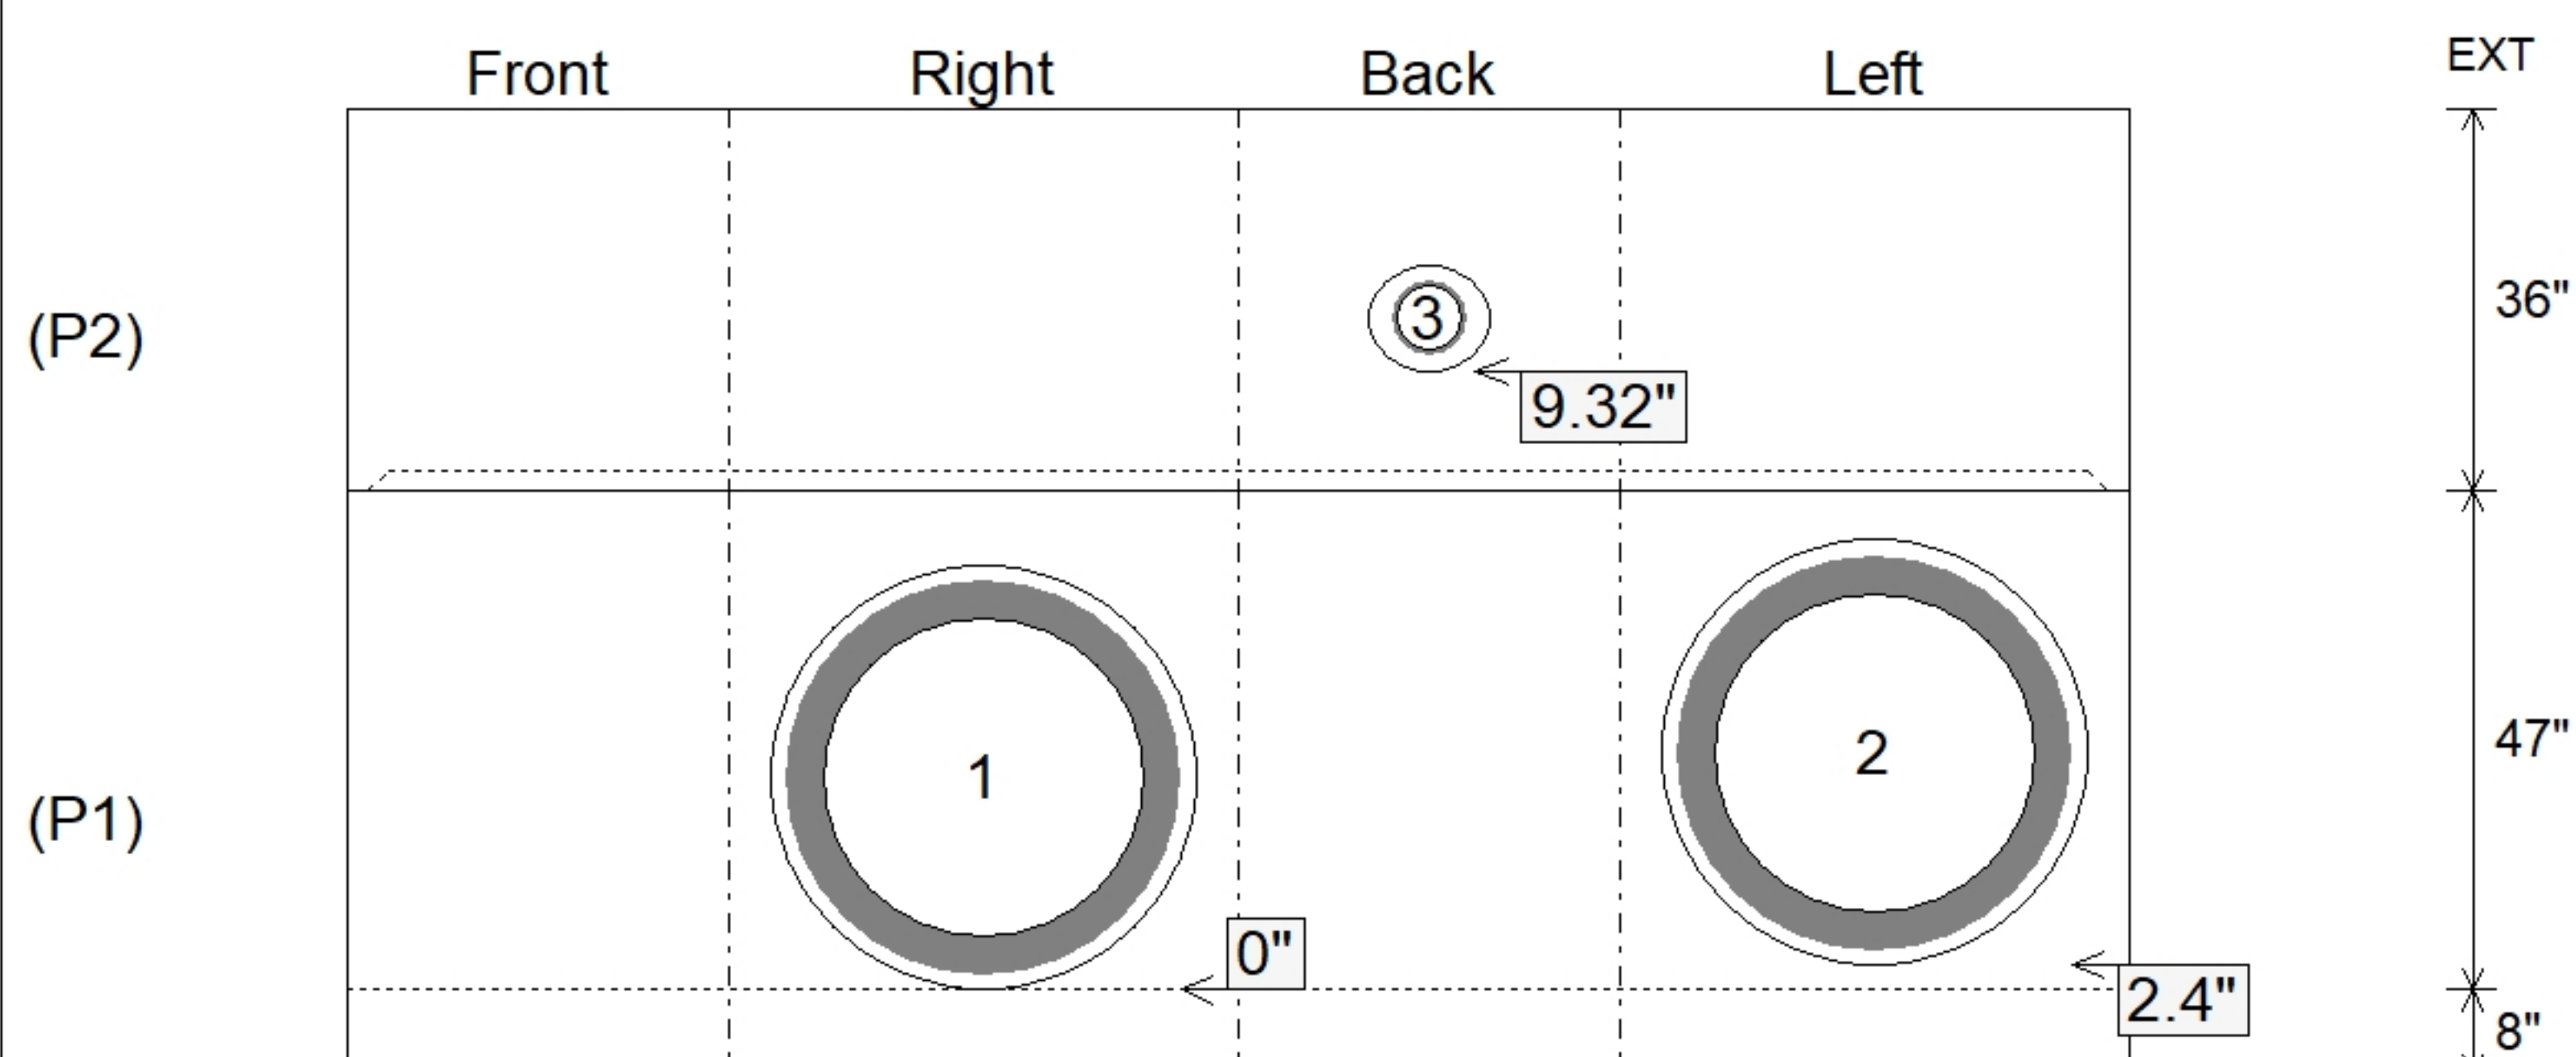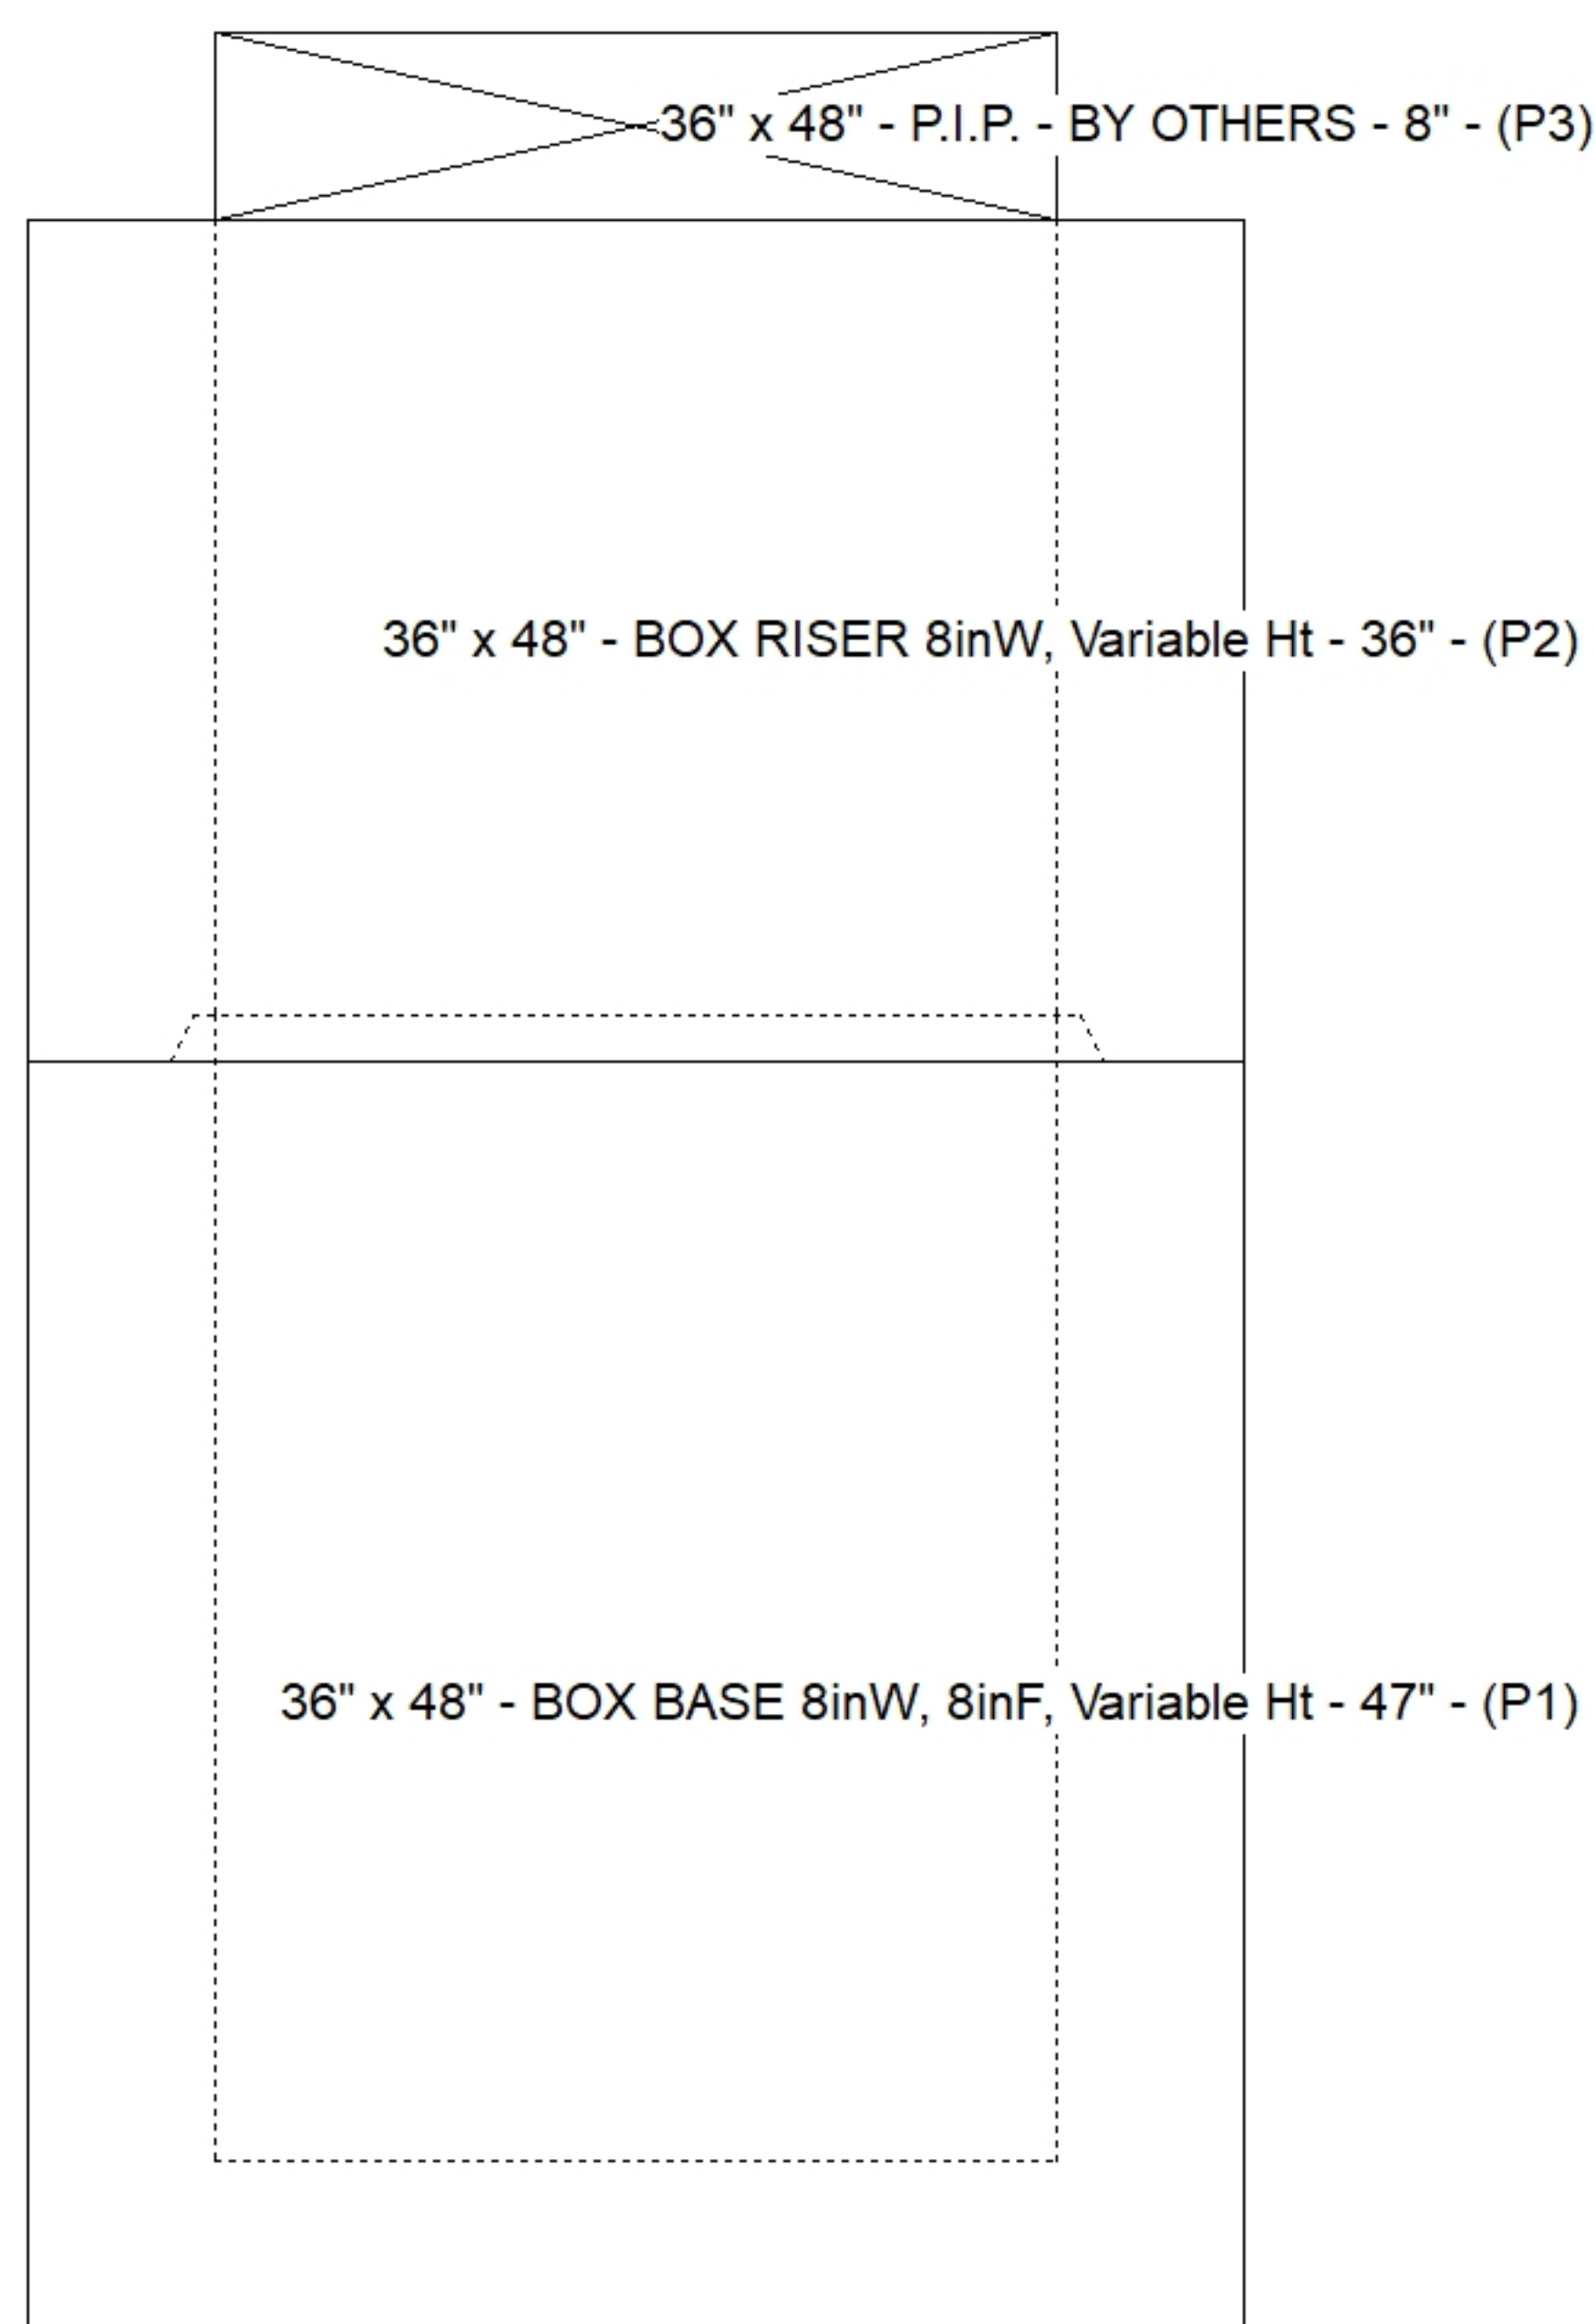

Submittal Drawing
8/3/2026 2:43:21 PM

SUBMITTAL
APPROVED BY:
