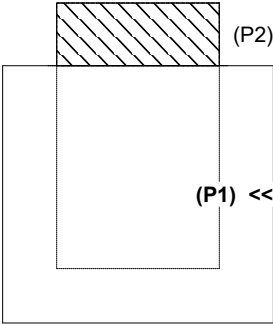


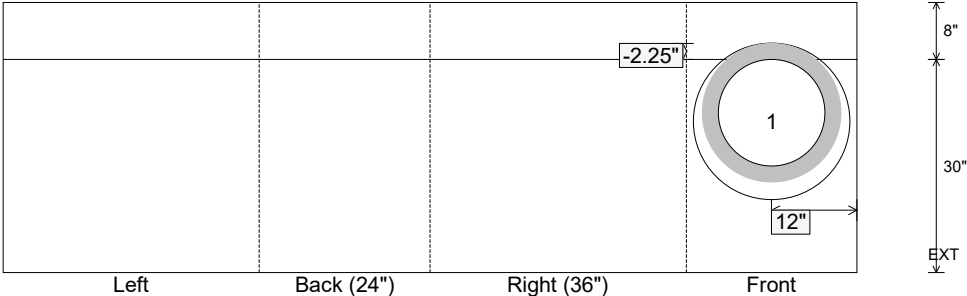


Job Name: 26-2056 - John Stigall Change Order #2 Job Location: Danville, KY Contractor: Todd Johnson Contracting, Inc.					Plant: 100 6/16/2026 7:38:33 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: CI J-1 CID											
P1		BX2436-08BA30		BOX BASE 8inW, 8inF F/n							
P2) 24" x 36" - CASTING HEIGHT - 9.25" P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 30" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22"					0 lb 4202 lb 0 lb 0 lb ----- Structure Total: 4202 lb		<u>Structure Notes:</u> 1. PER LEFUCG CBI TYPE D / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (grade 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 963.8'		Rim to Invert: 3.42'		Slack: 1.79"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	960.38'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P1)											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 30" Height (Ext): 38"		Weight (Net): 4202 lb Volume (Net): 1.07cu.yd		
