

**Contractor: Todd Johnson Contracting, Inc.**

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 3.42'

Floor Height: 8"


Slack: 1.79"

REINFORCING PER ASTM A615 (grade 60).  
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 9.25"  
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"  
1) 24" x 36" - Conseal CS-102 1.00"  
1) Hole - 22

0 lb  
4202 lb  
0 lb  
0 lb

Structure Total: 4202 lb

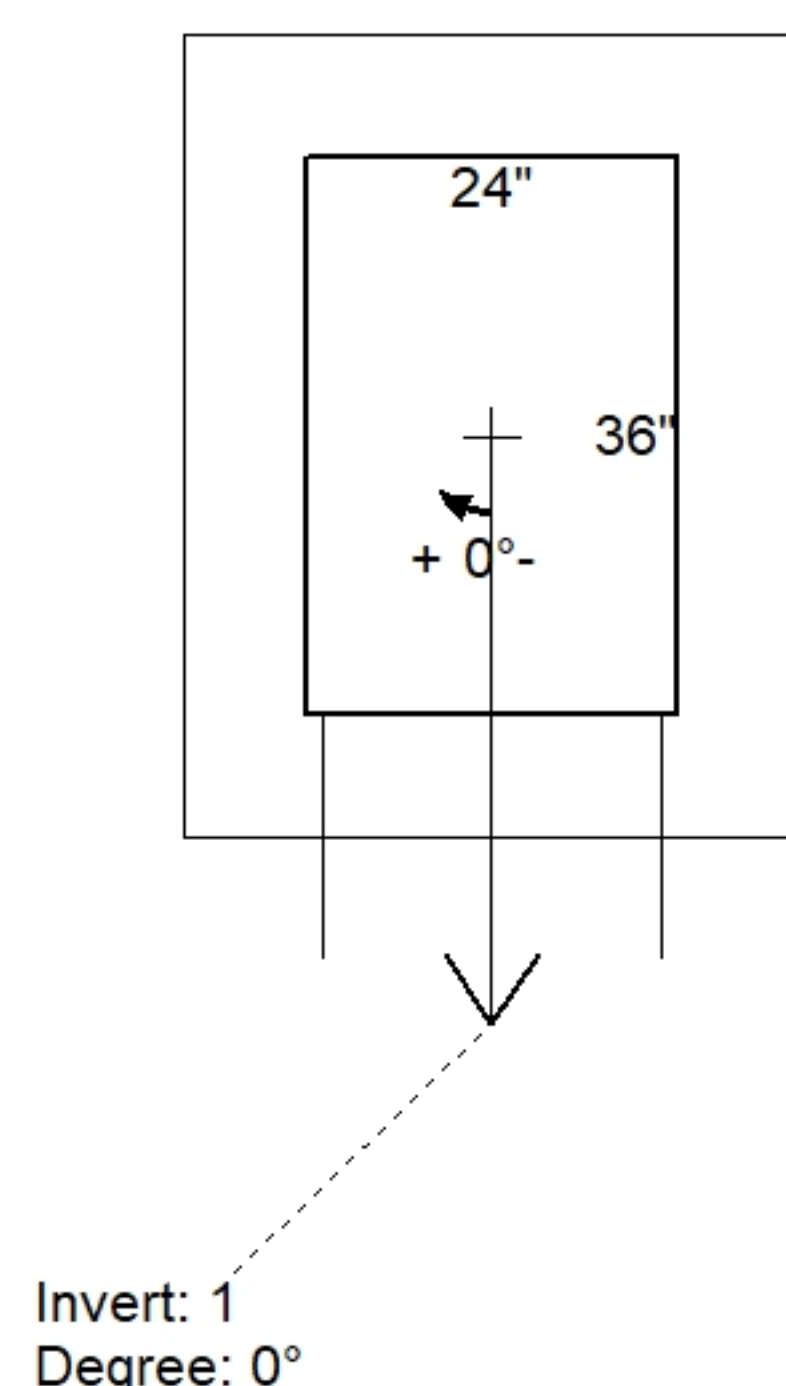


| Position | Elev    | Angle | Pipe           | Pipe OD | Hole | Connector | Up (↓) | Ref |
|----------|---------|-------|----------------|---------|------|-----------|--------|-----|
| Rim      | 963.8'  |       |                |         |      |           |        |     |
| Reducer  |         |       |                |         |      |           |        |     |
| Invert 1 | 960.38' | 0°    | 15" RCP B WALL | 19.5"   | 22"  | Hole 22   | -2.25" | P1  |
| Invert 2 |         |       |                |         |      |           |        |     |
| Invert 3 |         |       |                |         |      |           |        |     |
| Invert 4 |         |       |                |         |      |           |        |     |
| Invert 5 |         |       |                |         |      |           |        |     |
| Invert 6 |         |       |                |         |      |           |        |     |
| Invert 7 |         |       |                |         |      |           |        |     |
| Invert 8 |         |       |                |         |      |           |        |     |

24" x 36" - CASTING HEIGHT - 9.25" - (P2)

24" x 36" - BOX BASE 8inW, 8inF - 30" - (P1)

### Default - Interior Dimensions

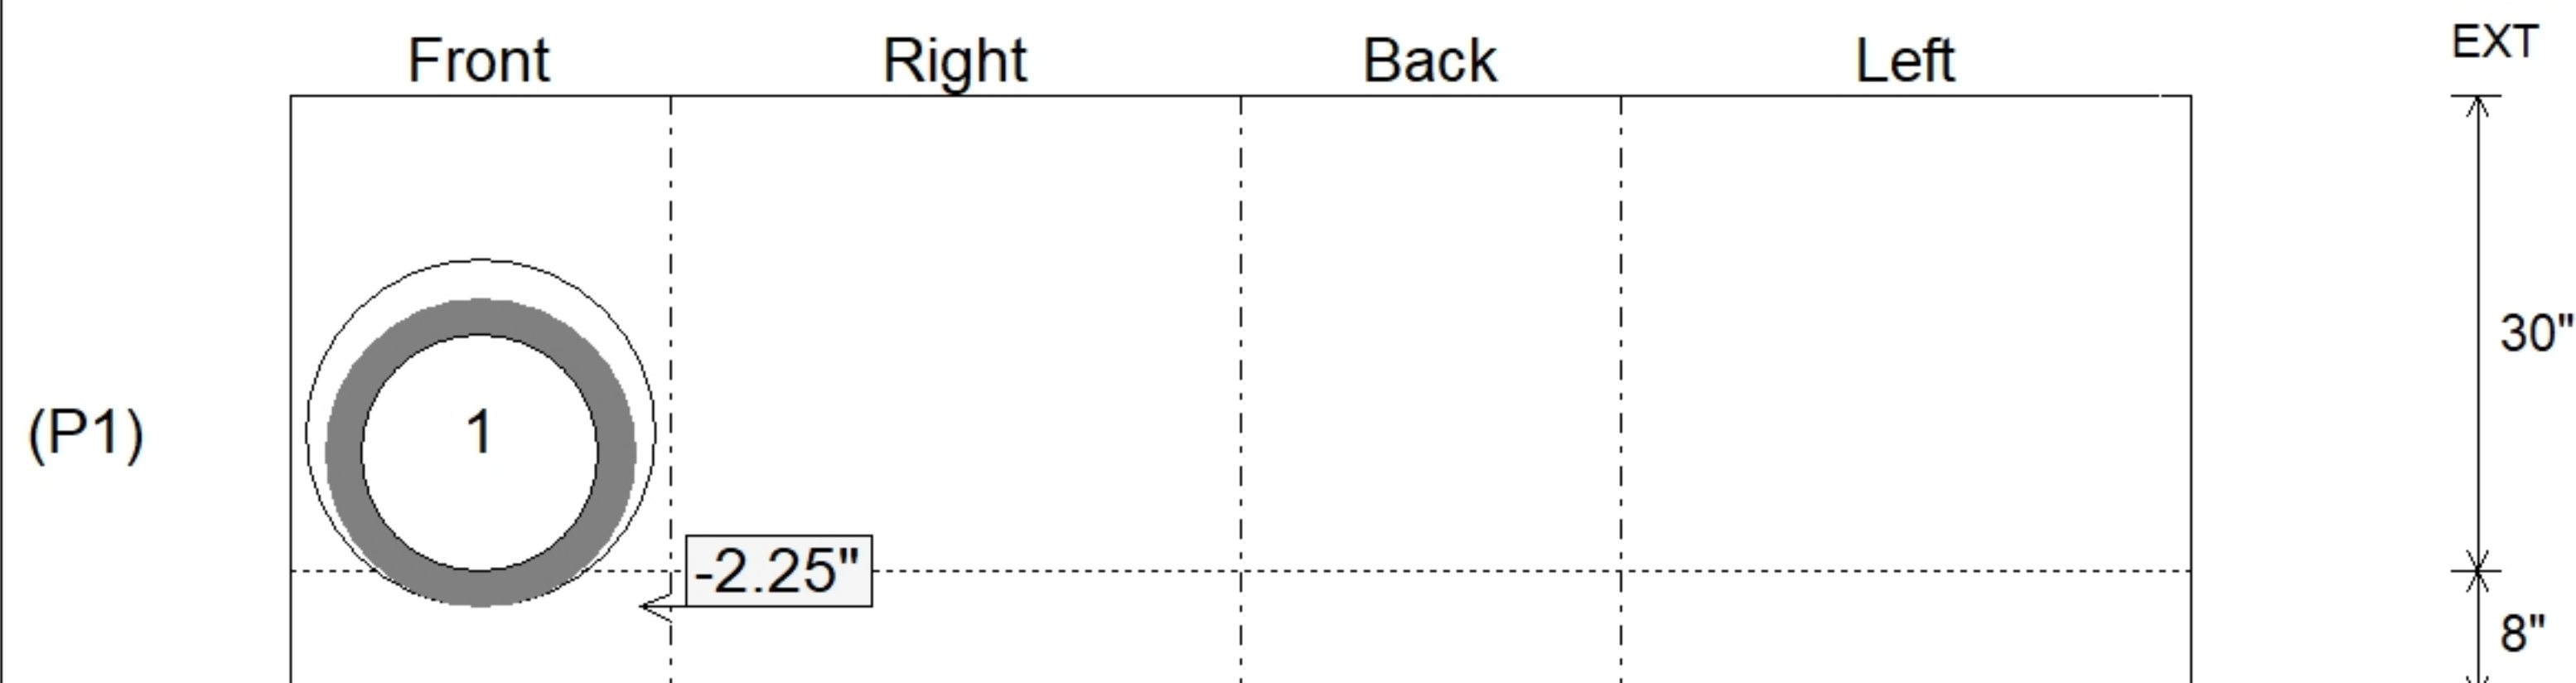

Submittal Drawing  
6/17/2026 8:34:42 AM

SUBMITTAL  
APPROVED BY:
