

Contractor: Shouse Excavating

TECH: S. Felleter

Plant: Beaver Dam



Size: 48"

Rim to Invert: 2.14'

Floor Height: 6"


Slack: 0.68"

STRUCTURE SUMMARY:

P3) 24" - CASTING HEIGHT - 4"
P2) 48" - MH FLAT TOP SPEC. HT. (6") w/24" ECC Hole F/F - 6"
P1) 48" - MH BASE Custom Ht F/n - 17"



- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) CASTING - HOE MC-285 F/C Sanitary
- 1) 48" - Conseal CS-102 1.00" (Double)
- 2) PSX - 12-08 NYLO
- 1) MH Step ML-10-TDS-NCR - 10"

Structure Total: 5264 lb

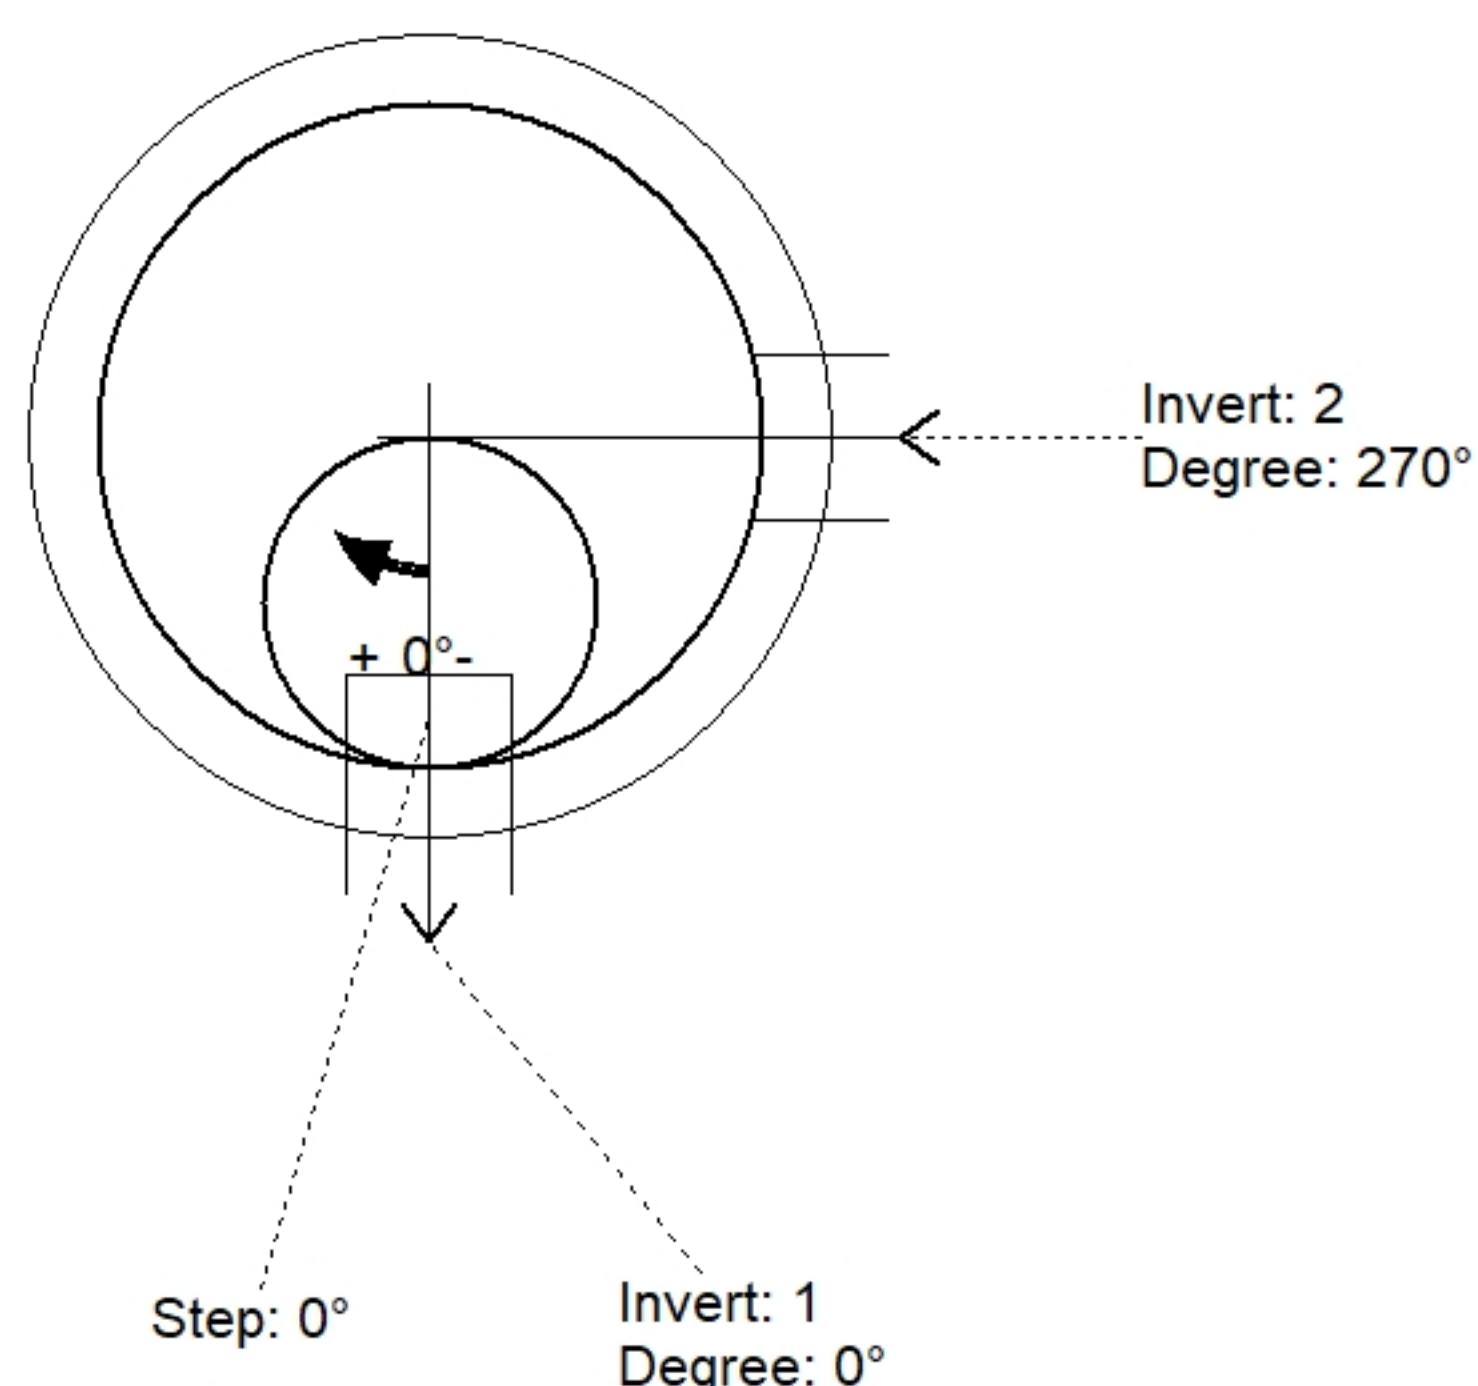

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌋)	Ref
Rim	805.15'							
Reducer								
Invert 1	803.01'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	803.11'	270°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

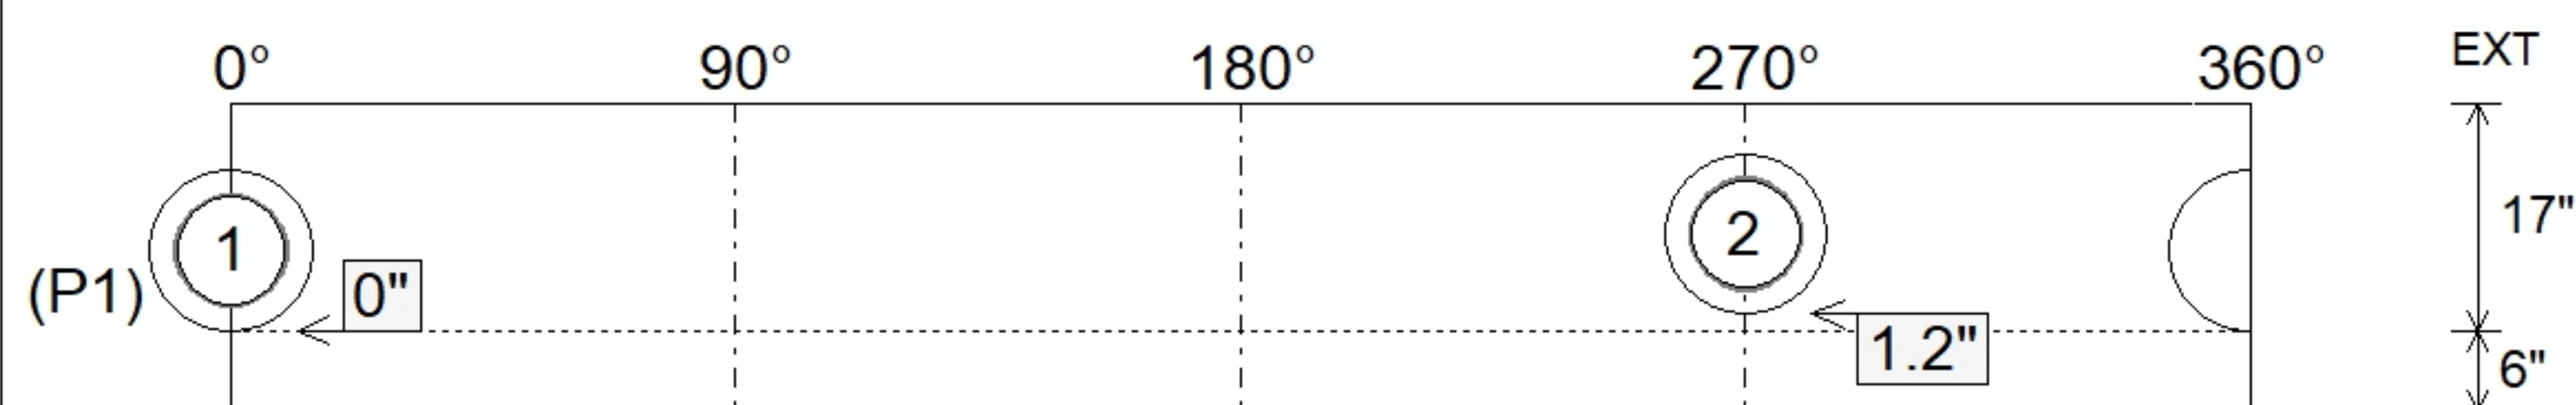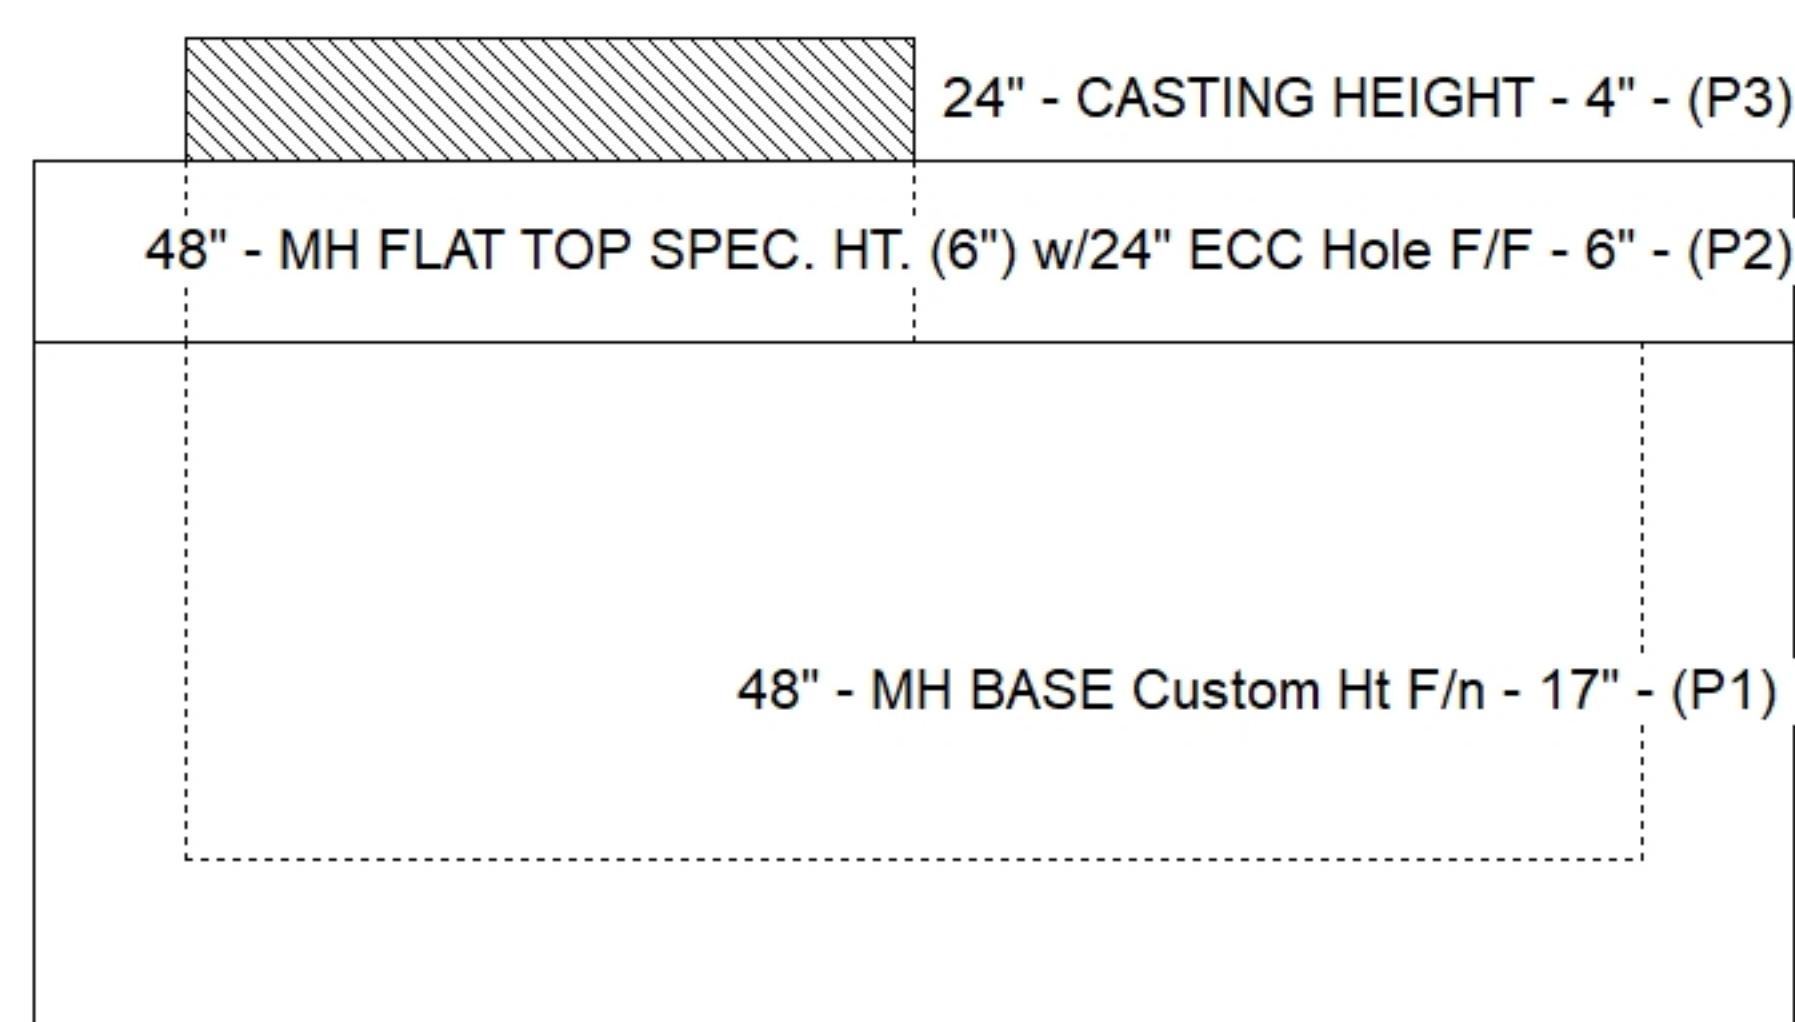

Submittal Drawing
5/15/2026 11:32:30 AM

SUBMITTAL
APPROVED BY:
