





Job Name: 26-2078 Lincoln & Coleman Street Sewer Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: Beaver Dam 5/14/2026 1:16:01 PM		Tech: S. Felletter PC: C. Goff				
Structure ID: A3 SS-MH											
P1 MH048BA24		MH BASE T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 1561 lb 2959 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 8 lb 0 lb ----- Structure Total: 6428 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 813' Rim to Invert: 3.67' Slack: 0.04" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	809.33'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											










INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2959 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--

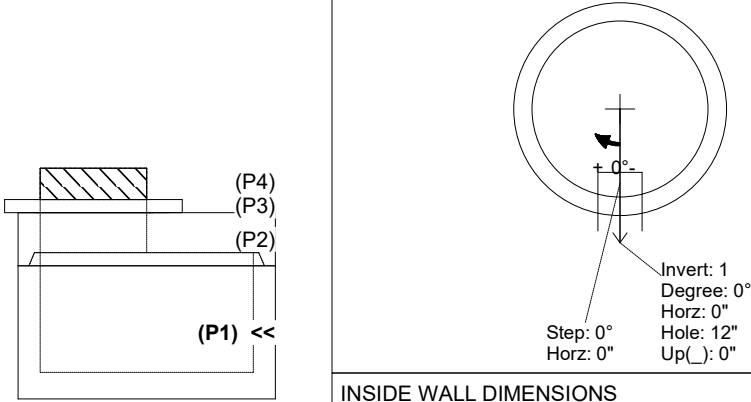Job Name: 26-2078 Lincoln & Coleman Street Sewer Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: Beaver Dam 5/14/2026 1:16:01 PM		Tech: S. Felletter PC: C. Goff						
Structure ID: A3 SS-MH													
P1 MH048BA24		MH BASE T/n											
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 1561 lb 2959 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 8 lb 0 lb ----- Structure Total: 6428 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C "SANITARY"). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					Invert channel drawing Full height invert	
Rim: 813' Rim to Invert: 3.67' Slack: 0.04" Sump: 2" Step Position: 0°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	809.33'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"			
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 24" Height (Ext): 30"		Weight (Net): 2959 lb Volume (Net): 0.76cu.yd				
