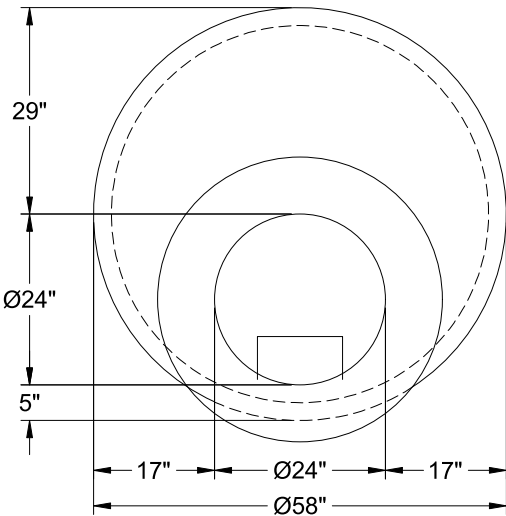



Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC		Plant: 100 6/22/2026 6:26:03 PM	Tech: Jared - A PC: E. Bradley	
Structure ID: A2 SS-MH P3 MH048CN24		ECC CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 31" 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) A-Lok - 0285 7) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 2515 lb 3401 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 0 lb 3 lb 0 lb ----- 9180 lb Structure Total:	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
 48" - ECC CONE w/ 24" HOLE F/G - 24" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
